

# STATE OF CONNECTICUT CONNECTICUT SITING COUNCIL

Ten Franklin Square, New Britain, CT 06051 Phone: (860) 827-2935 Fax: (860) 827-2950 E-Mail: siting.council@ct.gov Web Site: portal.ct.gov/csc

#### VIA ELECTRONIC MAIL

July 1, 2024

Lee D. Hoffman, Esq. Pullman & Comley, LLC 90 State House Square Hartford, CT 06103-3702 lhoffman@pullcom.com

RE: **PETITION NO. 1562** – 524 NLR LLC Declaratory Ruling, pursuant to Connecticut General Statutes §4-176 and §16-50k, for the construction, maintenance and operation of a 3.99-megawatt AC solar photovoltaic electric generating facility located at 524 New London Road, Colchester, Connecticut, and associated electrical interconnection. **Compliance with Modified Condition No. 3, and Reporting Requirements.** 

#### Dear Attorney Hoffman:

The Connecticut Siting Council (Council) is in receipt of your correspondence dated June 27, 2024 regarding compliance with Condition No. 3 of the Declaratory Ruling issued by the Council on June 9, 2023 for the above-referenced facility that was modified by the Council on April 19, 2024 (Modified Condition No. 3). The correspondence includes a copy of the final structural design for the tracking system stamped by a Professional Engineer duly licensed in the State of Connecticut in accordance with Modified Condition No. 3.

The June 27, 2024 correspondence also includes a request for project changes as follows:

- a. Relocate the interconnection line 210 feet to the south of its approved location and utilize seven new utility poles instead of four to facilitate the interconnection, per the design requirements of both Eversource Energy and the Connecticut Department of Transportation;
- b. Remove 2,000 linear feet of approved perimeter gravel access driveways along the southern and western site boundaries:
- c. Add 220 linear feet of gravel driveway in the northwest corner of the site to provide a turnaround location for large emergency vehicles;
- d. Relocate and redesign the concrete pads on the north side of the site by installing two 18'x20' and one 10'x16' pads instead of the approved 45'x10' and 35'x10' pads. The new pads will be installed in a more interior location along the northern site access drive;
- e. Install conduit in ground-mounted cable trays to avoid subsurface trenching;
- f. Relocate the perimeter fence to within 3 feet of the limit of disturbance demarcation line;
- g. Expand the solar array within the existing lease area by approximately 13,300 square feet; and
- h. Install 695-Watt modules instead of 665-Watt modules and decrease the number of modules from 7,655 modules to 7,618 modules. The AC output of the facility would not change.

Pursuant to Condition No. 1 of the Council's June 9, 2023 Declaratory Ruling and Regulations of Connecticut State Agencies §16-50j-62(b)(3), the requested project changes are hereby approved with the following condition:

1) Submit specification sheets for the new 695-Watt modules and corresponding Toxicity Characteristic Leaching Procedure test results that indicate the 695-Watt modules would not be characterized as hazardous waste at the time of disposal, under current testing criteria.

This approval applies only to the project changes described in the June 27, 2024 correspondence. The Council also acknowledges the receipt of the first quarter construction progress report.

Please be advised that deviations from the standards established by the Council in the Declaratory Ruling are enforceable under the provisions of Connecticut General Statutes §16-50u.

Thank you for your attention and cooperation.

Sincerely,

Melanie A. Bachman Executive Director

Meline Beal

c: The Honorable Bernie Dennler, First Selectperson, Town of Colchester (<u>bdennler@colchesterct.gov</u>)
The Honorable Ed Chmielewski, First Selectperson, Town of Salem (<u>selectman@salemct.gov</u>)
Service List, dated March 7, 2024



Lee D. Hoffman

90 State House Square Hartford, CT 06103-3702 p 860 424 4315 f 860 424 4370 lhoffman@pullcom.com www.pullcom.com

June 27, 2024

#### VIA ELECTRONIC MAIL AND U.S. MAIL

Melanie Bachman Executive Director/Staff Attorney Connecticut Siting Council 10 Franklin Square New Britain, CT 06051

Re: PETITION NO. 1562 - 524 NLR LLC petition for a declaratory ruling, pursuant to Connecticut General Statutes §4-176 and §16-50k, for the proposed construction, maintenance and operation of a 3.99-megawatt AC solar photovoltaic electric generating facility located at 524 New London Road, Colchester, Connecticut, and associated electrical interconnection.

Dear Ms. Bachman:

I am writing on behalf of my client, 524 NLR LLC ("Petitioner"), in connection with the above referenced Docket. Item No. 3 of the Council's June 9, 2023 Decision requires the Petitioner to submit final structural designs for the tracking system stamped by a Professional Engineer who is duly licensed in the State of Connecticut prior to the commencement of construction. The Petitioner has completed those designs, and an original and fifteen (15) copies of those designs are enclosed with this letter. The Petitioner thanks the Council for allowing the Petitioner to complete limited, phased work on the project prior to submitting these designs to the Council.

The Petitioner is now ready to begin placing racking in the ground and continuing with construction. However, before it does so, the Petitioner would like to call the Council's attention to several changes that have been made to the plan set that was previously approved by the Council. Item No. 1 of the Council's June 9, 2023 Decision delegates all changes in the project design to staff. Because there are several changes, I am providing the Council with a description of the changes for ease of review.

The largest change is in the placement of interconnection poles. Given the location near New London Road, the Petitioner consulted with both The Connecticut Light & Power Company, d/b/a Eversource Energy ("Eversource") and the Connecticut Department of Transportation ("DOT") regarding the placement of the poles. Eversource informed the Petitioner that it would require that the interconnection poles to be moved 210 ft to the south along New London Rd in order to comply with Eversource's latest pole placement design guidelines. This resulted in a total of seven poles for the interconnection, which is three more poles than were originally approved by the Council. Eversource is requiring the three additional poles to meet Eversource's bracing requirements. Although the number of poles as increased as a result of this Eversource-required design change, there is a significant benefit to the change. As a result of moving the interconnecting poles to this location, the poles have been moved 210feet further away from the residence to the north of the site.

pullcom.com Bridgeport Hartford Springfield Stamford Waterbury Westport White Plains



#### Page 2

Given the proximity to New London Road, DOT needed to approve the locations of the poles as well. The pole location plan was reviewed extensively by both Eversource and CT DOT, including consideration of several alternatives. Both Eversource and DOT agreed that the proposal being submitted to the Council today is the preferred approach, and DOT issued a site plan approval for the location of the poles pursuant to the enclosed plan set.

In addition to working on interconnection issues, the Petitioner has removed a significant amount of driveway from the project. This changes to the driveway areas are broken out as follows:

- All major electrical equipment has now been located along the norther portion of the site. As such, 36,000 sq ft (2,000 linear feet) of driveway was removed from the project, along the southern and western boundaries, as a perimeter access path is no longer needed in these locations. This has allowed the Petitioner to install approximately 6% more panels within the same project boundaries, making for a more efficient project.
- 2,500 sq ft (140 linear feet) of additional driveway was added along the northeast corner of the project in order to provide the property owner access to their existing building, without having to enter the fenced in area for the solar array. The existing building is not part of the leased area for the facility, and having the property owner enter into the fenced area of the project presented safety concerns which have now been alleviated.
- 4,000 sq ft (220 linear feet) of additional driveway was added in the northwest corner of the project in order to provide a location for large emergency vehicles such as fire trucks to turn around. The path to this turnaround provides access to all of the major electrical equipment at the project.

The plans also call for the relocation of the concrete pads on the site, however, the total concrete pad area for the project remains the same (800 sq ft). The new design now calls for three equipment pads instead of the original two pads. The pad locations are still along the north edge of the project. The bollards around the poles have been removed as the turn-offs are no longer facing the equipment pads, and so bollards are no longer needed to protect from vehicles. This will result in a safer and simpler design.

There is now an aboveground cable tray system, which reduces the amount of trenching planned for the project. The cable tray will run along the north of the project, in the same location that the underground system was originally planned. The distances are also the same. The reduced trenching will minimize subterranean risk at the project and reduce the amount of ground disturbance.

The fence line has been moved two feet closer to the project's LOD (which has not changed), to provide for wider turn radius and wider access roads if needed. There is still three of space between the fence and the LOD, so there will be no issue installing the fence. Along the south, this proposed change opens up space for a slightly larger array footprint, which allows the project to generate more power without increasing the project boundaries. The project's boundaries will remain unchanged.

The array footprint has been expanded to be about ten feet closer to the basins, while not affecting the location or size of any of the basins. This also slightly increased the array footprint, which allows the project to generate more power, without increasing the project boundaries, which remain the same.

# PULLMAN & COMLEY

#### Page 3

The total module count is now 7,618 modules. The size of the modules is the same, but the power rating increased from 665W-DC to 695 W-DC. While this is fewer modules than shown in the original plan (which showed 7,655 modules), the total DC size is slightly higher by 0.2MW-DC since the new modules are more powerful. The project's MW-AC system size is the same. This allows the project to be more efficient and to generate more power, without changing the AC system size.

On sheet EC-1, under Phase 2, note 12, the words "inverters and switchgear" have been added to "Install electrical conduit and equipment pads." so that it now reads "Install electrical conduit, equipment pads, inverters, and switchgear while stabilization occurs in the array footprint." This more clearly defines the work that will take place installing the electrical system along the northern access path, while the array footprint is being stabilized by grass growth. Similarly, the array footprint has been updated in the drawings to match the final footprint location. The new footprint is similar to the original footprint. The decorative sheep statue has been relocated above new entrance gate along the east side of project.

The Petitioner believes that all of these design changes will make the project a more efficient one, while further minimizing any impacts to the surrounding area. As such, the Petitioner would ask that the Council staff approve these changes as expeditiously as possible. Should you have any questions concerning this submittal, please contact me at your convenience. I certify that copies of this submittal have been made to all parties on the Petition's Service List as of this date.


Sincerely,

Lee D. Hoffman

Lee D. Hoffun

cc: Service List, Docket 1562

**Enclosures** 

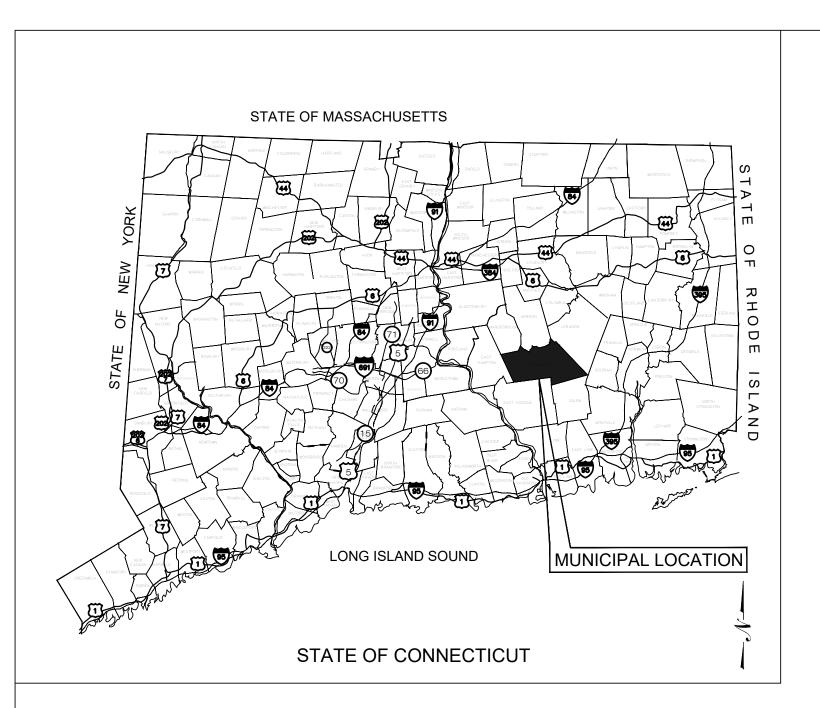

# **524 NLR LLC**

# "SCRAPYARD SOLAR"

# **524 NEW LONDON ROAD** COLCHESTER, CT

# LIST OF DRAWINGS

T-1 TITLE SHEET & INDEX

1 & 2 OF 2 PROPERTY & TOPOGRAPHIC SURVEY PROVIDED BY MARTIN **SURVEYING ASSOCIATES, LLC** 

**GN-1 GENERAL NOTES** 

**GN-2 ENVIRONMENTAL NOTES** 

**OP-1 OVERALL LOCUS MAP** 

EC-1 SEDIMENTATION & EROSION CONTROL NOTES

EC-2 SEDIMENTATION & EROSION CONTROL DETAILS

EC-3 PHASE 1 SEDIMENTATION & EROSION CONTROL PLAN

EC-4 PHASE 2 SEDIMENTATION & EROSION CONTROL PLAN

**GD-1 FINAL GRADING & DRAINAGE PLAN** 

SP-1 SITE & UTILITY PLAN

LP-1 LANDSCAPE SEEDING PLAN

**DN-1 SITE DETAILS** 

DN-2 SITE DETAILS

# SITE INFORMATION

SITE NAME: COLCHESTER SOLAR

LOCATION: 524 NEW LONDON ROAD COLCHESTER, CT

SITE TYPE/DESCRIPTION: ADD (1) GROUND MOUNTED SOLAR PANEL ARRAY W/ ASSOCIATED EQUIPMENT AND

PROPERTY OWNER: FIVE J, LLC 524 NEW LONDON ROAD

COLCHESTER, CT

APPLICANT: 524 NLR LLC

9 NOVELTY LANE - UNIT 9B ESSEX, CT 06426

ENGINEER CONTACT: ROBERT C. BURNS, P.E. (860) 581-4477

LATITUDE: 41.527693° LONGITUDE: -72.299056°


> MBLU: 01-10/03B-000 ZONE: RU - RURAL

TOTAL SITE ACREAGE: 35.56± AC. TOTAL DISTURBED AREA: 16.49± AC.

APPROX. VOLUME OF CUT: 5,192± CY (TEMPORARY)

APPROX. VOLUME OF FILL: 630± CY (TEMPORARY) APPROX. NET VOLUME: 4,562± CY OF CUT (TEMPORARY)

# USGS TOPOGRAPHIC MAP

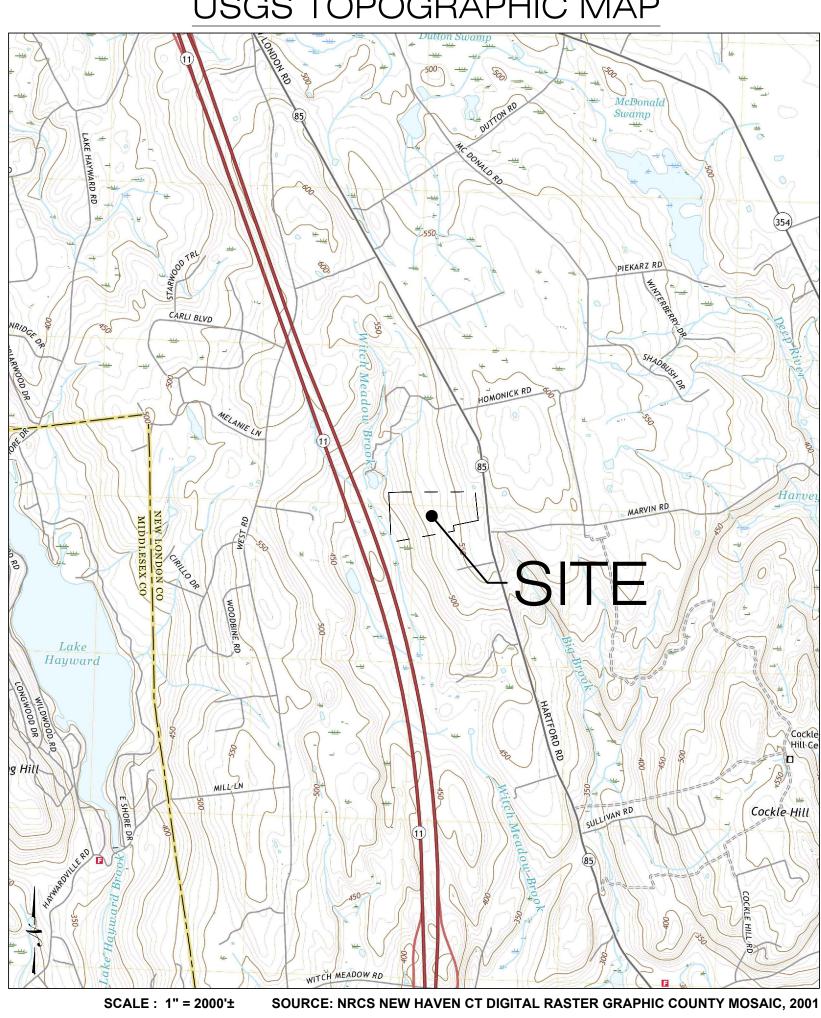

## 524 NLR LLC

9 NOVELTY LANE, UNIT 9B **ESSEX, CT 06426** 



567 VAUXHALL STREET EXTENSION - SUITE 311 WATERFORD, CT 06385 PHONE: (860)-663-1697 WWW.ALLPOINTSTECH.COM FAX: (860)-663-093

**CSC PERMIT SET** 

NO DATE REVISION 03/07/23 FOR FILING: KAM 06/15/23 FOR FILING: RCB

09/01/23 FENCE REVISIONS: RCB 09/08/23 FENCE REVISIONS: RCB 09/28/23 ADD EX. POLE CALOUTS: RCE

04/15/24 REVISED SEED MIX: RCB

05/03/24 REVISED SITE LAYOUT: UKA 05/16/24 REVISED PER CLIENT :TEL 06/11/24 REVISED PER CLIENT :TEL

10 06/21/24 REVISED PER CLIENT :TEL

### DESIGN PROFESSIONAL OF RECORD

**COMP: ALL-POINTS TECHNOLOGY** CORPORATION, P.C. ADD: 567 VAUXHALL STREET **EXTENSION - SUITE 311** WATERFORD, CT 06385

OWNER: FIVE J, LLC

ADDRESS: 524 NEW LONDON ROAD COLCHESTER, CT

SCRAPYARD SOLAR

SITE 524 NEW LONDON ROAD ADDRESS: COLCHESTER, CT


APT FILING NUMBER: CT580160

DATE: 03/07/23 | CHECKED BY: RCB

TITLE SHEET & INDEX

SHEET NUMBER:



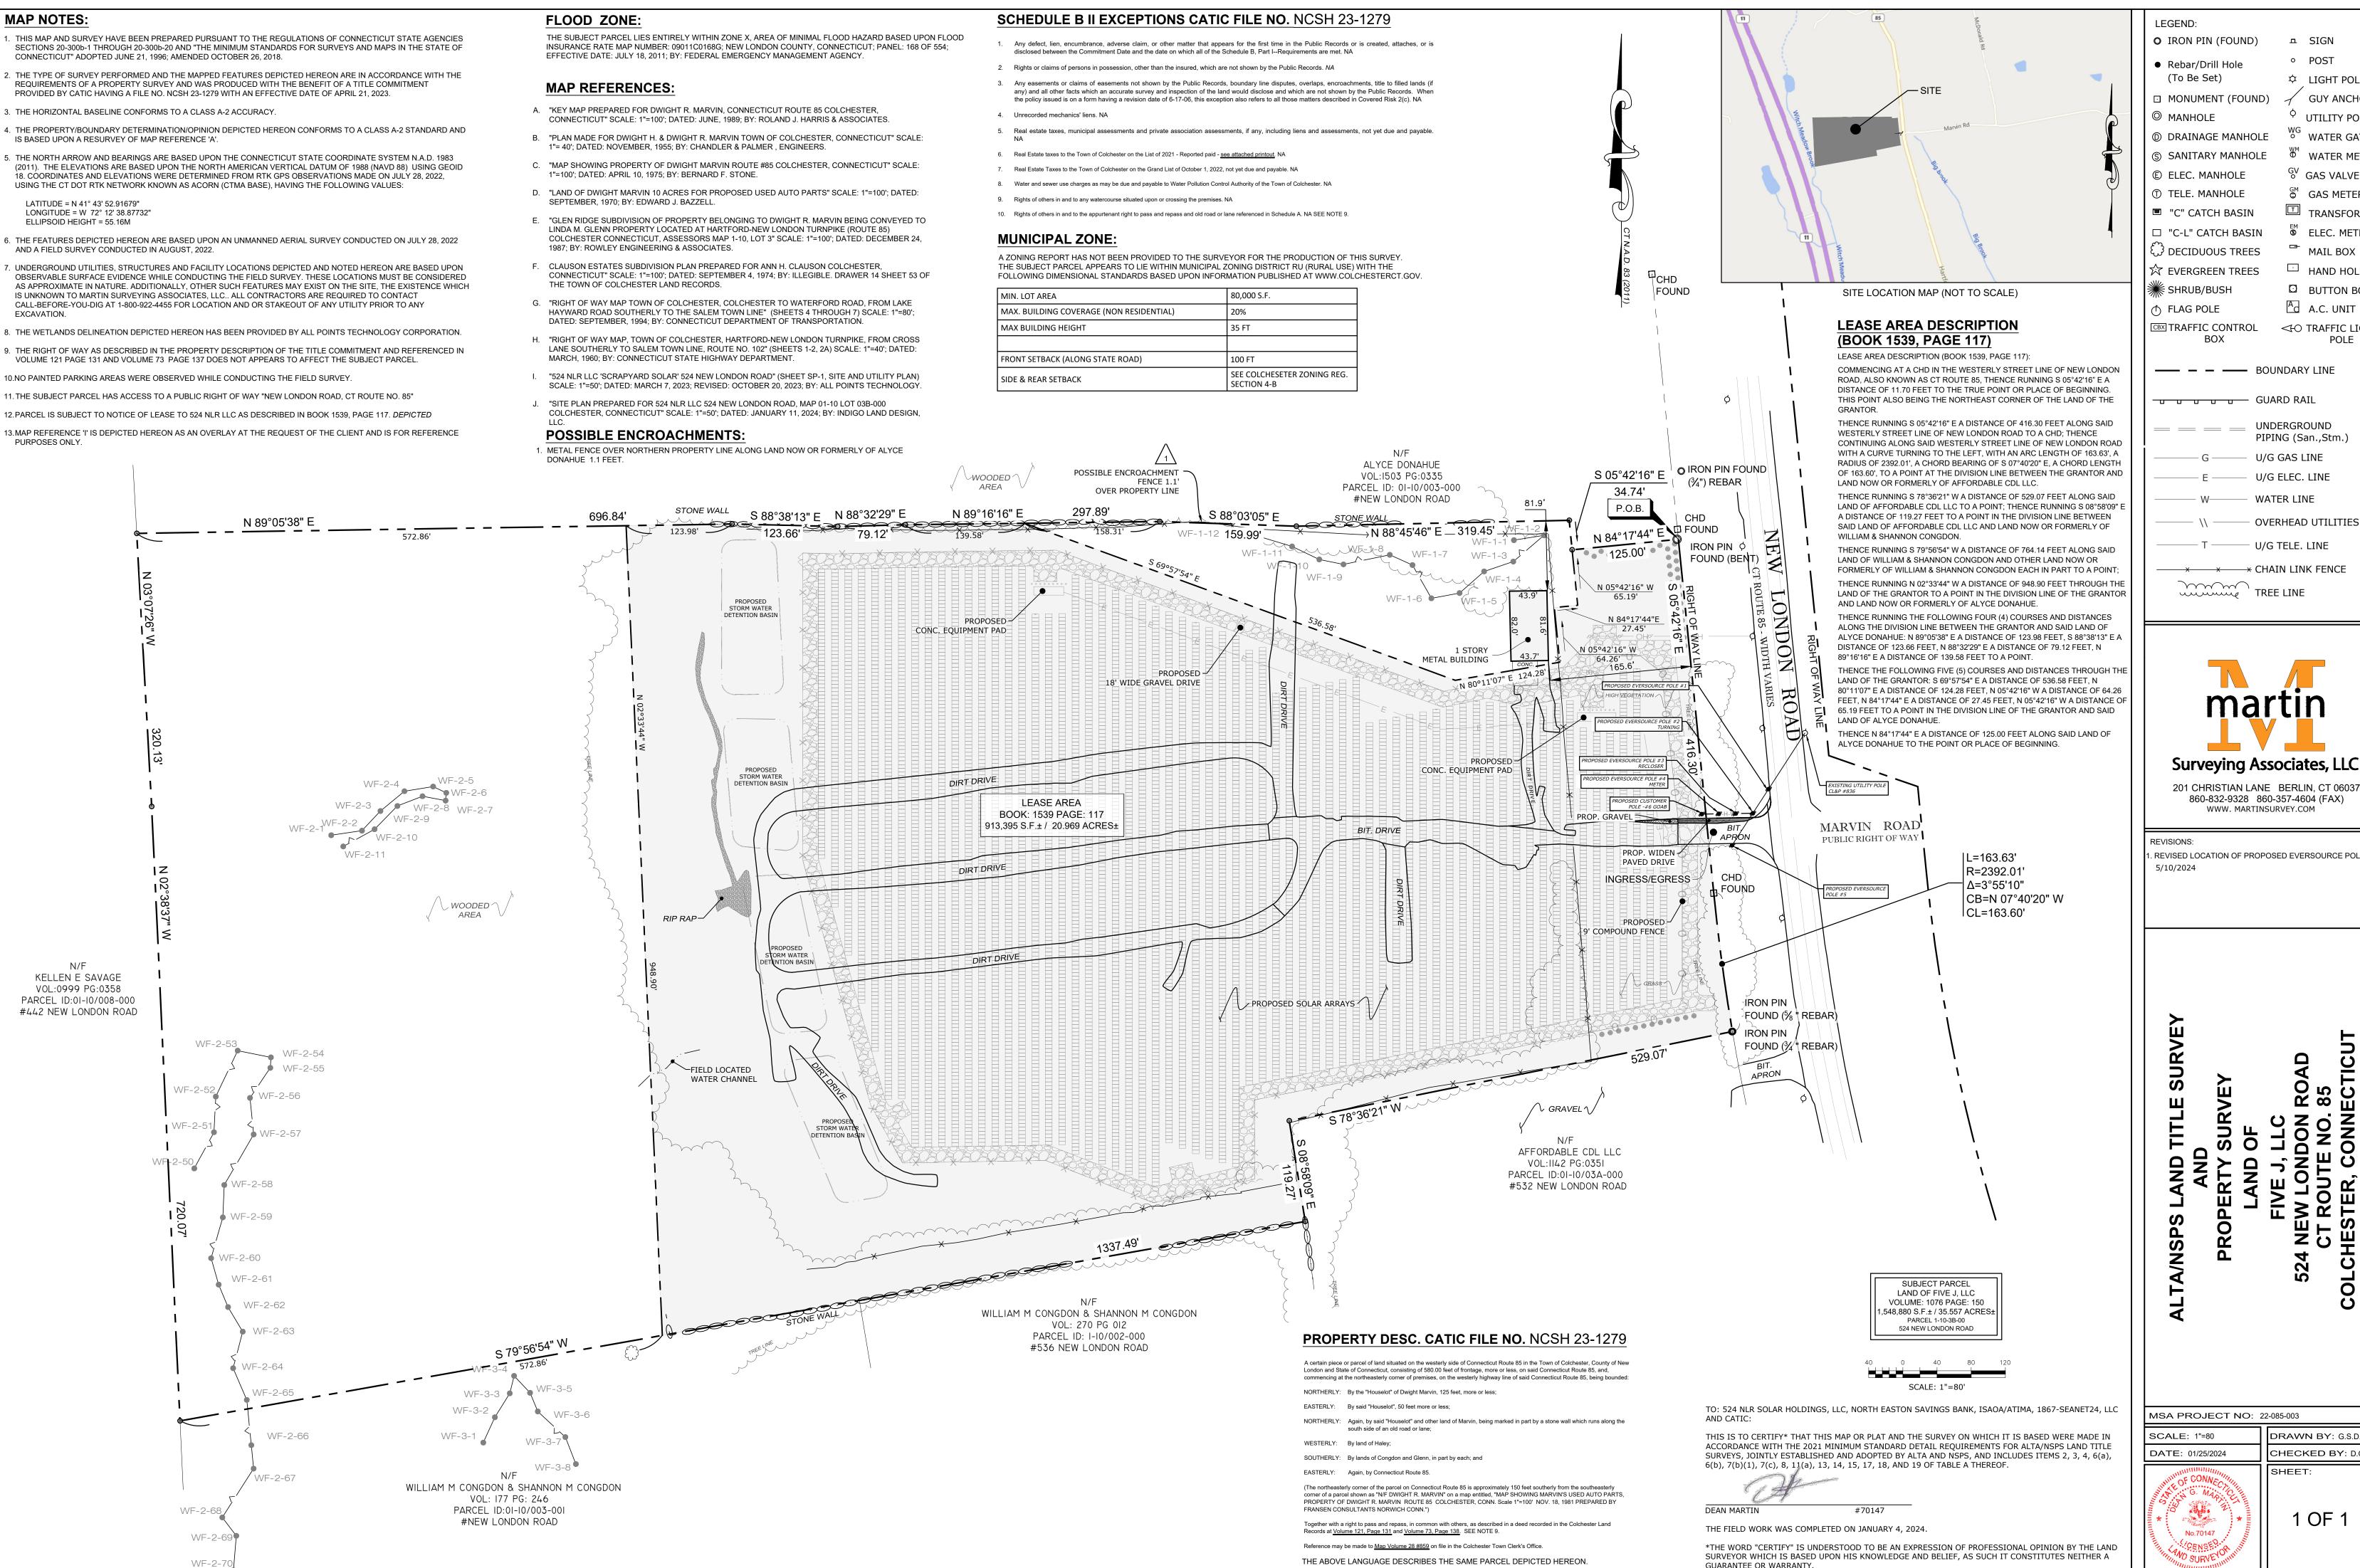

O IRON PIN (FOUND) ⊐ SIGN POST Rebar/Drill Hole (To Be Set) **GUY ANCHOR** UTILITY POLE <sup>₩G</sup> WATER GATE DRAINAGE MANHOLE WATER METER (S) SANITARY MANHOLE © ELEC. MANHOLE GAS VALVE TELE. MANHOLE © GAS METER TRANSFORMER "C" CATCH BASIN ☐ "C-L" CATCH BASIN S ELEC. METER MAIL BOX DECIDUOUS TREES ☐ HAND HOLE ☆ EVERGREEN TREES **₩** SHRUB/BUSH BUTTON BOX A.C. UNIT CBX TRAFFIC CONTROL <∪ TRAFFIC LIGHT POLE — — — BOUNDARY LINE GUARD RAIL UNDERGROUND PIPING (San.,Stm.) U/G GAS LINE U/G ELEC. LINE

WATER LINE

OVERHEAD UTILITIES

**Surveying Associates, LLC** 

860-832-9328 860-357-4604 (FAX) WWW. MARTINSURVEY.COM

1. REVISED LOCATION OF PROPOSED EVERSOURCE POLES

MSA PROJECT NO: 22-085-003

CHECKED BY: D.G.M.

DRAWN BY: G.S.D.

## **GENERAL NOTES**

- ALL CONSTRUCTION SHALL COMPLY WITH PROJECT DEVELOPER STANDARDS, TOWN OF COLCHESTER STANDARDS, CONNECTICUT DEPARTMENT OF TRANSPORTATION STANDARDS AND SPECIFICATIONS IN THE ABOVE REFERENCED INCREASING HIERARCHY. IF SPECIFICATIONS ARE IN CONFLICT. THE MORE STRINGENT SPECIFICATION SHALL APPLY.
- 2. IF NO PROJECT CONSTRUCTION SPECIFICATION PACKAGE IS PROVIDED BY THE PROJECT DEVELOPER OR THEIR REPRESENTATIVE, THE CONTRACTOR SHALL COMPLY WITH THE MANUFACTURER, TOWN OF COLCHESTER, OR CONNECTICUT DEPARTMENT OF TRANSPORTATION STANDARD SPECIFICATIONS, AND BE IN ACCORDANCE WITH ALL APPLICABLE OSHA, FEDERAL, STATE AND LOCAL REGULATIONS.
- 3. THE PROJECT DEVELOPER IS RESPONSIBLE FOR OBTAINING ALL NECESSARY ZONING AND STORMWATER PERMITS REQUIRED BY GOVERNMENT AGENCIES PRIOR TO CONSTRUCTION. THE CONTRACTOR SHALL OBTAIN ALL TOWN OF COLCHESTER CONSTRUCTION PERMITS. THE CONTRACTOR SHALL POST ALL BONDS, PAY ALL FEES, PROVIDE PROOF OF INSURANCE AND PROVIDE TRAFFIC CONTROL NECESSARY FOR THIS WORK.
- 4. REFER TO PLANS, DETAILS AND REPORTS PREPARED BY ALL-POINTS TECHNOLOGY CORPORATION FOR ADDITIONAL INFORMATION. THE CONTRACTOR SHALL VERIFY ALL SITE CONDITIONS IN THE FIELD AND CONTACT THE PROJECT DEVELOPER IF THERE ARE ANY QUESTIONS OR CONFLICTS REGARDING THE CONSTRUCTION DOCUMENTS AND/OR FIELD CONDITIONS SO THAT APPROPRIATE REVISIONS CAN BE MADE PRIOR TO BIDDING/CONSTRUCTION. ANY CONFLICT BETWEEN THE DRAWINGS AND SPECIFICATIONS SHALL BE CONFIRMED WITH THE PROJECT DEVELOPERS CONSTRUCTION MANAGER PRIOR TO
- THE CONTRACTOR SHALL SUBMIT SHOP DRAWINGS OF ALL PRODUCTS, MATERIALS PER PLANS, AND SPECIFICATIONS TO THE PROJECT DEVELOPER FOR REVIEW AND APPROVAL PRIOR TO FABRICATION OR DELIVERY TO THE SITE. ALLOW A MINIMUM OF 14 WORKING DAYS FOR REVIEW
- 6. SHOULD ANY UNKNOWN OR INCORRECTLY LOCATED EXISTING PIPING OR OTHER UTILITY BE UNCOVERED DURING EXCAVATION, CONSULT THE PROJECT DEVELOPER IMMEDIATELY FOR DIRECTIONS BEFORE PROCEEDING FURTHER WITH WORK IN THIS AREA.
- 7. DO NOT INTERRUPT EXISTING UTILITIES SERVICING FACILITIES OCCUPIED AND USED BY THE PROJECT DEVELOPER OR OTHERS DURING OCCUPIED HOURS, EXCEPT WHEN SUCH INTERRUPTIONS HAVE BEEN AUTHORIZED IN WRITING BY THE PROJECT DEVELOPER AND THE LOCAL MUNICIPALITY. INTERRUPTIONS SHALL ONLY OCCUR AFTER ACCEPTABLE TEMPORARY SERVICE HAS BEEN PROVIDED.
- 8. THE CONTRACT LIMIT IS THE PROPERTY LINE UNLESS OTHERWISE SPECIFIED OR SHOWN ON THE CONTRACT DRAWINGS.
- 9. THE CONTRACTOR SHALL ABIDE BY ALL OSHA, FEDERAL, STATE AND LOCAL REGULATIONS WHEN OPERATING CRANES, BOOMS, HOISTS, ETC. IN CLOSE PROXIMITY TO OVERHEAD ELECTRIC LINES. IF CONTRACTOR MUST OPERATE EQUIPMENT CLOSE TO ELECTRIC LINES, CONTACT POWER COMPANY TO MAKE ARRANGEMENTS FOR PROPER SAFEGUARDS. ANY UTILITY COMPANY FEES SHALL BE PAID FOR BY THE CONTRACTOR.
- 10. THE CONTRACTOR SHALL COMPLY WITH OSHA CFR 29 PART 1926 FOR EXCAVATION TRENCHING AND TRENCH PROTECTION REQUIREMENTS.
- 11. THE ENGINEER IS NOT RESPONSIBLE FOR SITE SAFETY MEASURES TO BE EMPLOYED DURING CONSTRUCTION. THE ENGINEER HAS NO CONTRACTUAL DUTY TO CONTROL THE SAFEST METHODS OR MEANS OF THE WORK, JOB SITE RESPONSIBILITIES, SUPERVISION OF PERSONNEL OR TO SUPERVISE SAFETY AND DO NOT VOLUNTARILY ASSUME ANY SUCH DUTY OR RESPONSIBILITY.
- 12. THE CONTRACTOR SHALL RESTORE ANY DRAINAGE STRUCTURE, PIPE, CONDUIT, PAVEMENT, CURBING, SIDEWALKS, LANDSCAPED AREAS OR SIGNAGE DISTURBED DURING CONSTRUCTION TO THEIR ORIGINAL CONDITION OR BETTER, AS APPROVED BY THE PROJECT DEVELOPER OR TOWN OF COLCHESTER.
- 13. THE CONTRACTOR SHALL PROVIDE AS-BUILT RECORDS OF ALL CONSTRUCTION (INCLUDING UNDERGROUND UTILITIES) TO THE PROJECT DEVELOPER AT THE END OF CONSTRUCTION.
- 14. ALTERNATIVE METHODS AND PRODUCTS, OTHER THAN THOSE SPECIFIED, MAY BE USED IF REVIEWED AND APPROVED BY THE PROJECT DEVELOPER, ENGINEER, AND APPROPRIATE REGULATORY AGENCY PRIOR TO INSTALLATION DURING THE BIDDING/CONSTRUCTION PROCESS
- 15. INFORMATION ON EXISTING UTILITIES AND STORM DRAINAGE SYSTEMS HAS BEEN COMPILED FROM AVAILABLE INFORMATION INCLUDING UTILITY PROVIDER AND MUNICIPAL RECORD MAPS AND/OR FIELD SURVEY AND IS NOT GUARANTEED CORRECT OR COMPLETE. UTILITIES AND STORM DRAINAGE SYSTEMS ARE SHOWN TO ALERT THE CONTRACTOR TO THEIR PRESENCE AND THE CONTRACTOR IS SOLELY RESPONSIBLE FOR DETERMINING ACTUAL LOCATIONS AND ELEVATIONS OF ALL UTILITIES AND STORM DRAINAGE SYSTEMS INCLUDING SERVICES. PRIOR TO DEMOLITION OR CONSTRUCTION, THE CONTRACTOR SHALL CONTACT "CALL BEFORE YOU DIG" 72 HOURS BEFORE COMMENCEMENT OF WORK AT "811" AND VERIFY ALL UTILITY AND STORM DRAINAGE SYSTEM LOCATIONS.
- 16. NO CONSTRUCTION OR DEMOLITION SHALL BEGIN UNTIL APPROVAL OF THE FINAL PLANS AND PERMITS ARE GRANTED BY ALL GOVERNING AND REGULATORY AGENCIES.

## SITE PLAN NOTES

THE SURVEY WAS PROVIDED BY MARTIN SURVEYING ASSOCIATES, LLC. DATED 09/06/2022.

- 2. THERE ARE BORDERING VEGETATED WETLANDS (BVW/S) LOCATED ON THE SITE AS INDICATED ON THE PLANS. BVW BOUNDARIES WERE FLAGGED AND LOCATED BY ALL POINTS TECHNOLOGY CORP. IN AUGUST 2022.
- 3. THERE WILL BE MINIMAL GRADING ON SITE IN THE AREAS OF THE MINOR CLEARING, TO ENSURE THAT PROPER DRAINAGE IS MAINTAINED.
- 4. THE CONTRACTOR SHALL FOLLOW THE RECOMMENDED SEQUENCE OF CONSTRUCTION NOTES PROVIDED ON THE EROSION CONTROL PLAN OR SUBMIT AN ALTERNATE PLAN FOR APPROVAL BY THE ENGINEER AND/OR PERMITTING AGENCIES PRIOR TO THE START CONSTRUCTION. ALLOW A MINIMUM OF 14 WORKING DAYS FOR REVIEW.
- 5. PROPER CONSTRUCTION PROCEDURES SHALL BE FOLLOWED ON ALL IMPROVEMENTS WITHIN THIS PARCEL SO AS TO PREVENT THE SILTING OF ANY WATERCOURSE OR BVWS IN ACCORDANCE WITH FEDERAL, STATE, AND LOCAL REGULATIONS. IN ADDITION, THE CONTRACTOR SHALL ADHERE TO THE "EROSION CONTROL PLAN" CONTAINED HEREIN. THE CONTRACTOR SHALL BE RESPONSIBLE TO POST ALL BONDS AS REQUIRED BY GOVERNMENT AGENCIES WHICH WOULD GUARANTEE THE PROPER IMPLEMENTATION OF THE PLAN.
- ALL SITE WORK, MATERIALS OF CONSTRUCTION, AND CONSTRUCTION METHODS FOR EARTHWORK AND STORM DRAINAGE WORK, SHALL CONFORM TO THE SPECIFICATIONS AND DETAILS AND APPLICABLE SECTIONS OF THE PROJECT SPECIFICATIONS MANUAL. OTHERWISE THIS WORK SHALL CONFORM TO THE STATE OF CONNECTICUT DEPARTMENT OF TRANSPORTATION AND PROJECT GEOTECHNICAL REPORT IF THERE IS NO PROJECT SPECIFICATIONS MANUAL. ALL FILL MATERIAL UNDER STRUCTURES AND PAVED AREAS SHALL BE PER THE ABOVE STATED APPLICABLE SPECIFICATIONS, AND/OR PROJECT GEOTECHNICAL REPORT, AND SHALL BE PLACED IN ACCORDANCE WITH THE APPLICABLE SPECIFICATIONS UNDER THE SUPERVISION OF A QUALIFIED PROFESSIONAL ENGINEER. MATERIAL SHALL BE COMPACTED IN 8" LIFTS TO 95% OF THE MAXIMUM DRY DENSITY AS DETERMINED BY ASTM D 1557 AT 95% PERCENT OF OPTIMUM MOISTURE CONTENT.
- 7. ALL DISTURBANCE INCURRED TO PUBLIC, MUNICIPAL, COUNTY, STATE PROPERTY DUE TO CONSTRUCTION SHALL BE RESTORED TO ITS PREVIOUS CONDITION OR BETTER, TO THE SATISFACTION OF THE TOWN OF COLCHESTER AND THE STATE OF CONNECTICUT.
- 8. SHOULD CONTAMINATED SOIL BE ENCOUNTERED ON THE SITE, SUCH SOIL SHALL BE HANDLED IN ACCORDANCE WITH SECTION 5 OF THE GENERAL PERMIT FOR CONTAMINATED SOIL AND/OR SEDIMENT MANAGEMENT (STAGING AND TRANSFER) THAT WAS ISSUED ON SEPTEMBER 20, 2013 BY CT DEEP, WHICH CAN BE FOUND AT:

HTTPS://PORTAL.CT.GOV/-/MEDIA/DEEP/PERMITS\_AND\_LICENSES/ WASTE GENERAL PERMITS/SOILSTAGINGGPPDF.PDF.

ALTHOUGH THE GENERAL PERMIT IS NOW EXPIRED, CT DEEP HAS INSTRUCTED ALL PARTIES THAT MAY ENCOUNTER CONTAMINATED SOIL ON A JOB SITE TO HANDLE SUCH SOIL IN ACCORDANCE WITH SECTION 5.

## **UTILITY NOTES**

- 1. CONTRACTOR IS RESPONSIBLE FOR CONTACTING THE TOWN OF COLCHESTER TO SECURE CONSTRUCTION PERMITS AND FOR PAYMENT OF FEES FOR STREET CUTS AND CONNECTIONS TO EXISTING UTILITIES.
- 2. REFER TO DRAWINGS BY PROJECT DEVELOPER FOR THE ONSITE ELECTRICAL DRAWINGS AND INTERCONNECTION TO EXISTING ELECTRICAL GRID. SITE CONTRACTOR SHALL SUPPLY AND INSTALL PIPE ADAPTERS AS NECESSARY AT BUILDING CONNECTION POINT OR AT EXISTING UTILITY OR PIPE CONNECTION POINT. THESE DETAILS ARE NOT INCLUDED IN THESE PLANS.
- 3. UTILITY LOCATIONS AND PENETRATIONS ARE SHOWN FOR THE CONTRACTOR'S INFORMATION AND SHALL BE VERIFIED WITH THE ELECTRICAL ENGINEER AND THE PROJECT DEVELOPER'S CONSTRUCTION MANAGER PRIOR TO THE START OF CONSTRUCTION.
- 4. THE CONTRACTOR SHALL VISIT THE SITE AND VERIFY THE ELEVATION AND LOCATION OF ALL UTILITIES BY VARIOUS MEANS PRIOR TO BEGINNING ANY EXCAVATION. TEST PITS SHALL BE DUG AT ALL LOCATIONS WHERE PROP. SANITARY SEWERS AND WHERE PROP. STORM PIPING WILL CROSS EXISTING UTILITIES, AND THE HORIZONTAL AND VERTICAL LOCATIONS OF THE UTILITIES SHALL BE DETERMINED. THE CONTRACTOR SHALL CONTACT THE PROJECT DEVELOPER IN THE EVENT OF ANY DISCOVERED OR UNFORESEEN CONFLICTS BETWEEN EXISTING AND PROPOSED SANITARY SEWERS, STORM PIPING AND UTILITIES SO THAT AN APPROPRIATE MODIFICATION MAY BE MADE.
- 5. UTILITY CONNECTION DESIGN AS REFLECTED ON THE PLAN MAY CHANGE SUBJECT TO UTILITY PROVIDER AND GOVERNING AUTHORITY STAFF REVIEW.
- 6. THE CONTRACTOR SHALL ENSURE THAT ALL UTILITY PROVIDERS AND GOVERNING AUTHORITY STANDARDS FOR MATERIALS AND CONSTRUCTION METHODS ARE MET. THE CONTRACTOR SHALL PERFORM PROPER COORDINATION WITH THE RESPECTIVE UTILITY PROVIDER.
- 7. THE CONTRACTOR SHALL ARRANGE FOR AND COORDINATE WITH THE RESPECTIVE UTILITY PROVIDERS FOR SERVICE INSTALLATIONS AND CONNECTIONS. THE CONTRACTOR SHALL COORDINATE WORK TO BE PERFORMED BY THE VARIOUS UTILITY PROVIDERS AND SHALL PAY ALL FEES FOR CONNECTIONS, DISCONNECTIONS, RELOCATIONS, INSPECTIONS, AND DEMOLITION UNLESS OTHERWISE STATED IN THE PROJECT SPECIFICATIONS MANUAL AND/OR GENERAL CONDITIONS OF THE CONTRACT.
- 8. ALL EXISTING PAVEMENT WHERE UTILITY PIPING IS TO BE INSTALLED SHALL BE SAW CUT. AFTER UTILITY INSTALLATION IS COMPLETED, THE CONTRACTOR SHALL INSTALL TEMPORARY AND/OR PERMANENT PAVEMENT REPAIR AS DETAILED ON THE DRAWINGS OR AS REQUIRED BY THE TOWN OF COLCHESTER.
- 9. ALL PIPES SHALL BE LAID ON STRAIGHT ALIGNMENTS AND EVEN GRADES USING A PIPE LASER OR OTHER ACCURATE METHOD.
- 10. RELOCATION OF UTILITY PROVIDER FACILITIES, SUCH AS POLES, SHALL BE DONE IN ACCORDANCE WITH THE REQUIREMENTS OF THE UTILITY PROVIDER.
- THE CONTRACTOR SHALL COMPACT PIPE BACKFILL IN 8" LIFTS ACCORDING TO THE PIPE BEDDING DETAILS. TRENCH BOTTOM SHALL BE STABLE IN HIGH GROUNDWATER AREAS. A PIPE FOUNDATION SHALL BE USED PER THE TRENCH DETAILS AND IN AREAS OF ROCK EXCAVATION.
   CONTRACTOR TO PROVIDE STEEL SLEEVES AND ANNULAR SPACE SAND FILL FOR UTILITY PIPE
- AND CONDUIT CONNECTIONS UNDER FOOTINGS.

  13. ALL UTILITY CONSTRUCTION IS SUBJECT TO INSPECTION FOR APPROVAL PRIOR TO BACKFILLING,
- IN ACCORDANCE WITH THE APPROPRIATE UTILITY PROVIDER REQUIREMENTS.

  14. A ONE-FOOT MINIMUM VERTICAL CLEARANCE BETWEEN WATER, GAS, ELECTRICAL, AND
- TELEPHONE LINES AND STORM PIPING SHALL BE PROVIDED. A SIX-INCH MINIMUM CLEARANCE SHALL BE MAINTAINED BETWEEN STORM PIPING AND SANITARY SEWER. A 6-INCH TO 18-INCH VERTICAL CLEARANCE BETWEEN SANITARY SEWER PIPING AND STORM PIPING SHALL REQUIRE CONCRETE ENCASEMENT OF THE SANITARY PIPING.
- 15. THE CONTRACTOR SHALL RESTORE ANY UTILITY STRUCTURE, PIPE, CONDUIT, PAVEMENT, CURBING, SIDEWALKS, DRAINAGE STRUCTURE, SWALE OR LANDSCAPED AREAS DISTURBED DURING CONSTRUCTION, TO THEIR ORIGINAL CONDITION OR BETTER TO THE SATISFACTION OF THE PROJECT DEVELOPER AND THE TOWN OF COLCHESTER.
- 16. INFORMATION ON EXISTING UTILITIES AND STORM DRAINAGE HAS BEEN COMPILED FROM AVAILABLE INFORMATION INCLUDING UTILITY PROVIDER AND MUNICIPAL RECORD MAPS AND/OR FIELD SURVEY, AND IS NOT GUARANTEED CORRECT OR COMPLETE. UTILITIES AND STORM DRAINAGE ARE SHOWN TO ALERT THE CONTRACTOR TO THEIR PRESENCE. THE CONTRACTOR IS SOLELY RESPONSIBLE FOR DETERMINING ACTUAL LOCATIONS AND ELEVATIONS OF ALL UTILITIES AND STORM DRAINAGE INCLUDING SERVICES. CONTACT "CALL BEFORE YOU DIG" AT 811 72 HOURS PRIOR TO CONSTRUCTION AND VERIFY ALL UNDERGROUND AND OVERHEAD UTILITY AND STORM DRAINAGE LOCATIONS. THE CONTRACTOR SHALL EMPLOY THE USE OF A UTILITY LOCATING COMPANY TO PROVIDE SUBSURFACE UTILITY ENGINEERING CONSISTING OF DESIGNATING UTILITIES AND STORM PIPING ON PRIVATE PROPERTY WITHIN THE CONTRACT LIMIT AND CONSISTING OF DESIGNATING AND LOCATING WHERE PROP. UTILITIES AND STORM PIPING CROSS EXISTING UTILITIES AND STORM PIPING WITHIN THE CONTRACT LIMITS.
- 17. THE CONTRACTOR SHALL ARRANGE AND COORDINATE WITH UTILITY PROVIDERS FOR WORK TO BE PERFORMED BY UTILITY PROVIDERS. THE CONTRACTOR SHALL PAY ALL UTILITY FEES UNLESS OTHERWISE STATED IN THE PROJECT SPECIFICATION MANUAL AND GENERAL CONDITIONS, AND REPAIR PAVEMENTS AS NECESSARY.
- 18. ELECTRIC DRAWINGS AND REQUIREMENTS ARE NOT INCLUDED AS PART OF THIS DRAWING SET AND SHOULD BE OBTAINED FROM THE PROJECT DEVELOPER.
- 19. ALTERNATIVE METHODS AND PRODUCTS OTHER THAN THOSE SPECIFIED MAY BE USED IF REVIEWED AND APPROVED BY THE PROJECT DEVELOPER, ENGINEER, AND APPROPRIATE REGULATORY AGENCIES PRIOR TO INSTALLATION.
- 20. THE CONTRACTOR SHALL MAINTAIN ALL FLOWS AND UTILITY CONNECTIONS TO EXISTING BUILDINGS WITHOUT INTERRUPTION UNLESS/UNTIL AUTHORIZED TO DISCONNECT BY THE PROJECT DEVELOPER, TOWN OF COLCHESTER, UTILITY PROVIDERS AND GOVERNING AUTHORITIES.

### **GENERAL LEGEND** PROPOSED **EXISTING** PROPERTY LINE BUILDING SETBACK SOLAR SETBACK EASEMENT \_\_\_\_\_\_\_ • TREE LINE WETLAND WETLAND BUFFER - - - - - - - - - -VERNAL POOL **VERNAL POOL** \_\_ · \_ · \_ · \_ BUFFER WATERCOURSE WATERCOURSE BUFFER MAJOR CONTOUR MINOR CONTOUR UNDERGROUND —— Е —— Е — ELECTRIC OVERHEAD ELECTRIC GAS LINE WATER LINE \_\_\_\_\_w \_\_\_\_w \_\_\_\_

SOLID FENCE

CHAIN LINK FENCE

LIMIT OF

DISTURBANCE

FILTER SOCK

SILT FENCE

BAFFLE

#### 524 NLR LLC

9 NOVELTY LANE, UNIT 9B ESSEX, CT 06426



| 567 VAUXHALL STREET EXTENSION - SUITE 311 | WATERFORD, CT 06385 PHONE: (860)-663-1697 | WWW.ALLPOINTSTECH.COM FAX: (860)-663-093

## CSC PERMIT SET

NO DATE REVISION
0 03/07/23 FOR FILING: KAM

1 06/15/23 FOR FILING: RCB

3 09/08/23 FENCE REVISIONS: RCB

4 09/28/23 ADD EX. POLE CALOUTS: RCE 5 10/20/23 ADD LOD EXHIBIT DWG: RCB

2 09/01/23 FENCE REVISIONS: RCB

5 | 10/20/23 | ADD LOD EXHIBIT DWG: R 6 | 04/15/24 | REVISED SEED MIX: RCB

7 05/03/24 REVISED SITE LAYOUT: UKA 8 05/16/24 REVISED PER CLIENT :TEL

8 | 05/16/24 | REVISED PER CLIENT :TEL 9 | 06/11/24 | REVISED PER CLIENT :TEL

10 06/21/24 REVISED PER CLIENT :TEL

# DESIGN PROFESSIONAL OF RECORD PROF: ROBERT C. BURNS, P.E.

COMP: ALL-POINTS TECHNOLOGY
CORPORATION, P.C.
ADD: 567 VAUXHALL STREET
EXTENSION - SUITE 311
WATERFORD, CT 06385

— x— x— x—

— FS —— FS —

OWNER: FIVE J, LLC

ADDRESS: 524 NEW LONDON ROAD

COLCHESTER, CT

SCRAPYARD SOLAR

SITE 524 NEW LONDON ROAD ADDRESS: COLCHESTER, CT

APT FILING NUMBER: CT580160

DATE: 03/07/23 CHECKED BY: RCB

SHEET TITLE:

**GENERAL NOTES** 

SHEET NUMBER

GN-1



DRAWN BY: ELZ

## **ENVIRONMENTAL NOTES - RESOURCES PROTECTION MEASURES**

#### WETLAND PROTECTION PROGRAM

AS A RESULT OF THE PROJECT'S LOCATION IN THE VICINITY OF SENSITIVE WETLAND RESOURCES, THE FOLLOWING PROTECTION PROGRAM SHALL BE IMPLEMENTED BY THE CONTRACTOR TO AVOID UNINTENTIONAL IMPACTS TO PROXIMATE WETLAND RESOURCES DURING CONSTRUCTION ACTIVITIES.

IT IS OF THE UTMOST IMPORTANCE THAT THE CONTRACTOR COMPLIES WITH THE REQUIREMENT FOR THE INSTALLATION OF PROTECTIVE MEASURES AND THE EDUCATION OF ITS EMPLOYEES AND SUBCONTRACTORS PERFORMING WORK ON THE PROJECT SITE. THE WETLAND PROTECTION MEASURES SHALL BE IMPLEMENTED AND MAINTAINED THROUGHOUT THE DURATION OF CONSTRUCTION ACTIVITIES UNTIL PERMANENT STABILIZATION OF SITE SOILS HAS OCCURRED.

ALL-POINTS TECHNOLOGY CORPORATION, P.C. ("APT") WILL SERVE AS THE ENVIRONMENTAL MONITOR FOR THIS PROJECT TO ENSURE THAT THESE PROTECTION MEASURES ARE IMPLEMENTED PROPERLY AND WILL PROVIDE AN EDUCATION SESSION ON THE PROJECT'S PROXIMITY TO SENSITIVE WETLANDS PRIOR TO THE START OF CONSTRUCTION ACTIVITIES. THE CONTRACTOR SHALL CONTACT DEAN GUSTAFSON, SENIOR WETLAND SCIENTIST AT APT, AT LEAST 5 BUSINESS DAYS PRIOR TO THE PRE-CONSTRUCTION MEETING. MR. GUSTAFSON CAN BE REACHED BY PHONE AT (860) 552-2033 OR VIA EMAIL AT DGUSTAFSON@ALLPOINTSTECH.COM.

THIS RESOURCES PROTECTION PROGRAM CONSISTS OF SEVERAL COMPONENTS INCLUDING: EDUCATION OF ALL CONTRACTORS AND SUB-CONTRACTORS PRIOR TO INITIATION OF WORK ON THE SITE; INSTALLATION OF EROSION CONTROLS; PETROLEUM MATERIALS STORAGE AND SPILL PREVENTION; PROTECTIVE MEASURES; RARE SPECIES PROTECTION MEASURES; HERBICIDE, PESTICIDE, AND SALT RESTRICTIONS; AND REPORTING.

#### 1. CONTRACTOR EDUCATION:

- a. PRIOR TO WORK ON SITE AND INITIAL DEPLOYMENT/MOBILIZATION OF EQUIPMENT AND MATERIALS, THE CONTRACTOR SHALL ATTEND AN EDUCATIONAL SESSION AT THE PRE-CONSTRUCTION MEETING WITH APT. THIS ORIENTATION AND EDUCATIONAL SESSION WILL CONSIST OF INFORMATION SUCH AS, BUT NOT LIMITED TO: IDENTIFICATION OF WETLAND RESOURCES PROXIMATE TO WORK AREAS, REPRESENTATIVE PHOTOGRAPHS OF TYPICAL HERPETOFAUNA THAT MAY BE ENCOUNTERED, TYPICAL SPECIES BEHAVIOR, AND PROPER PROCEDURES IF SPECIES ARE ENCOUNTERED, AND THE ENVIRONMENTALLY SENSITIVE NATURE OF THE DEVELOPMENT SITE.
- b. THE CONTRACTOR'S PROJECT MONITOR WILL BE PROVIDED WITH CELL PHONE AND EMAIL CONTACTS FOR APT PERSONNEL. EDUCATIONAL POSTER MATERIALS WILL BE PROVIDED BY APT AND DISPLAYED ON THE JOB SITE TO MAINTAIN WORKER AWARENESS AS THE PROJECT PROGRESSES.
- c. APT WILL ALSO POST CAUTION SIGNS THROUGHOUT THE PROJECT SITE FOR THE DURATION OF THE CONSTRUCTION PROJECT PROVIDING NOTICE OF THE ENVIRONMENTALLY SENSITIVE NATURE OF THE WORK AREA.

#### 2. EROSION AND SEDIMENTATION CONTROLS/ISOLATION BARRIERS

- a. PLASTIC NETTING USED IN A VARIETY OF EROSION CONTROL PRODUCTS (I.E., EROSION CONTROL BLANKETS, FIBER ROLLS [WATTLES], REINFORCED SILT FENCE) HAS BEEN FOUND TO ENTANGLE WILDLIFE, INCLUDING REPTILES, AMPHIBIANS, BIRDS AND SMALL MAMMALS. NO PERMANENT EROSION CONTROL PRODUCTS OR REINFORCED SILT FENCE WILL BE USED ON THE PROJECT. TEMPORARY EROSION CONTROL PRODUCTS THAT WILL BE EXPOSED AT THE GROUND SURFACE AND REPRESENT A POTENTIAL FOR WILDLIFE ENTANGLEMENT WILL USE EITHER EROSION CONTROL BLANKETS AND FIBER ROLLS COMPOSED OF PROCESSED FIBERS MECHANICALLY BOUND TOGETHER TO FORM A CONTINUOUS MATRIX (NETLESS) OR NETTING COMPOSED OF PLANAR WOVEN NATURAL BIODEGRADABLE FIBER TO AVOID/MINIMIZE WILDLIFE ENTANGLEMENT.
- b. THE EXTENT OF THE EROSION CONTROLS WILL BE AS SHOWN ON THE SITE PLANS. THE CONTRACTOR SHALL HAVE ADDITIONAL SEDIMENTATION AND EROSION CONTROLS STOCKPILED ON SITE SHOULD FIELD OR CONSTRUCTION CONDITIONS WARRANT EXTENDING DEVICES. IN ADDITION TO THE CONTRACTOR MAKING THESE DETERMINATIONS, REQUESTS FOR ADDITIONAL CONTROLS WILL ALSO BE AT THE DISCRETION OF THE ENVIRONMENTAL MONITOR.
- c. THE CONTRACTOR SHALL BE RESPONSIBLE FOR DAILY INSPECTIONS OF THE SEDIMENTATION AND EROSION CONTROLS FOR TEARS OR BREACHES AND ACCUMULATION LEVELS OF SEDIMENT, PARTICULARLY FOLLOWING STORM EVENTS THAT GENERATE A DISCHARGE, AS DEFINED BY AND IN ACCORDANCE WITH APPLICABLE LOCAL, STATE AND FEDERAL REGULATIONS. THE CONTRACTOR SHALL NOTIFY THE APT ENVIRONMENTAL MONITOR WITHIN 24 HOURS OF ANY BREACHES OF THE SEDIMENTATION AND EROSION CONTROLS AND ANY SEDIMENT RELEASES BEYOND THE PERIMETER CONTROLS THAT IMPACT WETLANDS, THE VERNAL POOL, OR AREAS WITHIN 100 FEET OF WETLANDS. THE APT ENVIRONMENTAL MONITOR WILL PROVIDE PERIODIC INSPECTIONS OF THE SEDIMENTATION AND EROSION CONTROLS THROUGHOUT THE DURATION OF CONSTRUCTION ACTIVITIES ONLY AS IT PERTAINS TO THEIR FUNCTION TO PROTECT NEARBY WETLANDS. SUCH INSPECTIONS WILL GENERALLY OCCUR ONCE PER MONTH. THE FREQUENCY OF MONITORING MAY INCREASE DEPENDING UPON SITE CONDITIONS, LEVEL OF CONSTRUCTION ACTIVITIES IN PROXIMITY TO SENSITIVE RECEPTORS, OR AT THE REQUEST OF REGULATORY AGENCIES. IF THE ENVIRONMENTAL MONITOR IS NOTIFIED BY THE CONTRACTOR OF A SEDIMENT RELEASE, AN INSPECTION WILL BE SCHEDULED SPECIFICALLY TO INVESTIGATE AND EVALUATE POSSIBLE IMPACTS TO WETLAND
- d. THIRD PARTY MONITORING OF SEDIMENTATION AND EROSION CONTROLS WILL BE PERFORMED BY OTHER PARTIES, AS NECESSARY, UNDER APPLICABLE LOCAL, STATE AND/OR FEDERAL REGULATIONS AND PERMIT CONDITIONS.
- e. NO EQUIPMENT, VEHICLES OR CONSTRUCTION MATERIALS SHALL BE STORED WITHIN 100 FEET OF WETLAND RESOURCES.
- f. ALL SILT FENCING AND OTHER EROSION CONTROL DEVICES SHALL BE REMOVED WITHIN 30 DAYS OF COMPLETION OF WORK AND PERMANENT STABILIZATION OF SITE SOILS. IF FIBER ROLLS/WATTLES, STRAW BALES, OR OTHER NATURAL MATERIAL EROSION CONTROL PRODUCTS ARE USED, SUCH DEVICES WILL NOT BE LEFT IN PLACE TO BIODEGRADE AND SHALL BE PROMPTLY REMOVED AFTER SOILS ARE STABLE SO AS NOT TO CREATE A BARRIER TO WILDLIFE MOVEMENT. SEED FROM SEEDING OF SOILS SHOULD NOT SPREAD OVER FIBER ROLLS/WATTLES AS IT MAKES THEM HARDER TO REMOVE ONCE SOILS ARE STABILIZED BY VEGETATION.

#### 3. PETROLEUM MATERIALS STORAGE AND SPILL PREVENTION

- a. CERTAIN PRECAUTIONS ARE NECESSARY TO STORE PETROLEUM MATERIALS, REFUEL AND CONTAIN AND PROPERLY CLEAN UP ANY INADVERTENT FUEL OR PETROLEUM (I.E., OIL, HYDRAULIC FLUID, ETC.) SPILL DUE TO THE PROJECT'S LOCATION IN PROXIMITY TO WETLAND RESOURCES.
- b. A SPILL CONTAINMENT KIT CONSISTING OF A SUFFICIENT SUPPLY OF ABSORBENT PADS AND ABSORBENT MATERIAL WILL BE MAINTAINED BY THE CONTRACTOR AT THE CONSTRUCTION SITE THROUGHOUT THE DURATION OF THE PROJECT. IN ADDITION, A WASTE DRUM WILL BE KEPT ON SITE TO CONTAIN ANY USED ABSORBENT PADS/MATERIAL FOR PROPER AND TIMELY DISPOSAL OFF SITE IN ACCORDANCE WITH APPLICABLE LOCAL, STATE AND FEDERAL LAWS.

#### c. SERVICING OF MACHINERY SHALL NOT OCCUR WITHIN 100 FEET OF WETLANDS.

d. AT A MINIMUM, THE FOLLOWING PETROLEUM AND HAZARDOUS MATERIALS STORAGE AND REFUELING RESTRICTIONS AND SPILL RESPONSE PROCEDURES WILL BE ADHERED TO BY THE CONTRACTOR.

#### i.PETROLEUM AND HAZARDOUS MATERIALS STORAGE AND REFUELING

- 1. REFUELING OF VEHICLES OR MACHINERY SHALL OCCUR A MINIMUM OF 100 FEET FROM WETLANDS AND SHALL TAKE PLACE ON AN IMPERVIOUS PAD (I.E. COMPACTED GRAVEL ROAD OR PAVED AREA) WITH SECONDARY CONTAINMENT DESIGNED TO
- 2. ANY FUEL OR HAZARDOUS MATERIALS THAT MUST BE KEPT ON SITE SHALL BE STORED ON AN IMPERVIOUS SURFACE UTILIZING SECONDARY CONTAINMENT A MINIMUM OF 100 FEET FROM WETLANDS

#### ii. INITIAL SPILL RESPONSE PROCEDURES

- 1. STOP OPERATIONS AND SHUT OFF EQUIPMENT.
- 2. REMOVE ANY SOURCES OF SPARK OR FLAME.
- 3. CONTAIN THE SOURCE OF THE SPILL.
- 4. DETERMINE THE APPROXIMATE VOLUME OF THE SPILL.
- 5. IDENTIFY THE LOCATION OF NATURAL FLOW PATHS TO PREVENT THE RELEASE OF THE SPILL TO SENSITIVE NEARBY WETLANDS AND VERNAL POOL.
- 6. ENSURE THAT FELLOW WORKERS ARE NOTIFIED OF THE SPILL.

#### iii.SPILL CLEAN UP & CONTAINMENT

- 1. OBTAIN SPILL RESPONSE MATERIALS FROM THE ON-SITE SPILL RESPONSE KIT. PLACE ABSORBENT MATERIALS DIRECTLY ON THE RELEASE AREA.
- 2. LIMIT THE SPREAD OF THE SPILL BY PLACING ABSORBENT MATERIALS AROUND THE PERIMETER OF THE SPILL.
- 3. ISOLATE AND ELIMINATE THE SPILL SOURCE.
- 4. CONTACT APPROPRIATE LOCAL, STATE AND/OR FEDERAL AGENCIES, AS NECESSARY
- 5. CONTACT A DISPOSAL COMPANY TO PROPERLY DISPOSE OF CONTAMINATED MATERIALS.

- iv. REPORTING 1. OBTAIN SPILL RESPONSE MATERIALS FROM THE ON-SITE SPILL RESPONSE KIT. PLACE ABSORBENT MATERIALS DIRECTLY ON
- 2. LIMIT THE SPREAD OF THE SPILL BY PLACING ABSORBENT MATERIALS AROUND THE PERIMETER OF THE SPILL.

#### 4. HERBICIDE, PESTICIDE, AND SALT RESTRICTIONS

- a. THE USE OF HERBICIDES AND PESTICIDES AT THE FACILITY SHALL BE MINIMIZED. IF HERBICIDES AND/OR PESTICIDES ARE REQUIRED AT THE FACILITY, THEIR USE WILL BE USED IN ACCORDANCE WITH CURRENT INTEGRATED PEST MANAGEMENT ("IPM") PRINCIPLES WITH PARTICULAR ATTENTION TO AVOID/MINIMIZE APPLICATIONS WITHIN 100 FEET OF WETLAND AND VERNAL POOL
- b. MAINTENANCE OF THE FACILITY DURING THE WINTER MONTHS SHALL NOT INCLUDE THE APPLICATION OF SALT OR SIMILAR PRODUCTS FOR MELTING SNOW OR ICE.

## 5. REPORTING

- a. COMPLIANCE MONITORING REPORTS (BRIEF NARRATIVE AND APPLICABLE PHOTOS) DOCUMENTING EACH APT INSPECTION WILL BE SUBMITTED BY APT TO THE PERMITTEE AND ITS CONTRACTOR FOR COMPLIANCE VERIFICATION OF THESE PROTECTION MEASURES. THESE REPORTS ARE NOT TO BE USED TO DOCUMENT COMPLIANCE WITH ANY OTHER PERMIT AGENCY APPROVAL CONDITIONS (I.E., DEEP STORMWATER PERMIT MONITORING, ETC.). ANY NON-COMPLIANCE OBSERVATIONS OF EROSION CONTROL MEASURES OR EVIDENCE OF EROSION OR SEDIMENT RELEASE WILL BE IMMEDIATELY REPORTED TO THE PERMITTEE AND ITS CONTRACTOR AND INCLUDED IN THE REPORTS.
- b. FOLLOWING COMPLETION OF THE CONSTRUCTION PROJECT, APT WILL PROVIDE A FINAL COMPLIANCE MONITORING REPORT TO THE PERMITTEE DOCUMENTING IMPLEMENTATION OF THE WETLAND PROTECTION PROGRAM AND MONITORING OBSERVATIONS. THE PERMITTEE IS RESPONSIBLE FOR PROVIDING A COPY OF THE FINAL COMPLIANCE MONITORING REPORT TO THE CONNECTICUT SITING COUNCIL FOR COMPLIANCE VERIFICATION.

#### 524 NLR LLC

9 NOVELTY LANE, UNIT 9B **ESSEX. CT 06426** 



567 VAUXHALL STREET EXTENSION - SUITE 311 WATERFORD, CT 06385 PHONE: (860)-663-169 WWW.ALLPOINTSTECH.COM FAX: (860)-663-093

#### **CSC PERMIT SET**

#### NO DATE REVISION 0 | 03/07/23 | FOR FILING: KAM

- 1 06/15/23 FOR FILING: RCB
- 2 09/01/23 FENCE REVISIONS: RCB
- 3 | 09/08/23 | FENCE REVISIONS: RCB
- 4 09/28/23 ADD EX. POLE CALOUTS: RCE
- 5 | 10/20/23 | ADD LOD EXHIBIT DWG: RCB
- 6 04/15/24 REVISED SEED MIX: RCB
- 7 05/03/24 REVISED SITE LAYOUT: UKA
- 8 05/16/24 REVISED PER CLIENT :TEL
- 9 06/11/24 REVISED PER CLIENT :TEL
- 10 06/21/24 REVISED PER CLIENT :TEL

#### **DESIGN PROFESSIONAL OF RECORD**

WATERFORD, CT 06385

PROF: ROBERT C. BURNS, P.E. **COMP: ALL-POINTS TECHNOLOGY** CORPORATION, P.C. ADD: 567 VAUXHALL STREET **EXTENSION - SUITE 311** 

OWNER: FIVE J, LLC

ADDRESS: 524 NEW LONDON ROAD COLCHESTER, CT

SCRAPYARD SOLAR

SITE 524 NEW LONDON ROAD ADDRESS: COLCHESTER, CT

**APT FILING NUMBER: CT580160** DRAWN BY: ELZ


DATE: 03/07/23 | CHECKED BY: RCB

SHEET TITLE:

**ENVIRONMENTAL NOTES** 

**SHEET NUMBER** 



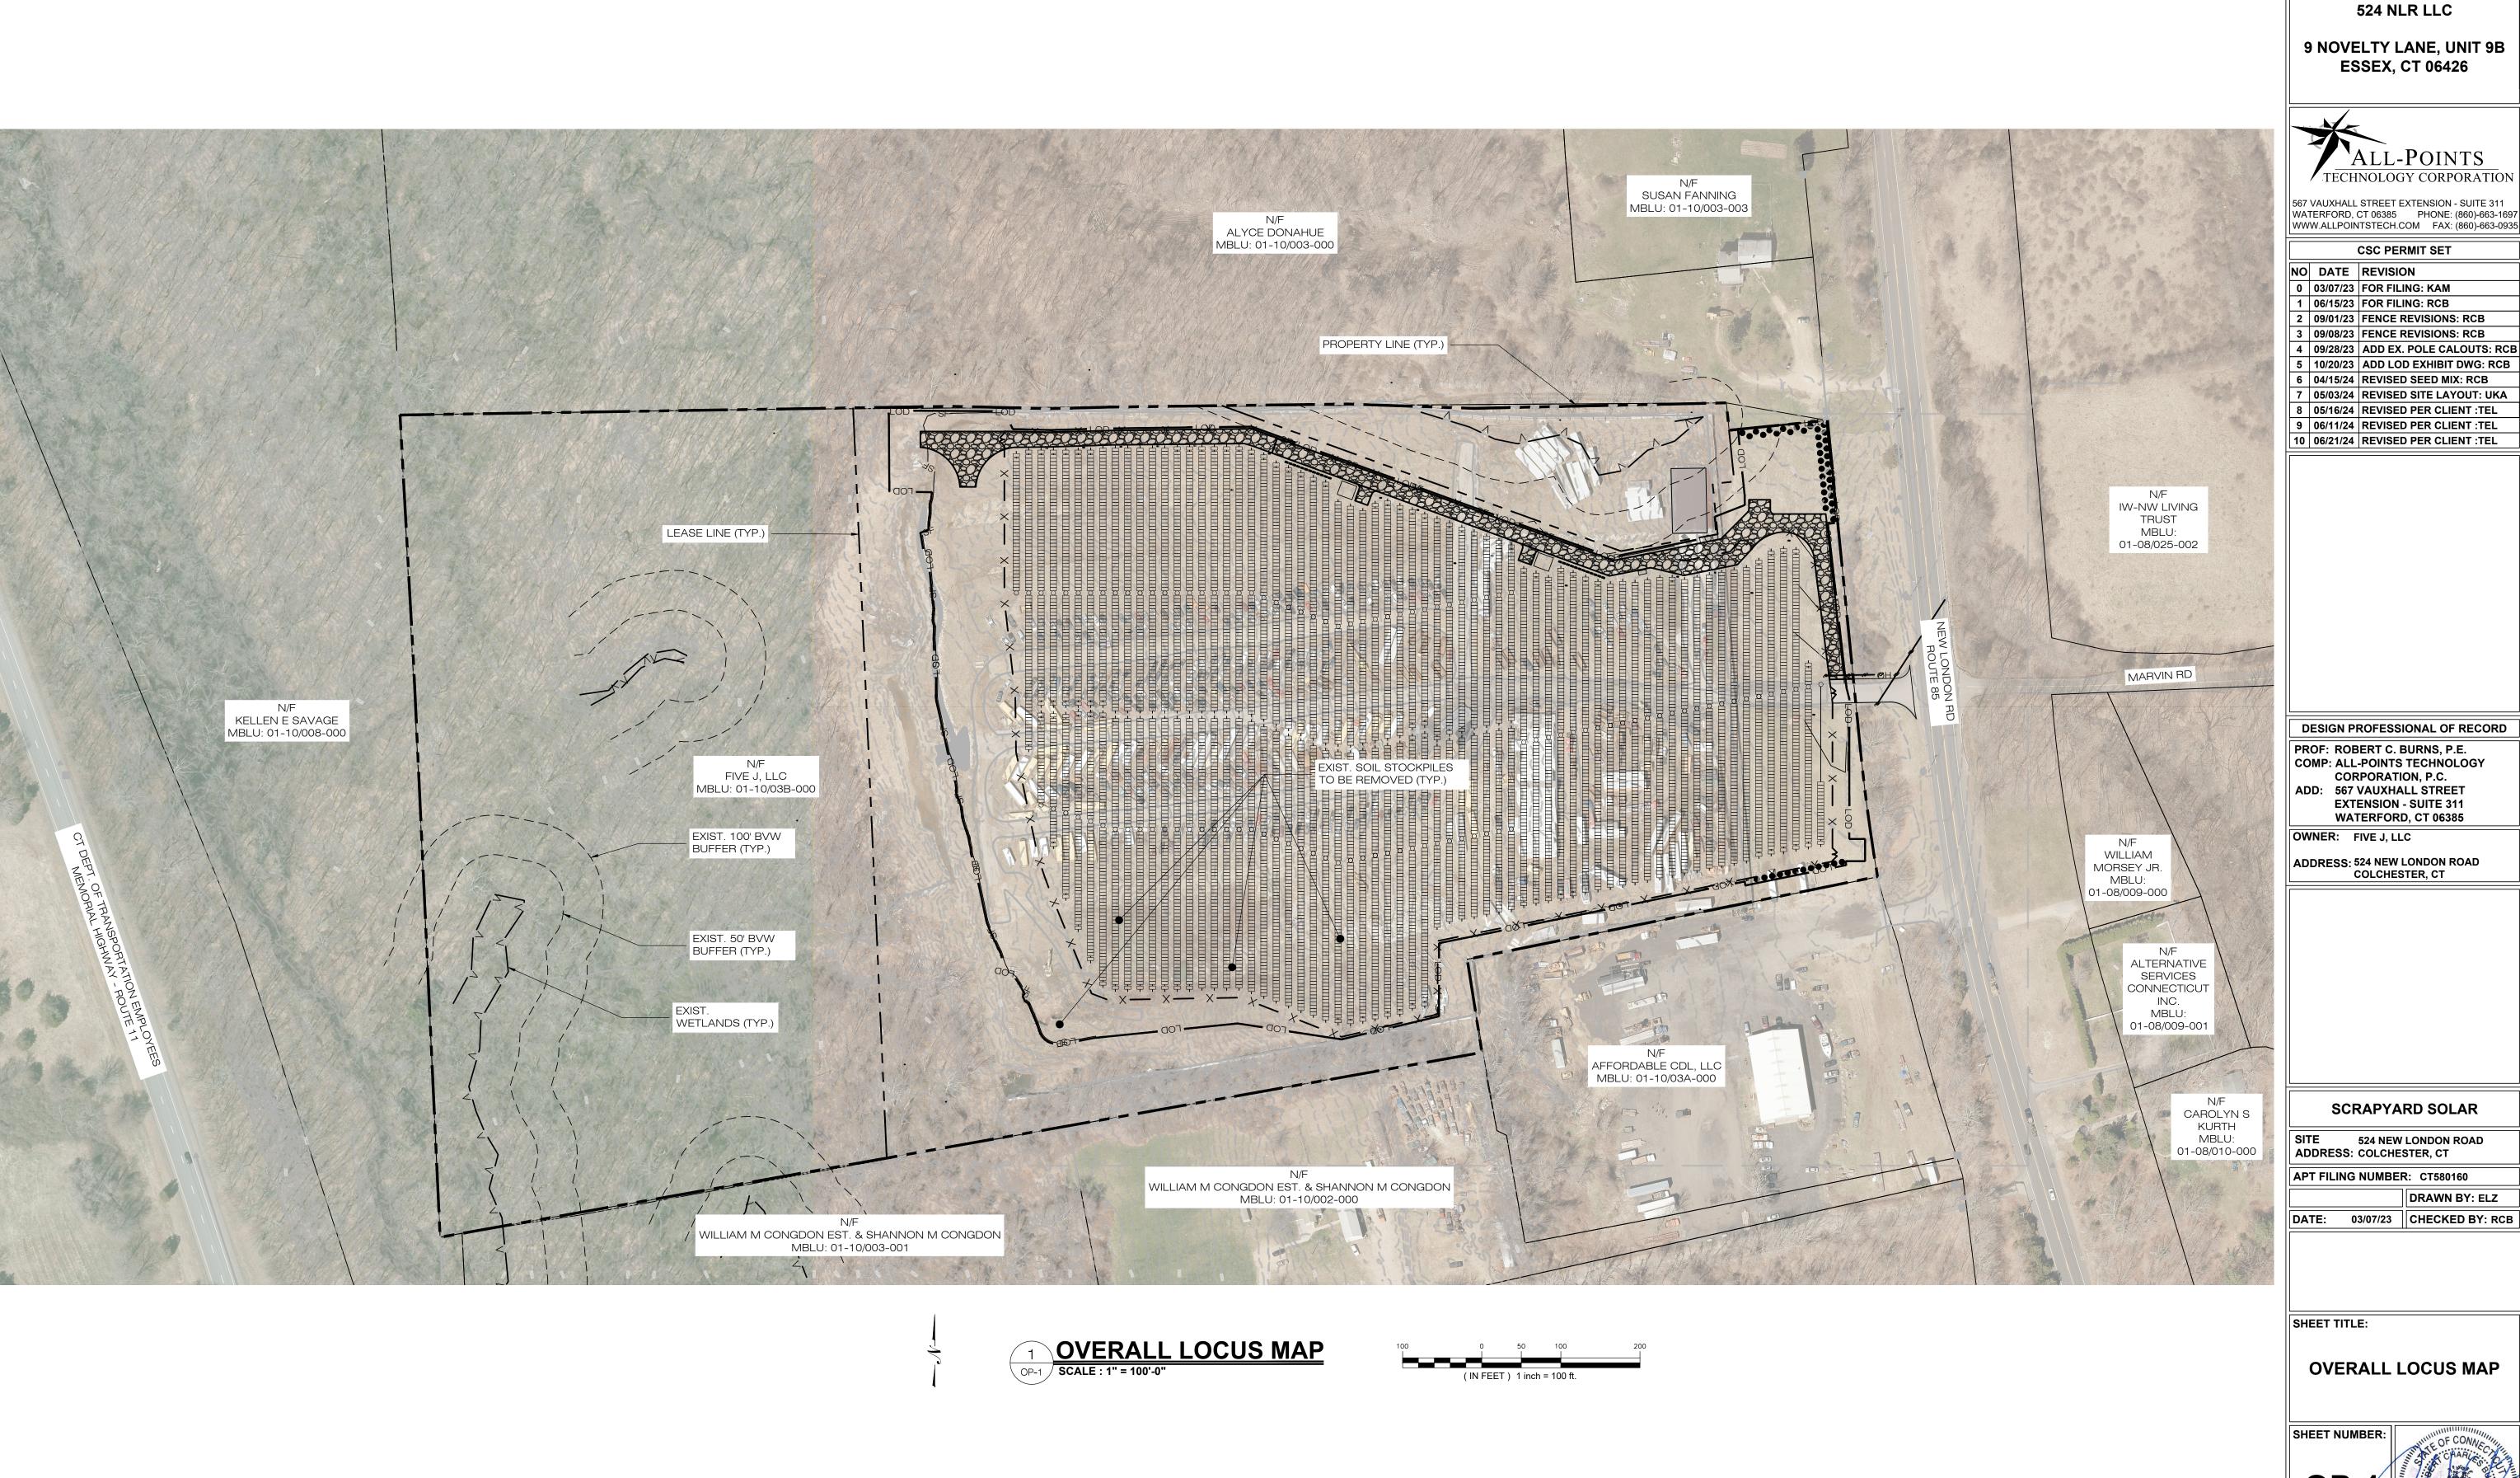

- 4 09/28/23 ADD EX. POLE CALOUTS: RCB



## **EROSION CONTROL NOTES**

EROSION AND SEDIMENT CONTROL PLAN NOTES

- THE CONTRACTOR SHALL CONSTRUCT ALL SEDIMENT AND EROSION CONTROLS IN ACCORDANCE WITH THE 2002 CONNECTICUT GUIDELINES FOR SOIL EROSION AND SEDIMENT CONTROL, LATEST EDITION, IN ACCORDANCE WITH THE CONTRACT DOCUMENTS, AND AS DIRECTED BY THE TOWN OF COLCHESTER, PERMITTEE, AND/OR SWPCP MONITOR. ALL PERIMETER SEDIMENTATION AND EROSION CONTROL MEASURES SHALL BE INSTALLED PRIOR TO THE START OF CLEARING AND GRUBBING AND DEMOLITION OPERATIONS.
- THESE DRAWINGS ARE ONLY INTENDED TO DESCRIBE THE SEDIMENT AND EROSION CONTROL MEASURES FOR THIS SITE. SEE CONSTRUCTION SEQUENCE FOR ADDITIONAL INFORMATION. ALL TEMPORARY EROSION AND SEDIMENT CONTROL MEASURES SHOWN ON THE EROSION & SEDIMENT CONTROL PLAN ARE SHOWN AS REQUIRED BY THE ENGINEER. THE CONTRACTOR SHALL BE RESPONSIBLE FOR ENSURING THAT ALL EROSION CONTROL MEASURES ARE CONFIGURED AND CONSTRUCTED IN A MANNER THAT WILL MINIMIZE EROSION OF SOILS AND PREVENT THE TRANSPORT OF SEDIMENTS AND OTHER POLLUTANTS TO STORM DRAINAGE SYSTEMS AND/OR WATERCOURSES. ACTUAL SITE CONDITIONS OR SEASONAL AND CLIMATIC CONDITIONS MAY WARRANT ADDITIONAL CONTROLS OR CONFIGURATIONS, AS REQUIRED, AND AS DIRECTED BY THE PERMITTEE AND/OR SWPCP MONITOR. REFER TO SITE PLAN FOR GENERAL INFORMATION AND OTHER CONTRACT PLANS FOR APPROPRIATE INFORMATION.
- A BOND OR LETTER OF CREDIT MAY BE REQUIRED TO BE POSTED WITH THE GOVERNING AUTHORITY FOR THE EROSION CONTROL INSTALLATION AND MAINTENANCE.
- 4. THE CONTRACTOR SHALL APPLY THE MINIMUM EROSION & SEDIMENT CONTROL MEASURES SHOWN ON THE PLAN IN CONJUNCTION WITH CONSTRUCTION SEQUENCING, SUCH THAT ALL ACTIVE WORK ZONES ARE PROTECTED. ADDITIONAL AND/OR ALTERNATIVE SEDIMENT AND EROSION CONTROL MEASURES MAY BE INSTALLED DURING THE CONSTRUCTION PERIOD IF FOUND NECESSARY BY THE CONTRACTOR, OWNER, SITE ENGINEER, MUNICIPAL OFFICIALS, OR ANY GOVERNING AGENCY. THE CONTRACTOR SHALL CONTACT THE OWNER AND APPROPRIATE GOVERNING AGENCIES FOR APPROVAL IF ALTERNATIVE CONTROLS OTHER THAN THOSE SHOWN ON THE PLANS ARE PROPOSED BY THE CONTRACTOR.
- THE CONTRACTOR SHALL TAKE EXTREME CARE DURING CONSTRUCTION SO AS NOT TO DISTURB UNPROTECTED WETLAND AREAS OR INSTALLED SEDIMENTATION AND EROSION CONTROL MEASURES. THE CONTRACTOR SHALL INSPECT ALL SEDIMENT AND EROSION CONTROLS WEEKLY AND WITHIN 24 HOURS OF A STORM WITH A RAINFALL AMOUNT OF 0.25 INCHES OR GREATER TO VERIFY THAT THE CONTROLS ARE OPERATING PROPERLY AND MAKE REPAIRS AS NECESSARY IN A TIMELY MANOR.
- THE CONTRACTOR SHALL KEEP A SUPPLY OF EROSION CONTROL MATERIAL (SILT FENCE, COMPOST FILTER SOCK, EROSION CONTROL BLANKET, ETC.) ON-SITE FOR PERIODIC MAINTENANCE AND EMERGENCY REPAIRS.
- ALL FILL MATERIAL PLACED ADJACENT TO ANY WETLAND AREA SHALL BE GOOD QUALITY, WITH LESS THAN 5% FINES PASSING THROUGH A #200 SIEVE (BANK RUN), SHALL BE PLACED IN MAXIMUM ONE FOOT LIFTS, AND SHALL BE COMPACTED TO 95% MAX. DRY DENSITY MODIFIED PROCTOR OR AS SPECIFIED IN THE CONTRACT SPECIFICATIONS.
- PROTECT EXISTING TREES THAT ARE TO BE SAVED BY FENCING, ORANGE SAFETY FENCE, CONSTRUCTION TAPE, OR EQUIVALENT FENCING/TAPE. ANY LIMB TRIMMING SHOULD BE DONE AFTER CONSULTATION WITH AN ARBORIST AND BEFORE CONSTRUCTION BEGINS IN THAT AREA; FENCING SHALL BE MAINTAINED AND REPAIRED DURING CONSTRUCTION.
- CONSTRUCTION ENTRANCES (ANTI-TRACKING PADS) SHALL BE INSTALLED PRIOR TO ANY SITE EXCAVATION OR CONSTRUCTION ACTIVITY AND SHALL BE MAINTAINED THROUGHOUT THE DURATION OF ALL CONSTRUCTION IF REQUIRED. THE LOCATION OF THE TRACKING PADS MAY CHANGE AS VARIOUS PHASES OF CONSTRUCTION ARE COMPLETED. CONTRACTOR SHALL ENSURE THAT ALL VEHICLES EXITING THE SITE ARE PASSING OVER THE ANTI-TRACKING PADS PRIOR TO EXITING.
- 10. ALL CONSTRUCTION SHALL BE CONTAINED WITHIN THE LIMIT OF DISTURBANCE, WHICH SHALL BE MARKED WITH SILT FENCE, SAFETY FENCE, STRAW BALES, RIBBONS, OR OTHER MEANS PRIOR TO CLEARING. CONSTRUCTION ACTIVITY SHALL REMAIN ON THE UPHILL SIDE OF THE SEDIMENT BARRIER UNLESS WORK IS SPECIFICALLY CALLED FOR ON THE DOWNHILL SIDE OF THE BARRIER.
- 11. NO CUT OR FILL SLOPES SHALL EXCEED 2:1 EXCEPT WHERE STABILIZED BY ROCK FACED EMBANKMENTS OR EROSION CONTROL BLANKETS. ALL SLOPES SHALL BE SEEDED AND BANKS WILL BE STABILIZED IMMEDIATELY UPON COMPLETION OF FINAL GRADING UNTIL TURF IS ESTABLISHED.
- 12. DIRECT ALL DEWATERING PUMP DISCHARGE TO A SEDIMENT CONTROL DEVICE CONFORMING TO THE GUIDELINES WITHIN THE APPROVED LIMIT OF DISTURBANCE IF REQUIRED. DISCHARGE TO STORM DRAINS OR SURFACE WATERS FROM SEDIMENT CONTROLS SHALL BE CLEAR AND APPROVED BY THE PERMITTEE OR MUNICIPALITY.
- 13. THE CONTRACTOR SHALL MAINTAIN A CLEAN CONSTRUCTION SITE AND SHALL NOT ALLOW THE ACCUMULATION OF RUBBISH OR CONSTRUCTION DEBRIS ON THE SITE. PROPER SANITARY DEVICES SHALL BE MAINTAINED ON-SITE AT ALL TIMES AND SECURED APPROPRIATELY. THE CONTRACTOR SHALL TAKE ALL NECESSARY PRECAUTIONS TO AVOID THE SPILLAGE OF FUEL OR OTHER POLLUTANTS ON THE CONSTRUCTION SITE AND SHALL ADHERE TO ALL APPLICABLE POLICIES AND REGULATIONS RELATED TO SPILL PREVENTION AND RESPONSE/CONTAINMENT.
- 14. MINIMIZE LAND DISTURBANCES. SEED AND MULCH DISTURBED AREAS WITH TEMPORARY MIX AS SOON AS PRACTICABLE (2 WEEK MAXIMUM UNSTABILIZED PERIOD) USING PERENNIAL RYEGRASS AT 40 LBS PER ACRE. MULCH ALL CUT AND FILL SLOPES AND SWALES WITH LOOSE STRAW AT A RATE OF 2 TONS PER ACRE. IF NECESSARY, REPLACE LOOSE STRAW ON SLOPES WITH EROSION CONTROL BLANKETS OR JUTE CLOTH. MODERATELY GRADED AREAS, ISLANDS, AND TEMPORARY CONSTRUCTION STAGING AREAS MAY BE HYDROSEEDED WITH TACKIFIER.
- 15. SWEEP AFFECTED PORTIONS OF OFF SITE ROADS ONE OR MORE TIMES A DAY (OR LESS FREQUENTLY IF TRACKING IS NOT A PROBLEM) DURING CONSTRUCTION. FOR DUST CONTROL, PERIODICALLY MOISTEN EXPOSED SOIL SURFACES WITH WATER ON UNPAVED TRAVELWAYS TO KEEP THE TRAVELWAYS DAMP. CALCIUM CHLORIDE MAY ALSO BE APPLIED TO ACCESS ROADS. DUMP TRUCK LOADS EXITING THE SITE SHALL BE COVERED.
- 16. VEGETATIVE ESTABLISHMENT SHALL OCCUR ON ALL DISTURBED SOIL, UNLESS THE AREA IS UNDER ACTIVE CONSTRUCTION, IT IS COVERED IN STONE OR SCHEDULED FOR PAVING WITHIN 30 DAYS. TEMPORARY SEEDING OR NON-LIVING SOIL PROTECTION OF ALL EXPOSED SOILS AND SLOPES SHALL BE INITIATED WITHIN THE FIRST 7 DAYS OF SUSPENDING WORK IN AREAS TO BE LEFT LONGER THAN 30 DAYS.
- 17. MAINTAIN ALL PERMANENT AND TEMPORARY SEDIMENT CONTROL DEVICES IN EFFECTIVE CONDITION THROUGHOUT THE CONSTRUCTION PERIOD. UPON COMPLETION OF WORK SWEEP CONCRETE PADS, CLEAN THE STORMWATER MANAGEMENT SYSTEMS AND REMOVE ALL TEMPORARY SEDIMENT CONTROLS ONCE THE SITE IS FULLY STABILIZED AND APPROVAL HAS BEEN RECEIVED FROM PERMITTEE OR THE MUNICIPALITY.
- 18. THE SITE WAS DESIGNED TO COMPLY WITH FEDERAL, STATE, AND, IF APPLICABLE, LOCAL STANDARDS, PLUS CURRENT ACCEPTED PRACTICES FOR THE INDUSTRY. ADDITIONAL CONTROLS AND ACTIVITIES MAY BE DEEMED NECESSARY BY THE SWPCP MONITOR DURING CONSTRUCTION AS A RESULT OF UNFORESEEN CONDITIONS AND/OR MEANS AND METHODS. SUCH ITEMS MAY INCLUDE, BUT ARE NOT LIMITED TO: ADDITIONAL FOREBAYS, BASINS, OR UPSTREAM STRUCTURAL CONTROLS, THE USE OF FLOCCULANTS OR FLOCK LOGS TO DECREASE SEDIMENT, DISCHARGE MANAGEMENT SUCH AS ADDITIONAL ARMORING AND FILTERING MEASURES (I.E. STRAW BALES, WATTLES, ETC.), AND HYDROSEEDING WITH RAPIDLY GERMINATING SEED.
- 19. SEEDING MIXTURES SHALL BE AS SPECIFIED ON THE PLAN VIEW AND DETAIL SHEETS.

CONSTRUCTION OPERATION AND MAINTENANCE PLAN - BY CONTRACTOR						
E&S MEASURE	INSPECTION SCHEDULE	MAINTENANCE REQUIRED				
CONSTRUCTION ENTRANCE	DAILY	PLACE ADDITIONAL STONE, EXTEND THE LENGTH OR REMOVE AND REPLACE THE STONE. CLEAN PAVED SURFACES OF TRACKED SEDIMENT.				
COMPOST FILTER SOCK	WEEKLY & WITHIN 24 HOURS OF RAINFALL > 0.25"	REPAIR/REPLACE WHEN FAILURE OR DETERIORATION IS OBSERVED.				
SILT FENCE	WEEKLY & WITHIN 24 HOURS OF RAINFALL > 0.25"	REPAIR/REPLACE WHEN FAILURE OR DETERIORATION IS OBSERVED. REMOVE SILT WHEN IT REACHES 1/2 THE HEIGHT OF THE FENCE.				
TOPSOIL/BORROW STOCKPILES	DAILY	REPAIR/REPLACE SEDIMENT BARRIERS AS NECESSARY.				
TEMPORARY SEDIMENT BASIN (W/ BAFFLES)	WEEKLY & WITHIN 24 HOURS OF RAINFALL > 0.5"	REMOVE SEDIMENT ONCE IT HAS ACCUMULATED TO ONE HALF OF MINIMUM REQUIRED VOLUME OF THE WET STORAGE, DEWATERING AS NEEDED. RESTORE TRAP TO ORIGINAL DIMENSIONS. REPAIR/REPLACE BAFFLES WHEN FAILURE OR DETERIORATION IS OBSERVED.				
TEMPORARY SEDIMENT TRAP (W/ BAFFLES)	WEEKLY & WITHIN 24 HOURS OF RAINFALL > 0.5"	REMOVE SEDIMENT ONCE IT HAS ACCUMULATED TO ONE HALF OF MINIMUM REQUIRED VOLUME OF THE WET STORAGE, DEWATERING AS NEEDED. RESTORE TRAP TO ORIGINAL DIMENSIONS. REPAIR/REPLACE BAFFLES WHEN FAILURE OR DETERIORATION IS OBSERVED.				
TEMPORARY SOIL PROTECTION	WEEKLY & WITHIN 24 HOURS OF RAINFALL > 0.25"	REPAIR ERODED OR BARE AREAS IMMEDIATELY. RESEED AND MULCH.				

#### SEDIMENT & EROSION CONTROL NARRATIVE

- 1. THE PROJECT INVOLVES THE CONSTRUCTION OF A GROUND MOUNTED SOLAR PANEL FACILITY WITH ASSOCIATED EQUIPMENT, INCLUDING THE CLEARING, GRUBBING AND GRADING OF APPROXIMATELY 16.49± ACRES OF EXISTING LOT.
- THE PROPOSED PROJECT INVOLVES THE FOLLOWING CONSTRUCTION:
- A. CLEARING AND GRUBBING WHERE NECESSARY.
- B. REMOVAL OF EXISTING ACCESS ROAD AND MATERIAL STOCKPILES AND GRADING OF EXISTING LOT.
- C. CONSTRUCTION OF 7,655 GROUND MOUNTED SOLAR PANELS AND ASSOCIATED EQUIPMENT. D. THE STABILIZATION OF DISTURBED AREAS WITH PERMANENT VEGETATIVE TREATMENTS.
- 2. FOR THIS PROJECT, THERE ARE APPROXIMATELY 16.49± ACRE OF THE SITE BEING DISTURBED WITH A NET DECREASE OF IMPERVIOUS AREA ON THE SITE. PROPOSED IMPERVIOUS AREAS CONSIST OF CONCRETE PADS FOR ELECTRICAL EQUIPMENT AND COMPACTED GRAVEL ACCESS ROADS.
- 3. THE PROJECT SITE, AS MAPPED IN THE SOIL SURVEY OF STATE OF CONNECTICUT (NRCS, VERSION 18, DEC 6, 2018), CONTAINS TYPE 60B AND 72C (HYDROLOGIC SOIL GROUP B), 50B AND 52C (HYDROLOGIC SOIL GROUP B/D), 45A AND 45B (HYDROLOGIC SOIL GROUP C/D) AND 2 AND 3 (HYDROLOGIC SOIL GROUP D) SOILS. A GEOTECHNICAL ENGINEERING REPORT HAS BEEN COMPLETED DATED 25 OCTOBER 2022.
- 4. IT IS ANTICIPATED THAT ARRAY CONSTRUCTION WILL BE COMPLETED IN APPROXIMATELY 4-6 MONTHS. IT IS ANTICIPATED THAT A PRELIMINARY PHASE OF SITE WORK WILL OCCUR PRIOR TO ARRAY CONSTRUCTION, TO RE-GRADE AND STABILIZE THE SITE, WHICH WILL BE COMPLETED IN APPROXIMATELY 2-3 MONTHS.
- 5. REFER TO THE CONSTRUCTION SEQUENCING AND EROSION AND SEDIMENTATION NOTES FOR INFORMATION REGARDING SEQUENCING OF MAJOR OPERATIONS IN THE ON-SITE CONSTRUCTION PHASES.
- 6. STORMWATER MANAGEMENT DESIGN CRITERIA UTILIZES THE APPLICABLE SECTIONS OF THE 2004 CONNECTICUT STORMWATER QUALITY MANUAL AND THE TOWN OF COLCHESTER STANDARDS, TO THE EXTENT POSSIBLE AND PRACTICABLE FOR THIS PROJECT ON THIS SITE. EROSION AND SEDIMENTATION MEASURES ARE BASED UPON ENGINEERING PRACTICE, JUDGEMENT AND THE APPLICABLE SECTIONS OF THE CONNECTICUT EROSION AND SEDIMENT CONTROL GUIDELINES FOR URBAN AND SUBURBAN AREAS, LATEST EDITION.
- 7. DETAILS FOR THE TYPICAL STORMWATER MANAGEMENT AND EROSION AND SEDIMENTATION MEASURES ARE SHOWN ON THE PLAN SHEETS OR PROVIDED AS SEPARATE SUPPORT DOCUMENTATION FOR REVIEW IN THIS PLAN.
- 8. CONSERVATION PRACTICES TO BE USED DURING CONSTRUCTION:
- B. STAGED CONSTRUCTION; C. MINIMIZE THE DISTURBED AREAS TO THE EXTENT PRACTICABLE DURING CONSTRUCTION;
- D. STABILIZE DISTURBED AREAS WITH TEMPORARY OR PERMANENT MEASURES AS SOON AS POSSIBLE, BUT NO LATER THAN 7-DAYS FOLLOWING DISTURBANCE; E. MINIMIZE IMPERVIOUS AREAS;
- F. UTILIZE APPROPRIATE CONSTRUCTION EROSION AND SEDIMENTATION MEASURES.
- 9. THE FOLLOWING SEPARATE DOCUMENTS ARE TO BE CONSIDERED A PART OF THE EROSION AND SEDIMENTATION PLAN:
- A. STORMWATER MANAGEMENT REPORT DATED FEBRUARY 2023.

#### SUGGESTED CONSTRUCTION SEQUENCE

B. SWPCP, TO BE ISSUED.

THE FOLLOWING SUGGESTED SEQUENCE OF CONSTRUCTION ACTIVITIES IS PROJECTED BASED UPON ENGINEERING JUDGEMENT AND BEST MANAGEMENT PRACTICES. THE CONTRACTOR MAY ELECT TO ALTER THE SEQUENCING TO BEST MEET THE CONSTRUCTION SCHEDULE, THE EXISTING SITE ACTIVITIES AND WEATHER CONDITIONS. SHOULD THE CONTRACTOR ALTER THE CONSTRUCTION SEQUENCE OR ANY EROSION AND SEDIMENTATION CONTROL MEASURES THEY SHALL MODIFY THE STORMWATER POLLUTION CONTROL PLAN ("SWPCP") AS REQUIRED BY THE GENERAL PERMIT. MAJOR CHANGES IN SEQUENCING AND/OR METHODS MAY REQUIRE REGULATORY APPROVAL PRIOR TO IMPLEMENTATION.

- 1. THE CONTRACTOR SHALL SCHEDULE A PRE-CONSTRUCTION MEETING. PHYSICALLY FLAG THE LIMITS OF DISTURBANCE IN THE FIELD AS NECESSARY TO FACILITATE THE PRE-CONSTRUCTION MEETING.
- 2. CONDUCT A PRE-CONSTRUCTION MEETING TO DISCUSS THE PROPOSED WORK AND EROSION AND SEDIMENTATION CONTROL MEASURES. THE MEETING SHOULD BE ATTENDED BY THE OWNER. THE OWNER'S REPRESENTATIVE(S), THE GENERAL CONTRACTOR, DESIGNATED SUB-CONTRACTORS AND THE PERSON, OR PERSONS, RESPONSIBLE FOR THE IMPLEMENTATION, OPERATION, MONITORING AND MAINTENANCE OF THE EROSION AND SEDIMENTATION MEASURES. THE CONSTRUCTION PROCEDURES FOR THE ENTIRE PROJECT SHALL BE REVIEWED AT THIS MEETING.
- 3. NOTIFY CALL BEFORE YOU DIG AT 811, AS REQUIRED, PRIOR TO THE START OF CONSTRUCTION.

## PHASE 1

- 4. REMOVE EXISTING IMPEDIMENTS AS NECESSARY AND PROVIDE MINIMAL CLEARING AND GRUBBING TO INSTALL THE REQUIRED CONSTRUCTION ENTRANCE/S.
- 5. CLEAR ONLY AS NEEDED TO INSTALL THE PERIMETER EROSION AND SEDIMENTATION CONTROL MEASURES AND, IF APPLICABLE, TREE PROTECTION. ALL WETLAND AREAS SHALL BE PROTECTED BEFORE MAJOR CONSTRUCTION BEGINS.
- 6. INSTALL PERIMETER EROSION CONTROL.
- 7. INSTALL TEMPORARY SEDIMENT TRAPS 1-4 (TST-1, TST-2, TST-3 & TST-4), AND ASSOCIATED OVERFLOW WEIRS, STOCKPILE AREAS AND SEDIMENT TRAP BAFFLES. UPON COMPLETION OF THE INSTALLATION AND STABILIZATION OF THE SEDIMENT TRAPS AND SWALES. PHASE 2 WORK UP GRADIENT CAN PROCEED.

## PHASE 2

- 8. UPON COMPLETION OF THE INSTALLATION OF EACH OF THE TEMPORARY SEDIMENT BASINS; THE AREA ABOVE THE BASIN CAN HAVE THE REMAINING ARRAY AREA CLEARING AND GRUBBING COMPLETED AS REQUIRED. REMOVE CUT WOOD AND STOCKPILE FOR FUTURE USE OR REMOVE OFF-SITE. REMOVE AND DISPOSE OF DEMOLITION DEBRIS OFF-SITE IN ACCORDANCE WITH APPLICABLE LAWS.
- 9. INSTALL NEW ACCESS ROADS IF SITE CONDITIONS ALLOW.
- 10. TEMPORARILY SEED DISTURBED AREAS NOT UNDER CONSTRUCTION FOR THIRTY (30) DAYS OR MORE.
- 11. FINISH GRADE AREA WITHIN ARRAY FOOTPRINT, PROVIDE SOIL AMENDMENT AND SEEDING MIX AS DETAILED IN PLANS AND DETAILS, INSTALL INTERIOR FILTER SOCK.
- 12. INSTALL ELECTRICAL CONDUIT, EQUIPMENT PADS, INVERTERS, AND SWITCHGEAR WHILE STABILIZATION OCCURS IN THE ARRAY FOOTPRINT
- 13. REMOVE INTERIOR COMPOST FILTER SOCKS WITH APPROVAL OF SWPCP MONITOR AND CONSERVATION DISTRICT.
- 14. INSTALL RACKING POSTS FOR GROUND MOUNTED SOLAR PANELS.
- 15. INSTALL GROUND MOUNTED SOLAR PANELS AND COMPLETE ELECTRICAL INSTALLATION.
- 16. AFTER SUBSTANTIAL COMPLETION OF THE INSTALLATION OF THE SOLAR PANELS, COMPLETE REMAINING SITE WORK, INCLUDING ANY REQUIRED LANDSCAPE SCREENING, AND STABILIZE ALL DISTURBED AREAS.
- 17. FINE GRADE, RAKE, SEED AND MULCH ALL REMAINING DISTURBED AREAS.

## FINAL GRADING & DRAINAGE PLAN

- 18. AFTER THE SITE IS STABILIZED AND WITH THE APPROVAL OF THE PERMITTEE AND CONSERVATION DISTRICT AGENT, REMOVE TEMPORARY SEDIMENT TRAPS 1-4 (TST-1, TST-2, TST-3 & TST-4), AS WELL AS ASSOCIATED OVERFLOW WEIRS, SEDIMENT TRAP BAFFLES AND ANY PERIMETER EROSION AND SEDIMENTATION CONTROLS. ANY AREAS DISTURBED DURING CLEAN UP SHALL BE PERMANENTLY SEEDED.
- 19. THE SITE SHALL BE MONITORED ONCE A MONTH FOR TWO FULL GROWING SEASONS (APRIL OCTOBER).
- 20. ISSUE NOTICE OF TERMINATION UPON COMPLETION OF MONITORING REQUIRED PER APPENDIX I.

#### 524 NLR LLC

9 NOVELTY LANE. UNIT 9B **ESSEX, CT 06426** 



567 VAUXHALL STREET EXTENSION - SUITE 311 WATERFORD, CT 06385 PHONE: (860)-663-169 WWW.ALLPOINTSTECH.COM FAX: (860)-663-093

#### CSC PERMIT SET

## NO DATE REVISION

- 0 | 03/07/23 | FOR FILING: KAM
- 1 06/15/23 FOR FILING: RCB 2 09/01/23 FENCE REVISIONS: RCB
- 3 | 09/08/23 | FENCE REVISIONS: RCB
- 4 09/28/23 ADD EX. POLE CALOUTS: RCE
- 5 | 10/20/23 | ADD LOD EXHIBIT DWG: RCB
- 6 04/15/24 REVISED SEED MIX: RCB
- 7 05/03/24 REVISED SITE LAYOUT: UKA
- 8 | 05/16/24 | REVISED PER CLIENT :TEL
- 9 06/11/24 REVISED PER CLIENT :TEL 10 | 06/21/24 | REVISED PER CLIENT :TEL

#### **DESIGN PROFESSIONAL OF RECORD**

PROF: ROBERT C. BURNS, P.E. **COMP: ALL-POINTS TECHNOLOGY** CORPORATION, P.C. ADD: 567 VAUXHALL STREET **EXTENSION - SUITE 311** WATERFORD, CT 06385

OWNER: FIVE J, LLC

ADDRESS: 524 NEW LONDON ROAD

COLCHESTER, CT

**SCRAPYARD SOLAR** 

SITE 524 NEW LONDON ROAD **ADDRESS: COLCHESTER, CT** 

**APT FILING NUMBER: CT580160** 

DATE: 03/07/23 | CHECKED BY: RCB

SHEET TITLE:


SEDIMENTATION & **EROSION CONTROL NOTES** 

SHEET NUMBER:







DRAWN BY: ELZ

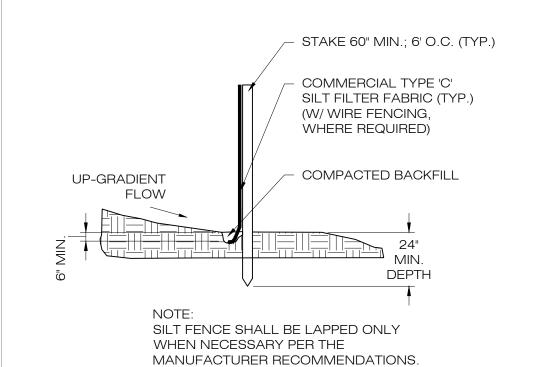

1 SILT FENCE DETAIL
EC-2 SCALE: N.T.S.

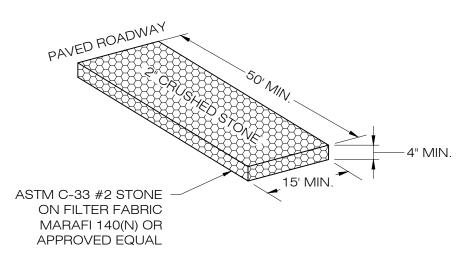



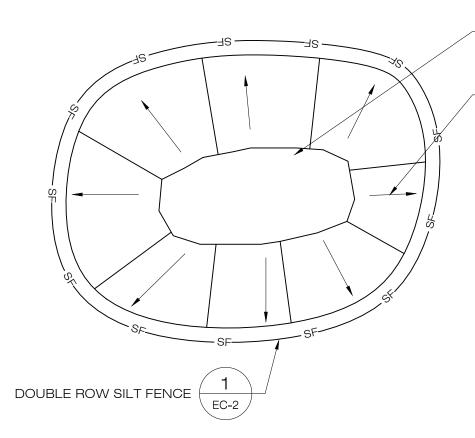

SOIL/AGGREGATE STOCKPILE OF EXISTING SITE MATERIAL TO BE REUSED AND/OR NEW MATERIAL TO BE INSTALLED IN THE WORK

DIRECTION OF RUN-OFF FLOW (TYP.)


1. ALL EXISTING EXCAVATED MATERIAL THAT IS NOT TO BE REUSED IN THE WORK IS TO BE IMMEDIATELY REMOVED FROM THE SITE AND PROPERLY DISPOSED OF.

2. SOIL/AGGREGATE STOCKPILE SITES TO BE WHERE SHOWN ON THE DRAWINGS.

3. RESTORE STOCKPILE SITES TO PRE-EXISTING PROJECT CONDITION AND RESEED AS REQUIRED.

4. STOCKPILE HEIGHTS MUST NOT EXCEED 35'. STOCKPILE SLOPES MUST BE 2:1 OR FLATTER.

# 3 MATERIALS STOCKPILE DETAIL SCALE: N.T.S.

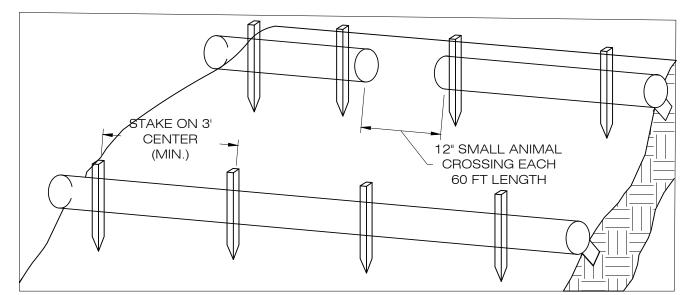



1. BEGIN AT THE LOCATION WHERE THE SOCK IS TO BE INSTALLED BY EXCAVATING A 2-3" (5-7.5 CM) DEEP X 9" (22.9 CM) WIDE TRENCH ALONG THE CONTOUR OF THE SLOPE. EXCAVATED SOIL

SHOULD BE PLACED UP SLOPE FROM THE ANCHOR TRENCH. 2. PLACE THE SOCK IN THE TRENCH SO THAT IT CONTOURS TO THE SOIL SURFACE. COMPACT SOIL FROM THE EXCAVATED TRENCH AGAINST THE SOCK ON THE UPHILL SIDE. SOCKS SHALL BE INSTALLED IN 60 FT CONTINUOUS LENGTHS WITH ADJACENT SOCKS TIGHTLY ABUT. EVERY 60 FT THE SOCK ROW SHALL BE SPACED 12 INCHES CLEAR, END TO END, FOR AMPHIBIAN AND REPTILE TRAVEL. THE OPEN SPACES SHALL BE STAGGERED MID LENGTH OF THE NEXT DOWN GRADIENT SOCK.

3. SECURE THE SOCK WITH 18-24" (45.7-61 CM) STAKES EVERY 3-4' (0.9 -1.2 M) AND WITH A STAKE ON EACH END. STAKES SHOULD BE DRIVEN THROUGH THE MIDDLE OF THE SOCK LEAVING AT LEAST 2-3" (5-7.5 CM) OF STAKE EXTENDING ABOVE THE SOCK. STAKES SHOULD BE DRIVEN PERPENDICULAR TO THE SLOPE FACE.

## COMPOST FILTER SOCK SEDIMENTATION CONTROL BARRIER EC-2 SCALE : N.T.S.

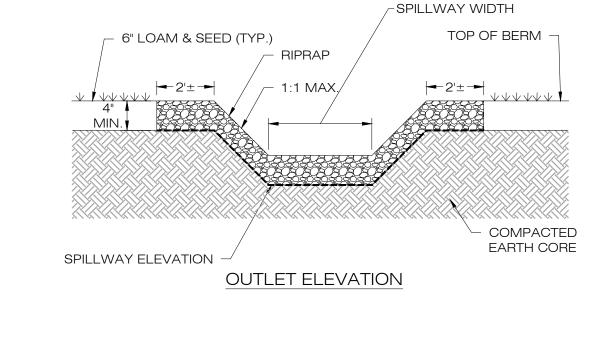

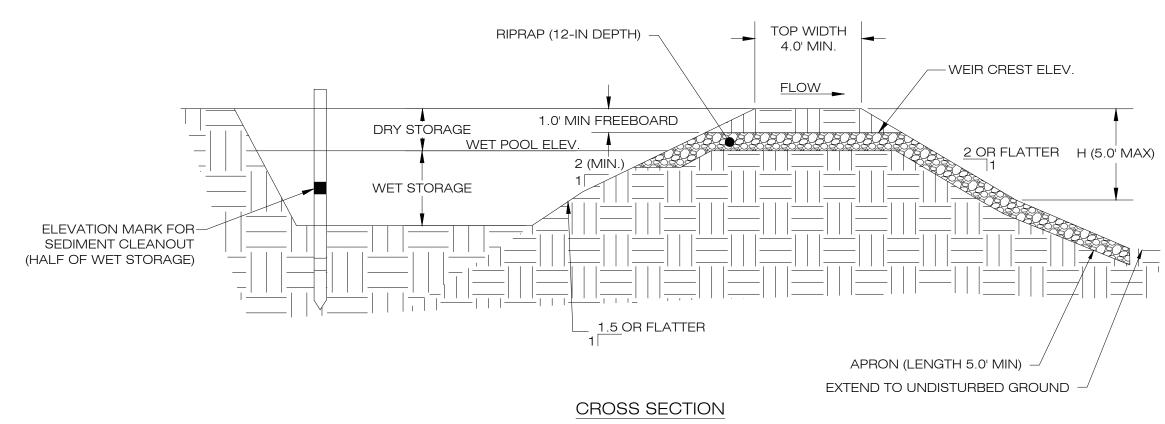


	TEMPORARY SEDIMENT TRAP SIZING TABLE									
NAME	DRAINAGE AREA (AC)	SEDIMENT VOLUME/ACRE AREA (CY)	REQ. VOLUME (CY)	REQ. WET VOLUME (CY)	PROP. BTM. ELEV. (FT)	PROP. PERVIOUS STONE BTM ELEV. (FT)	PROP. WEIR CREST ELEV. (FT)	PROP. TOP ELEV. (FT)	WET VOL. PROVIDED (CY)	TOTAL VOL. PROVIDED. (CY)
TST-1	4.94 AC	134 CYD	661.94 CY	330.97 CY	513.0'	514.5'	515.5'	517.0'	435.6 CY	1,400.7 CY
TST-2	4.93 AC	134 CYD	660.87 CY	330.44 CY	511.0'	512.5'	513.5'	515.0'	416.8 CY	1,328.3 CY
TST-3	4.80 AC	134 CYD	642.97 CY	321.48 CY	509.0'	510.5'	511.5'	513.0'	414.2 CY	1,345.9 CY
TST-4	4.56 AC	134 CYD	610.39 CY	305.19 CY	510.0'	511.5'	512.5'	514.0'	382.8 CY	1,251.7 CY

#### SEED MIX TO BE NEWP NEW ENGLAND EROSION CONTROL/ RESTORATION MIX FOR DETENTION BASINS AND MOIST SITES.

#### New England Erosion Control/Restoration Mix For Detention Basins and Moist Sites **Botanical Name** New England Erosion Control/Restoration Mix For Detention Basins and Moist Sites **Botanical Name** Indicator Common Name Riverbank Wild Rye **FACW FACU** Little Bluestem FACU Red Fescue Big Bluestem Switch Grass FAC New York Ironweed FACW+ **Upland Bentgrass** FACU Beggar Ticks **FACW**



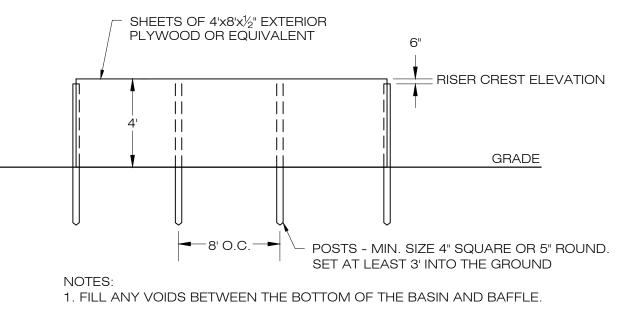

SEDIMENT TRAP BAFFLE EC-2 SCALE : N.T.S.

# TEMPORARY SEDIMENT TRAP

### 524 NLR LLC

9 NOVELTY LANE, UNIT 9B **ESSEX, CT 06426** 



567 VAUXHALL STREET EXTENSION - SUITE 311 WATERFORD, CT 06385 PHONE: (860)-663-1697 WWW.ALLPOINTSTECH.COM FAX: (860)-663-0935

### **CSC PERMIT SET**

# NO DATE REVISION

- 0 03/07/23 FOR FILING: KAM 1 | 06/15/23 | FOR FILING: RCB
- 2 09/01/23 FENCE REVISIONS: RCB
- 3 09/08/23 FENCE REVISIONS: RCB
- 4 09/28/23 ADD EX. POLE CALOUTS: RCE 5 10/20/23 ADD LOD EXHIBIT DWG: RCB
- 6 04/15/24 REVISED SEED MIX: RCB
- 7 05/03/24 REVISED SITE LAYOUT: UKA
- 8 05/16/24 REVISED PER CLIENT :TEL
- 9 06/11/24 REVISED PER CLIENT :TEL
- 10 06/21/24 REVISED PER CLIENT :TEL

### DESIGN PROFESSIONAL OF RECORD

PROF: ROBERT C. BURNS, P.E. **COMP: ALL-POINTS TECHNOLOGY** CORPORATION, P.C. ADD: 567 VAUXHALL STREET **EXTENSION - SUITE 311** WATERFORD, CT 06385

OWNER: FIVE J, LLC ADDRESS: 524 NEW LONDON ROAD COLCHESTER, CT

**SCRAPYARD SOLAR** 

SITE 524 NEW LONDON ROAD ADDRESS: COLCHESTER, CT

APT FILING NUMBER: CT580160

DRAWN BY: ELZ


DATE: 03/07/23 | CHECKED BY: RCB


SHEET TITLE:


**SEDIMENTATION & EROSION CONTROL DETAILS** 


**SHEET NUMBER:** 




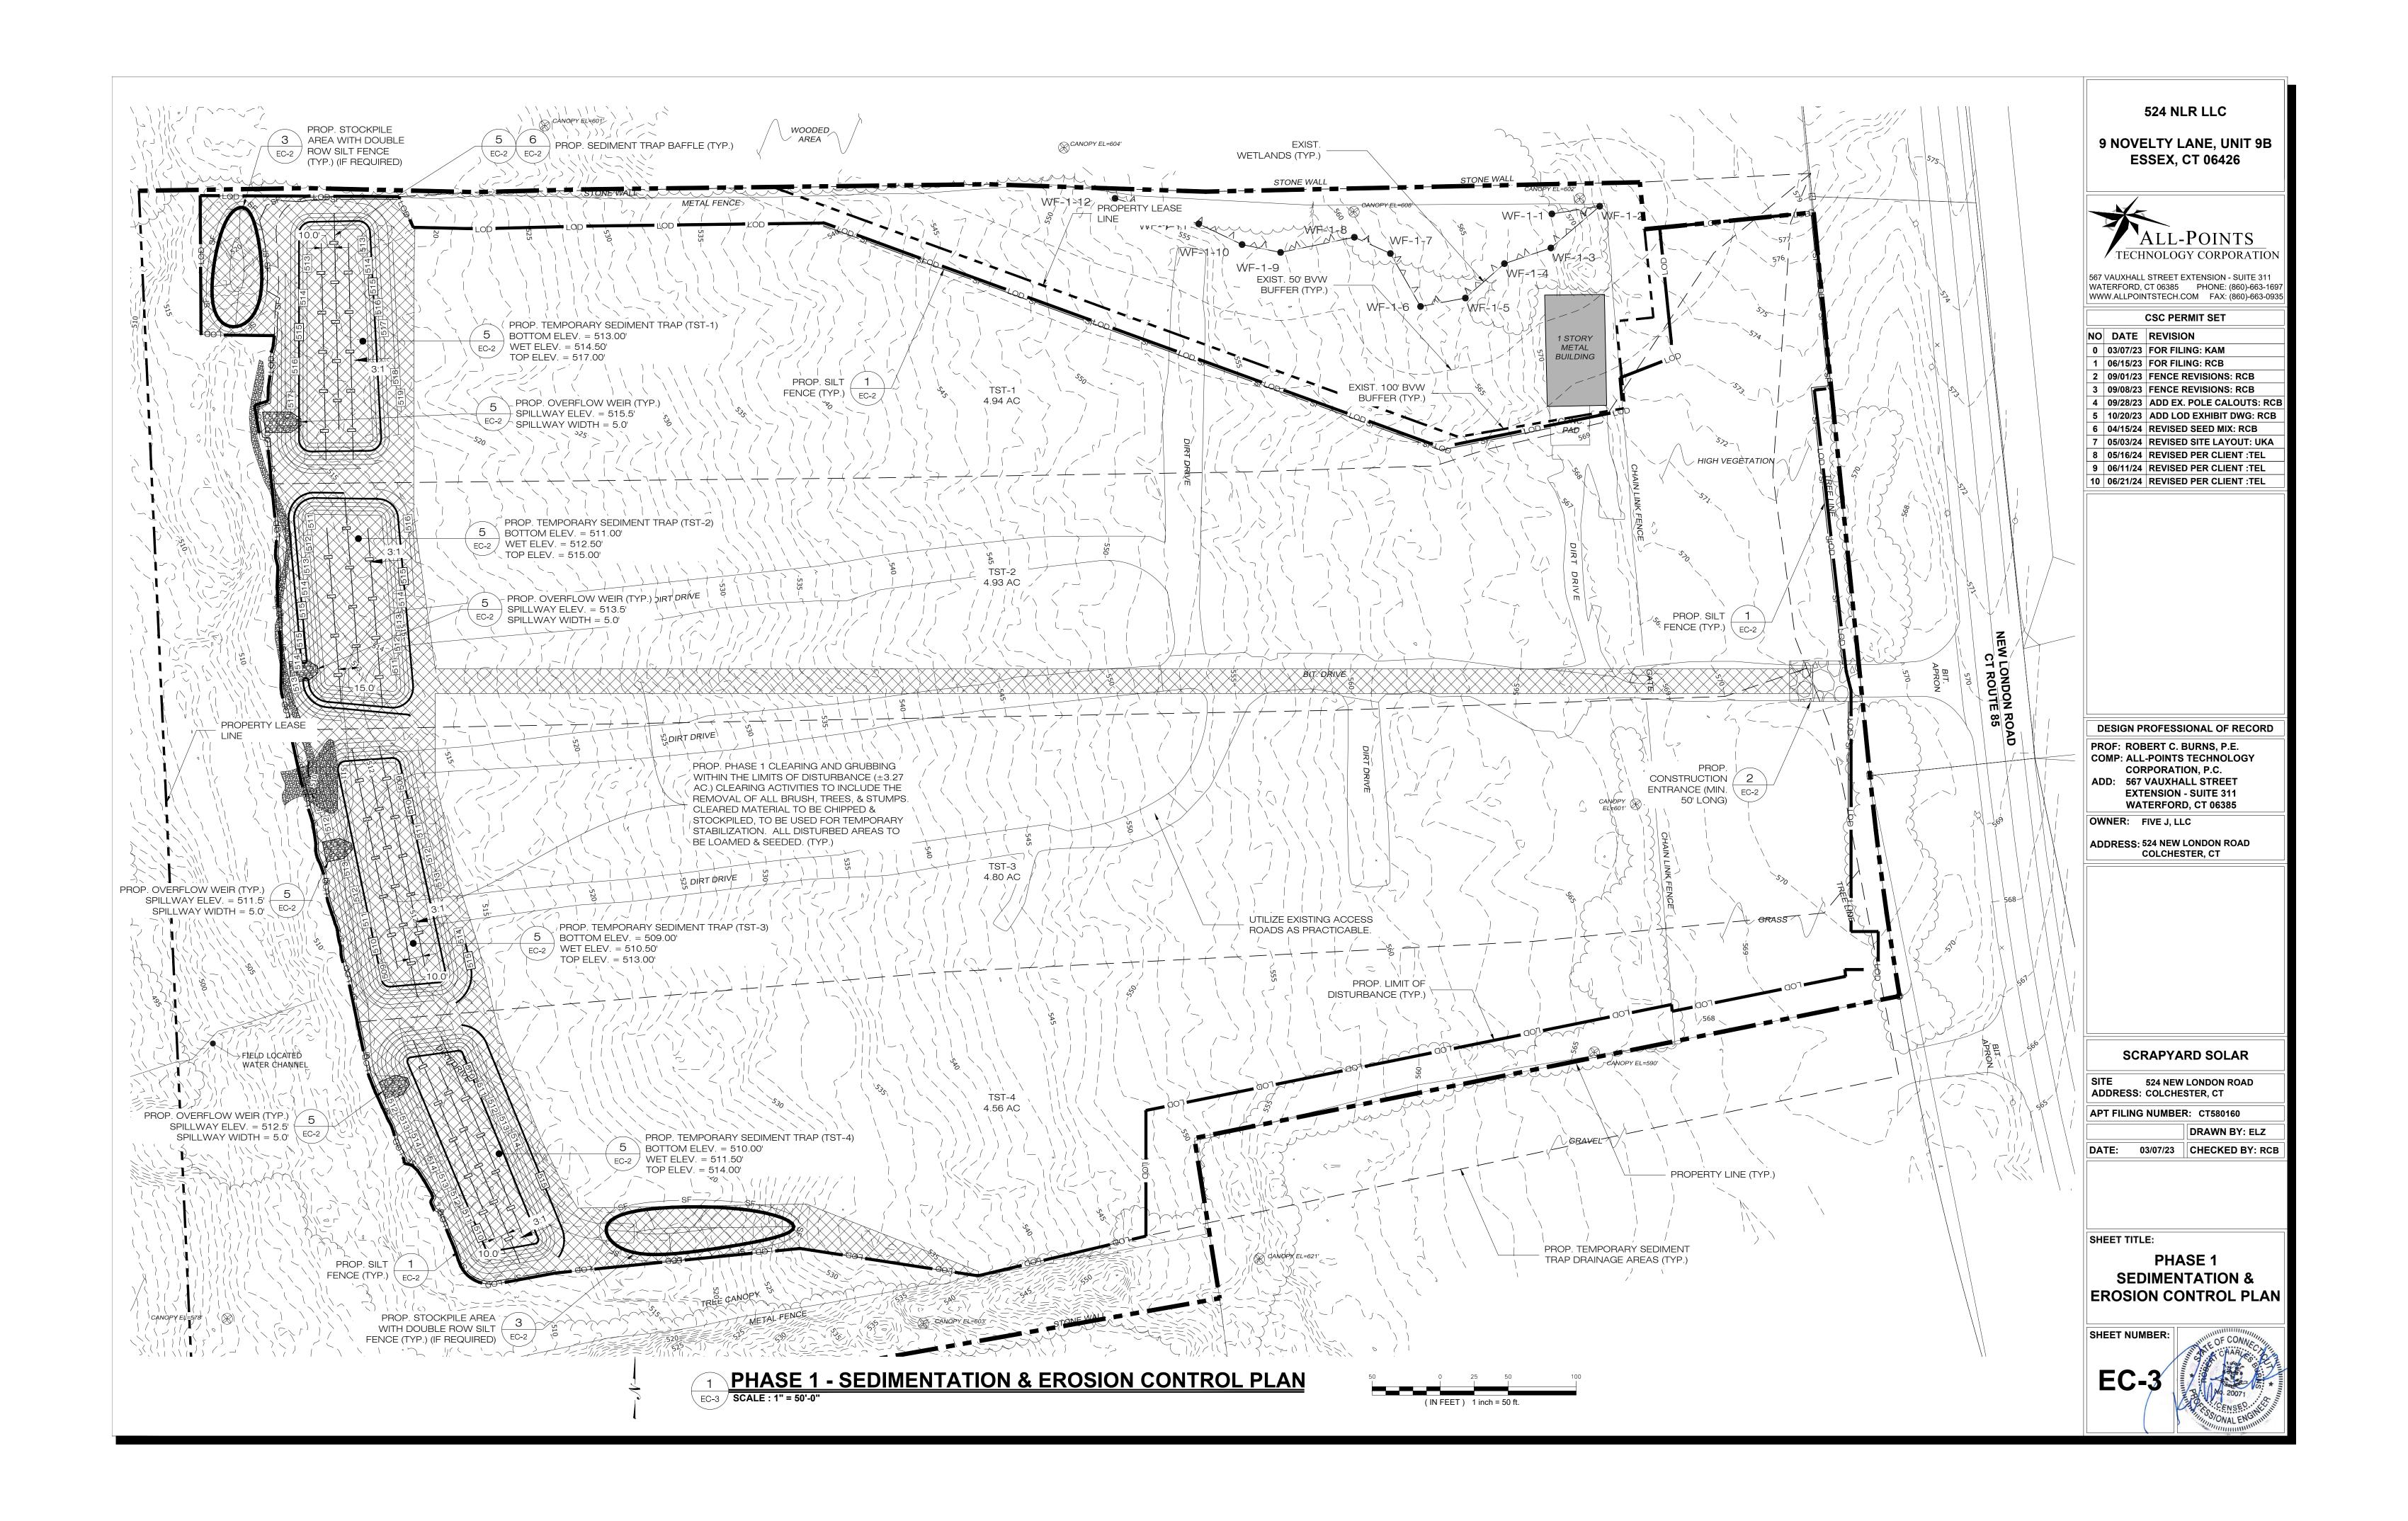


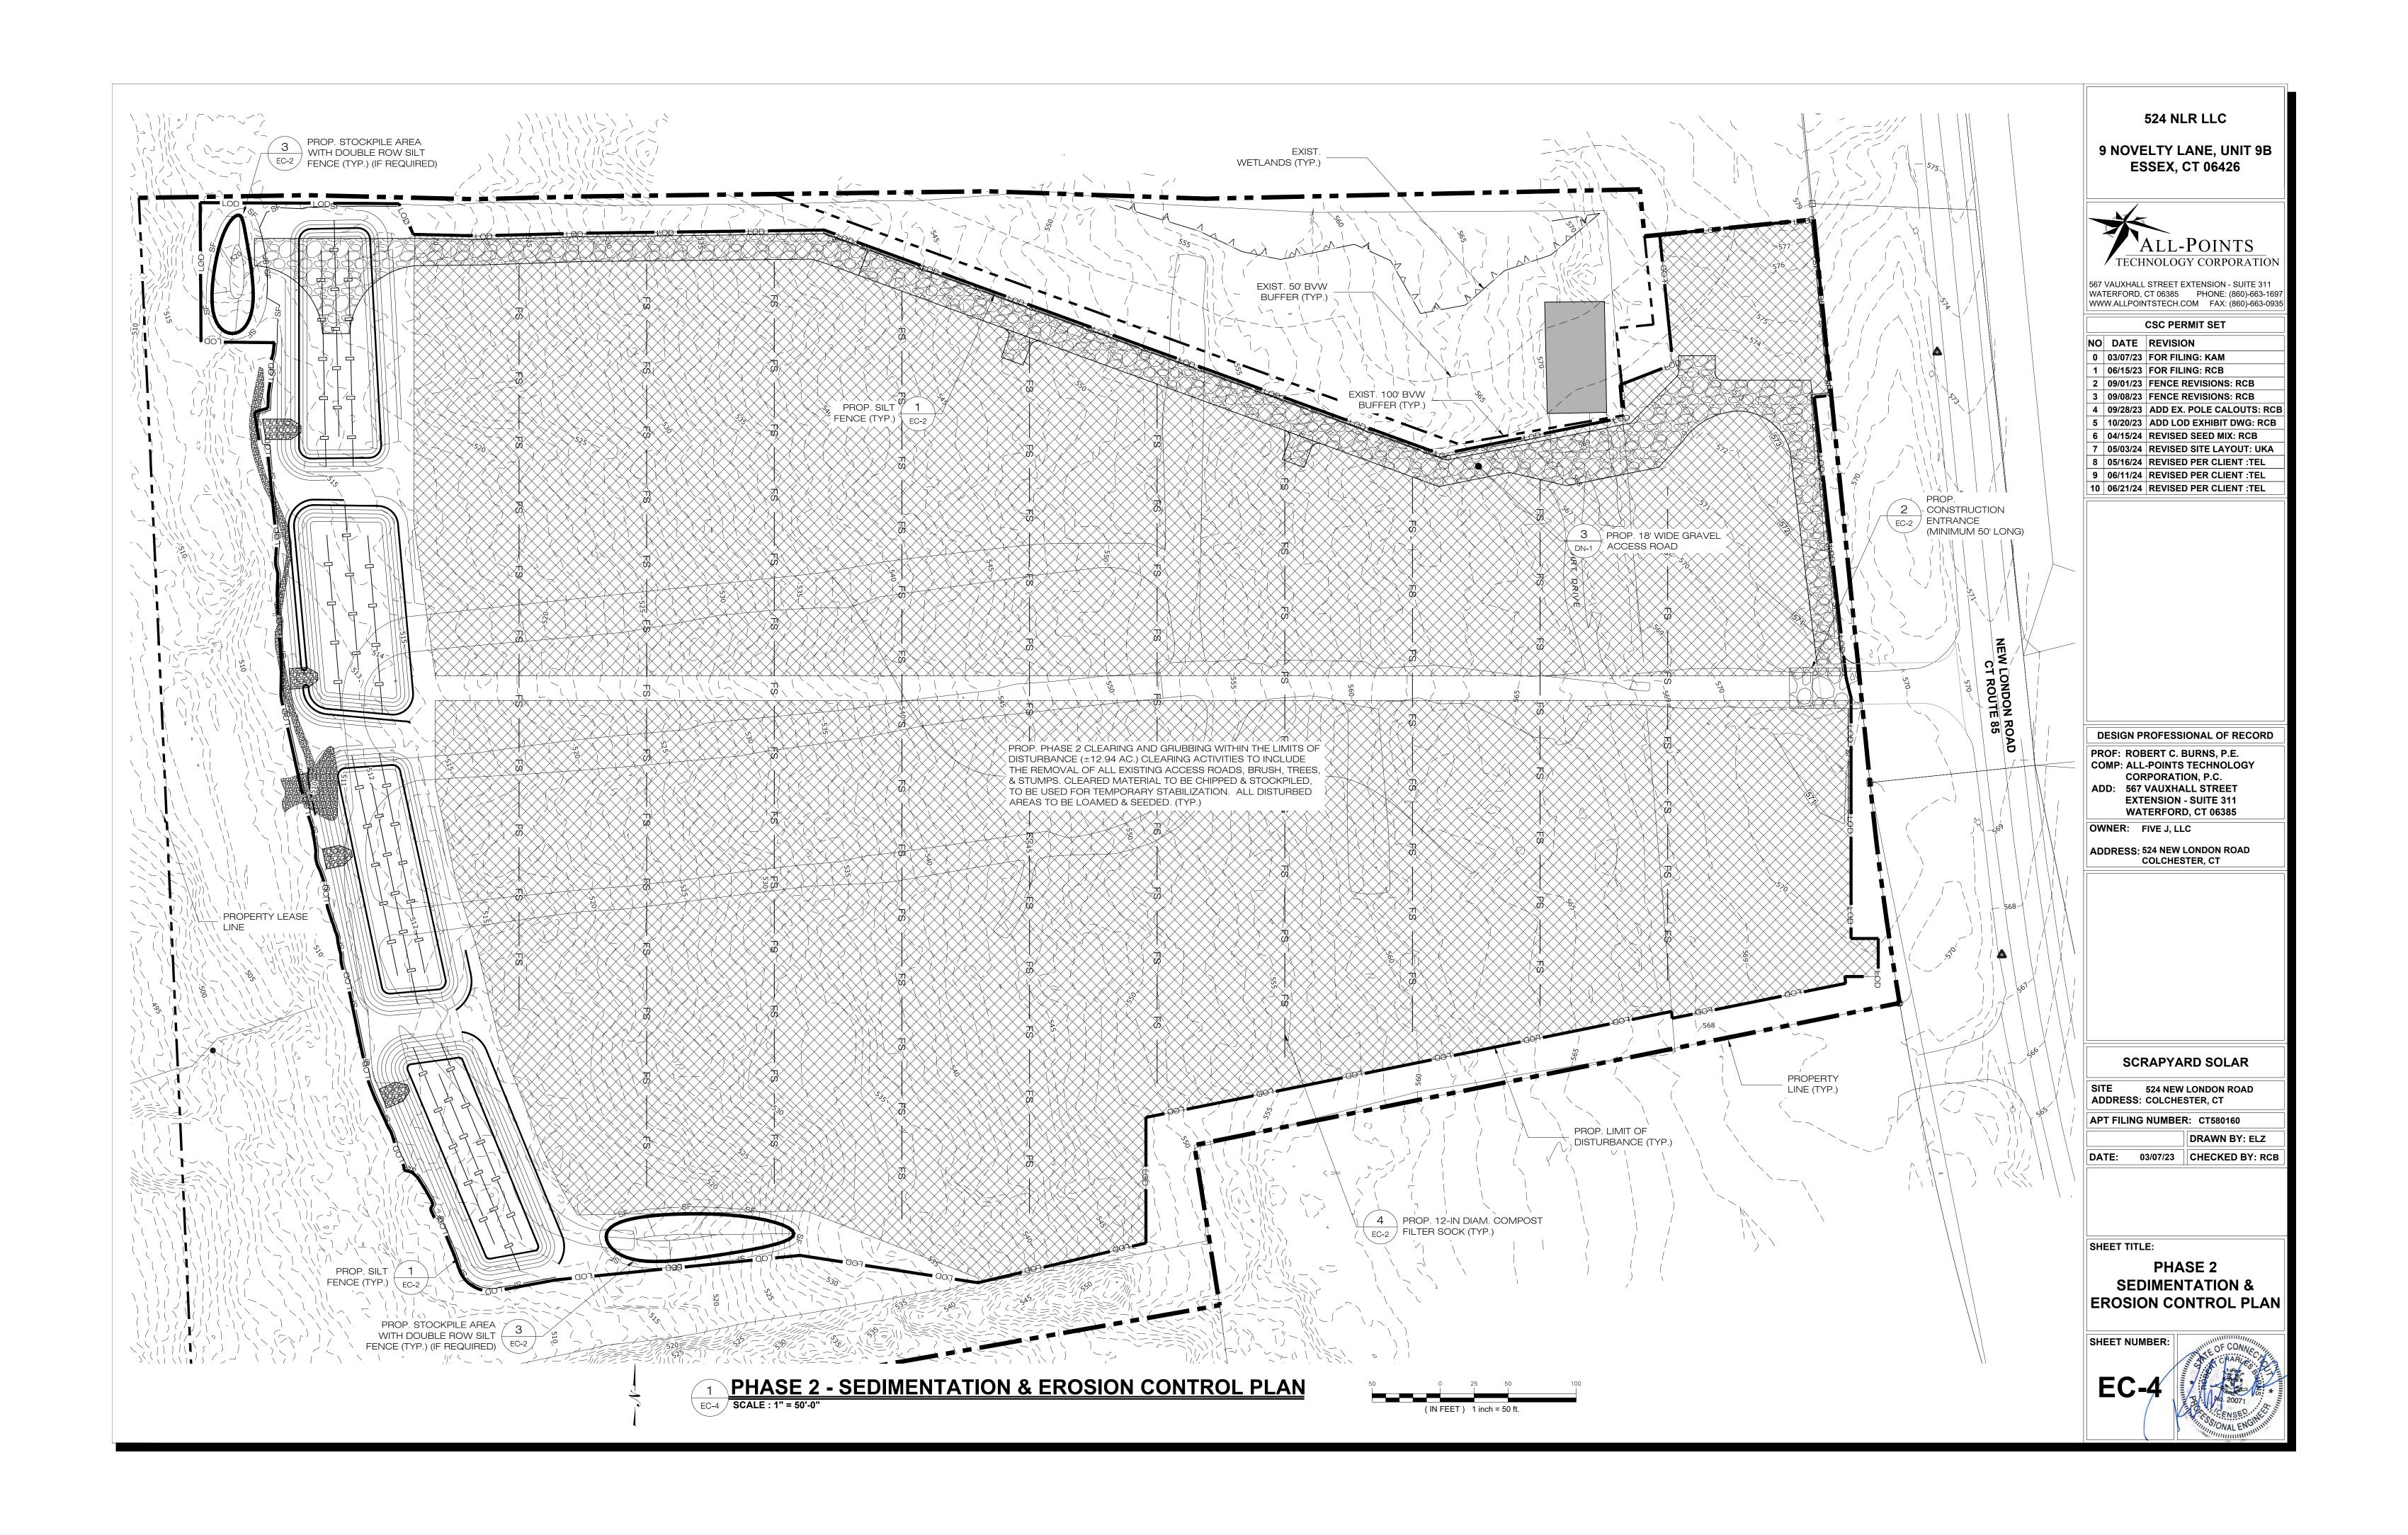

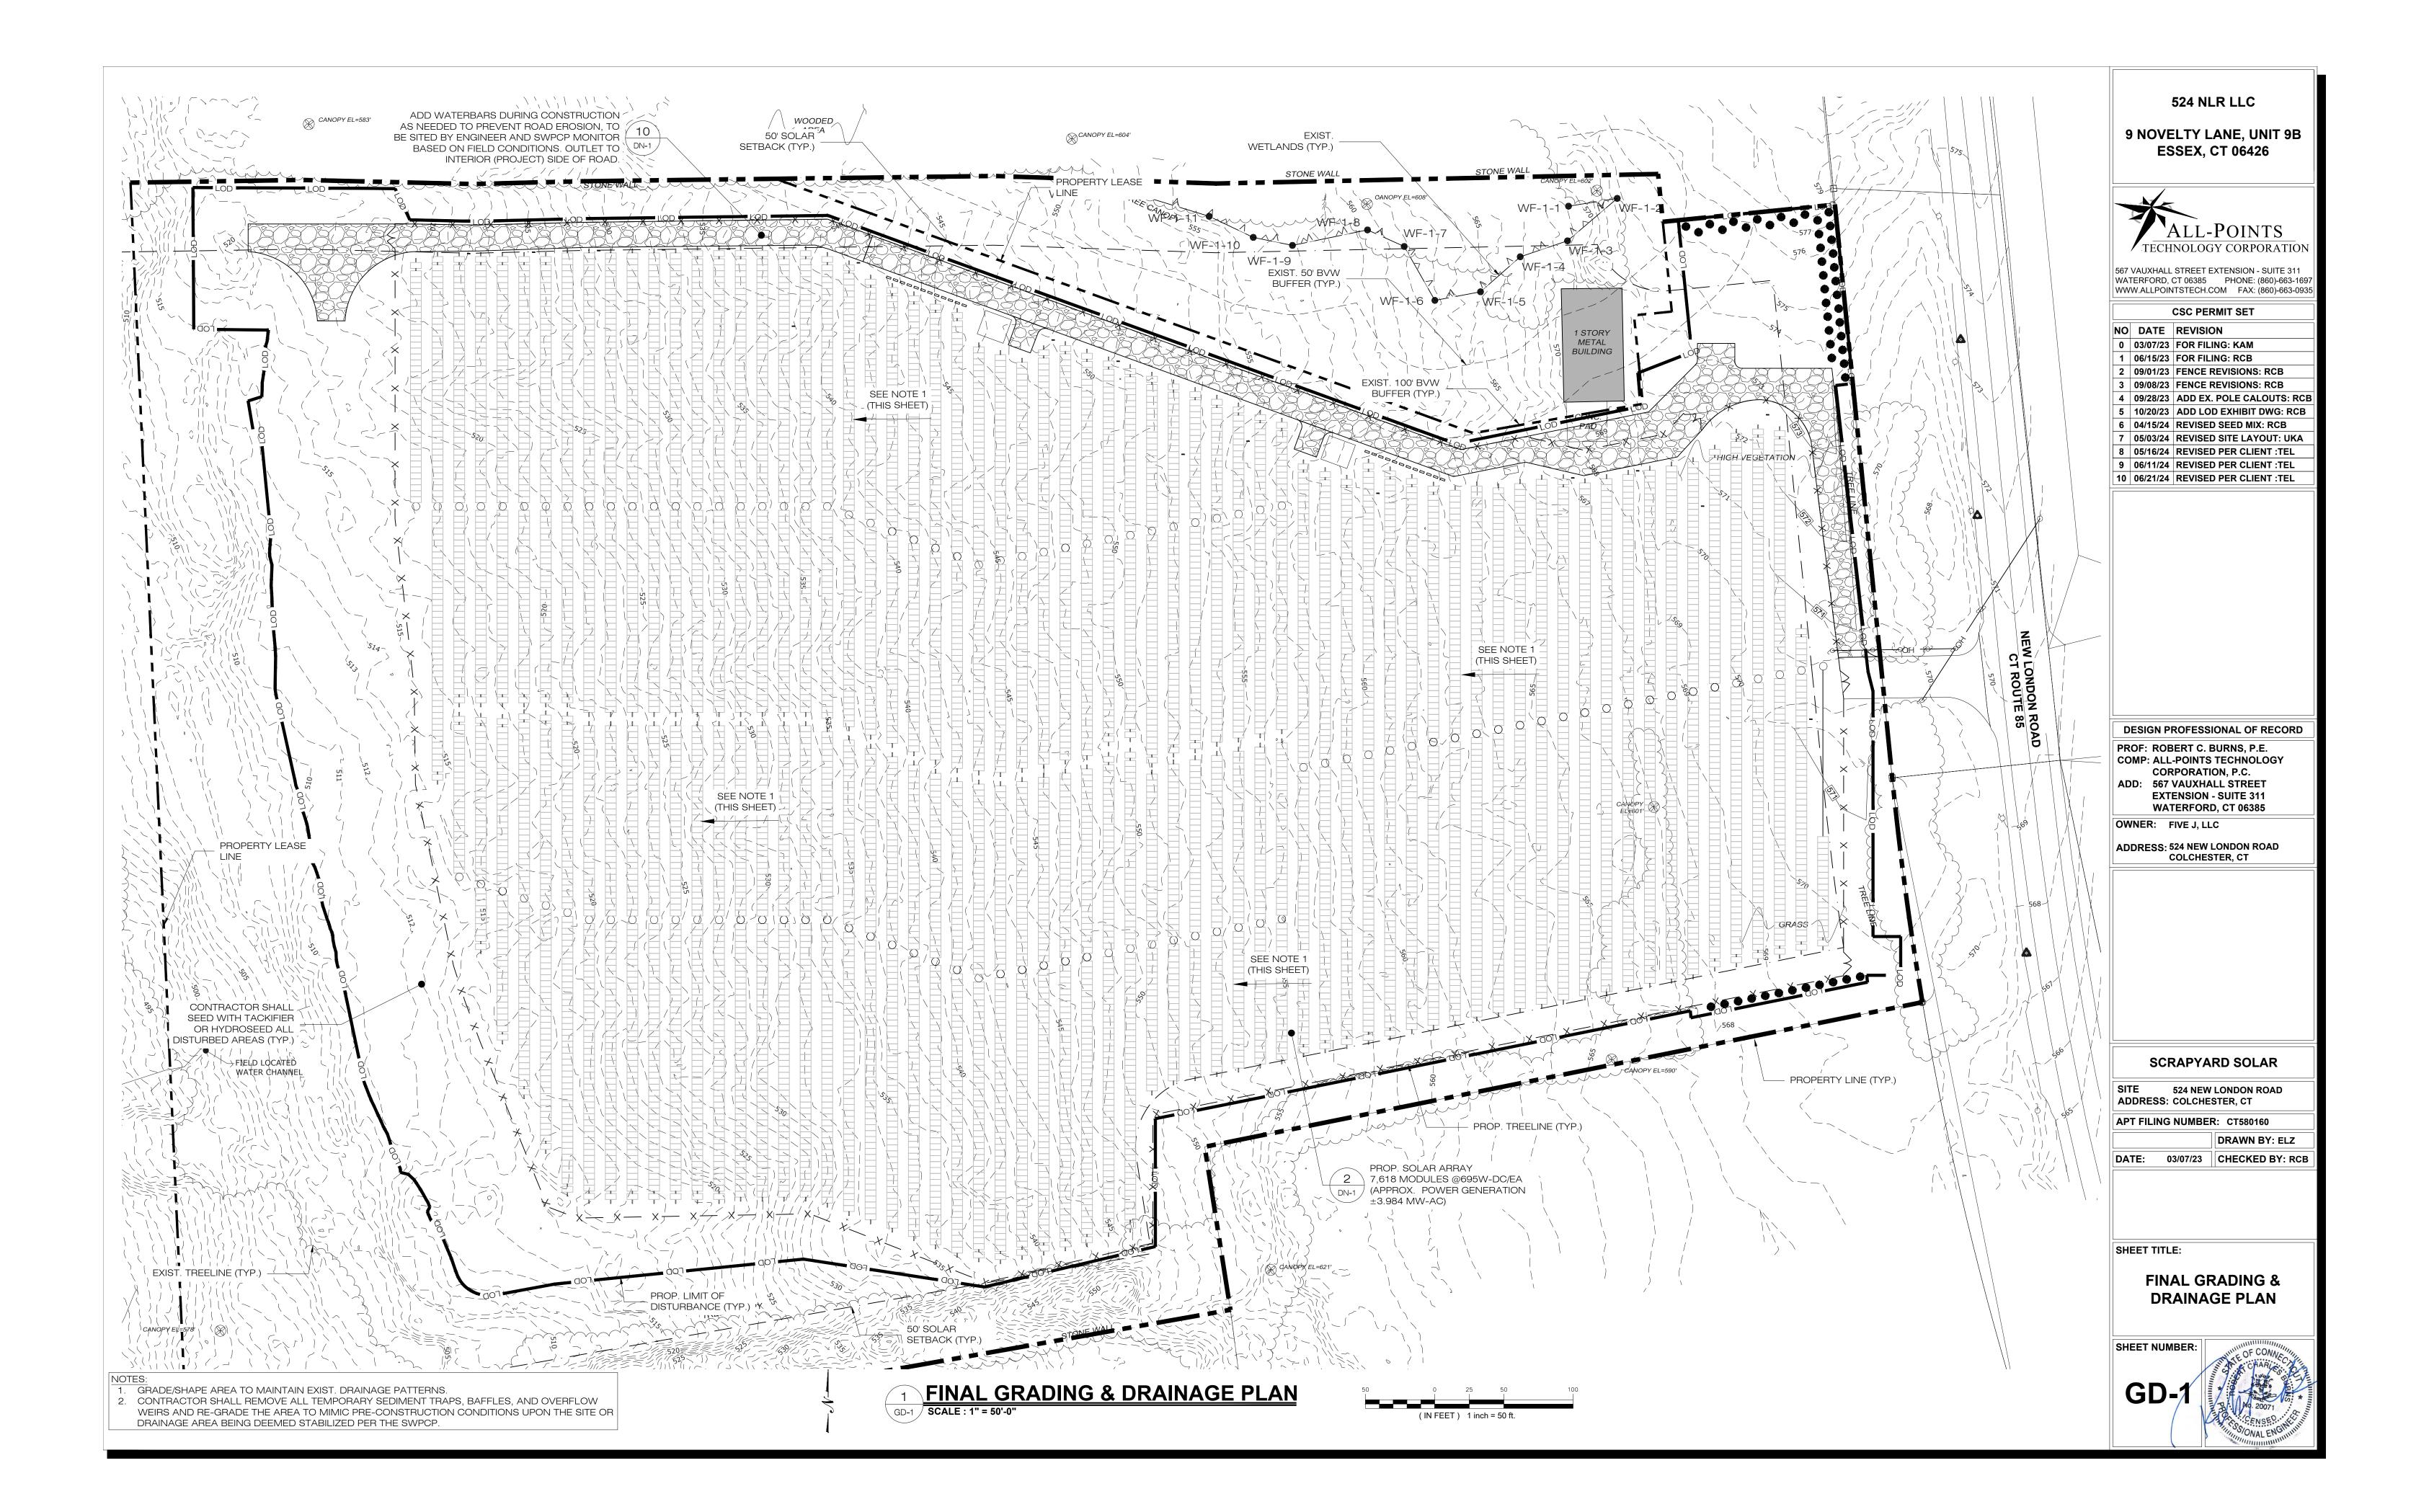

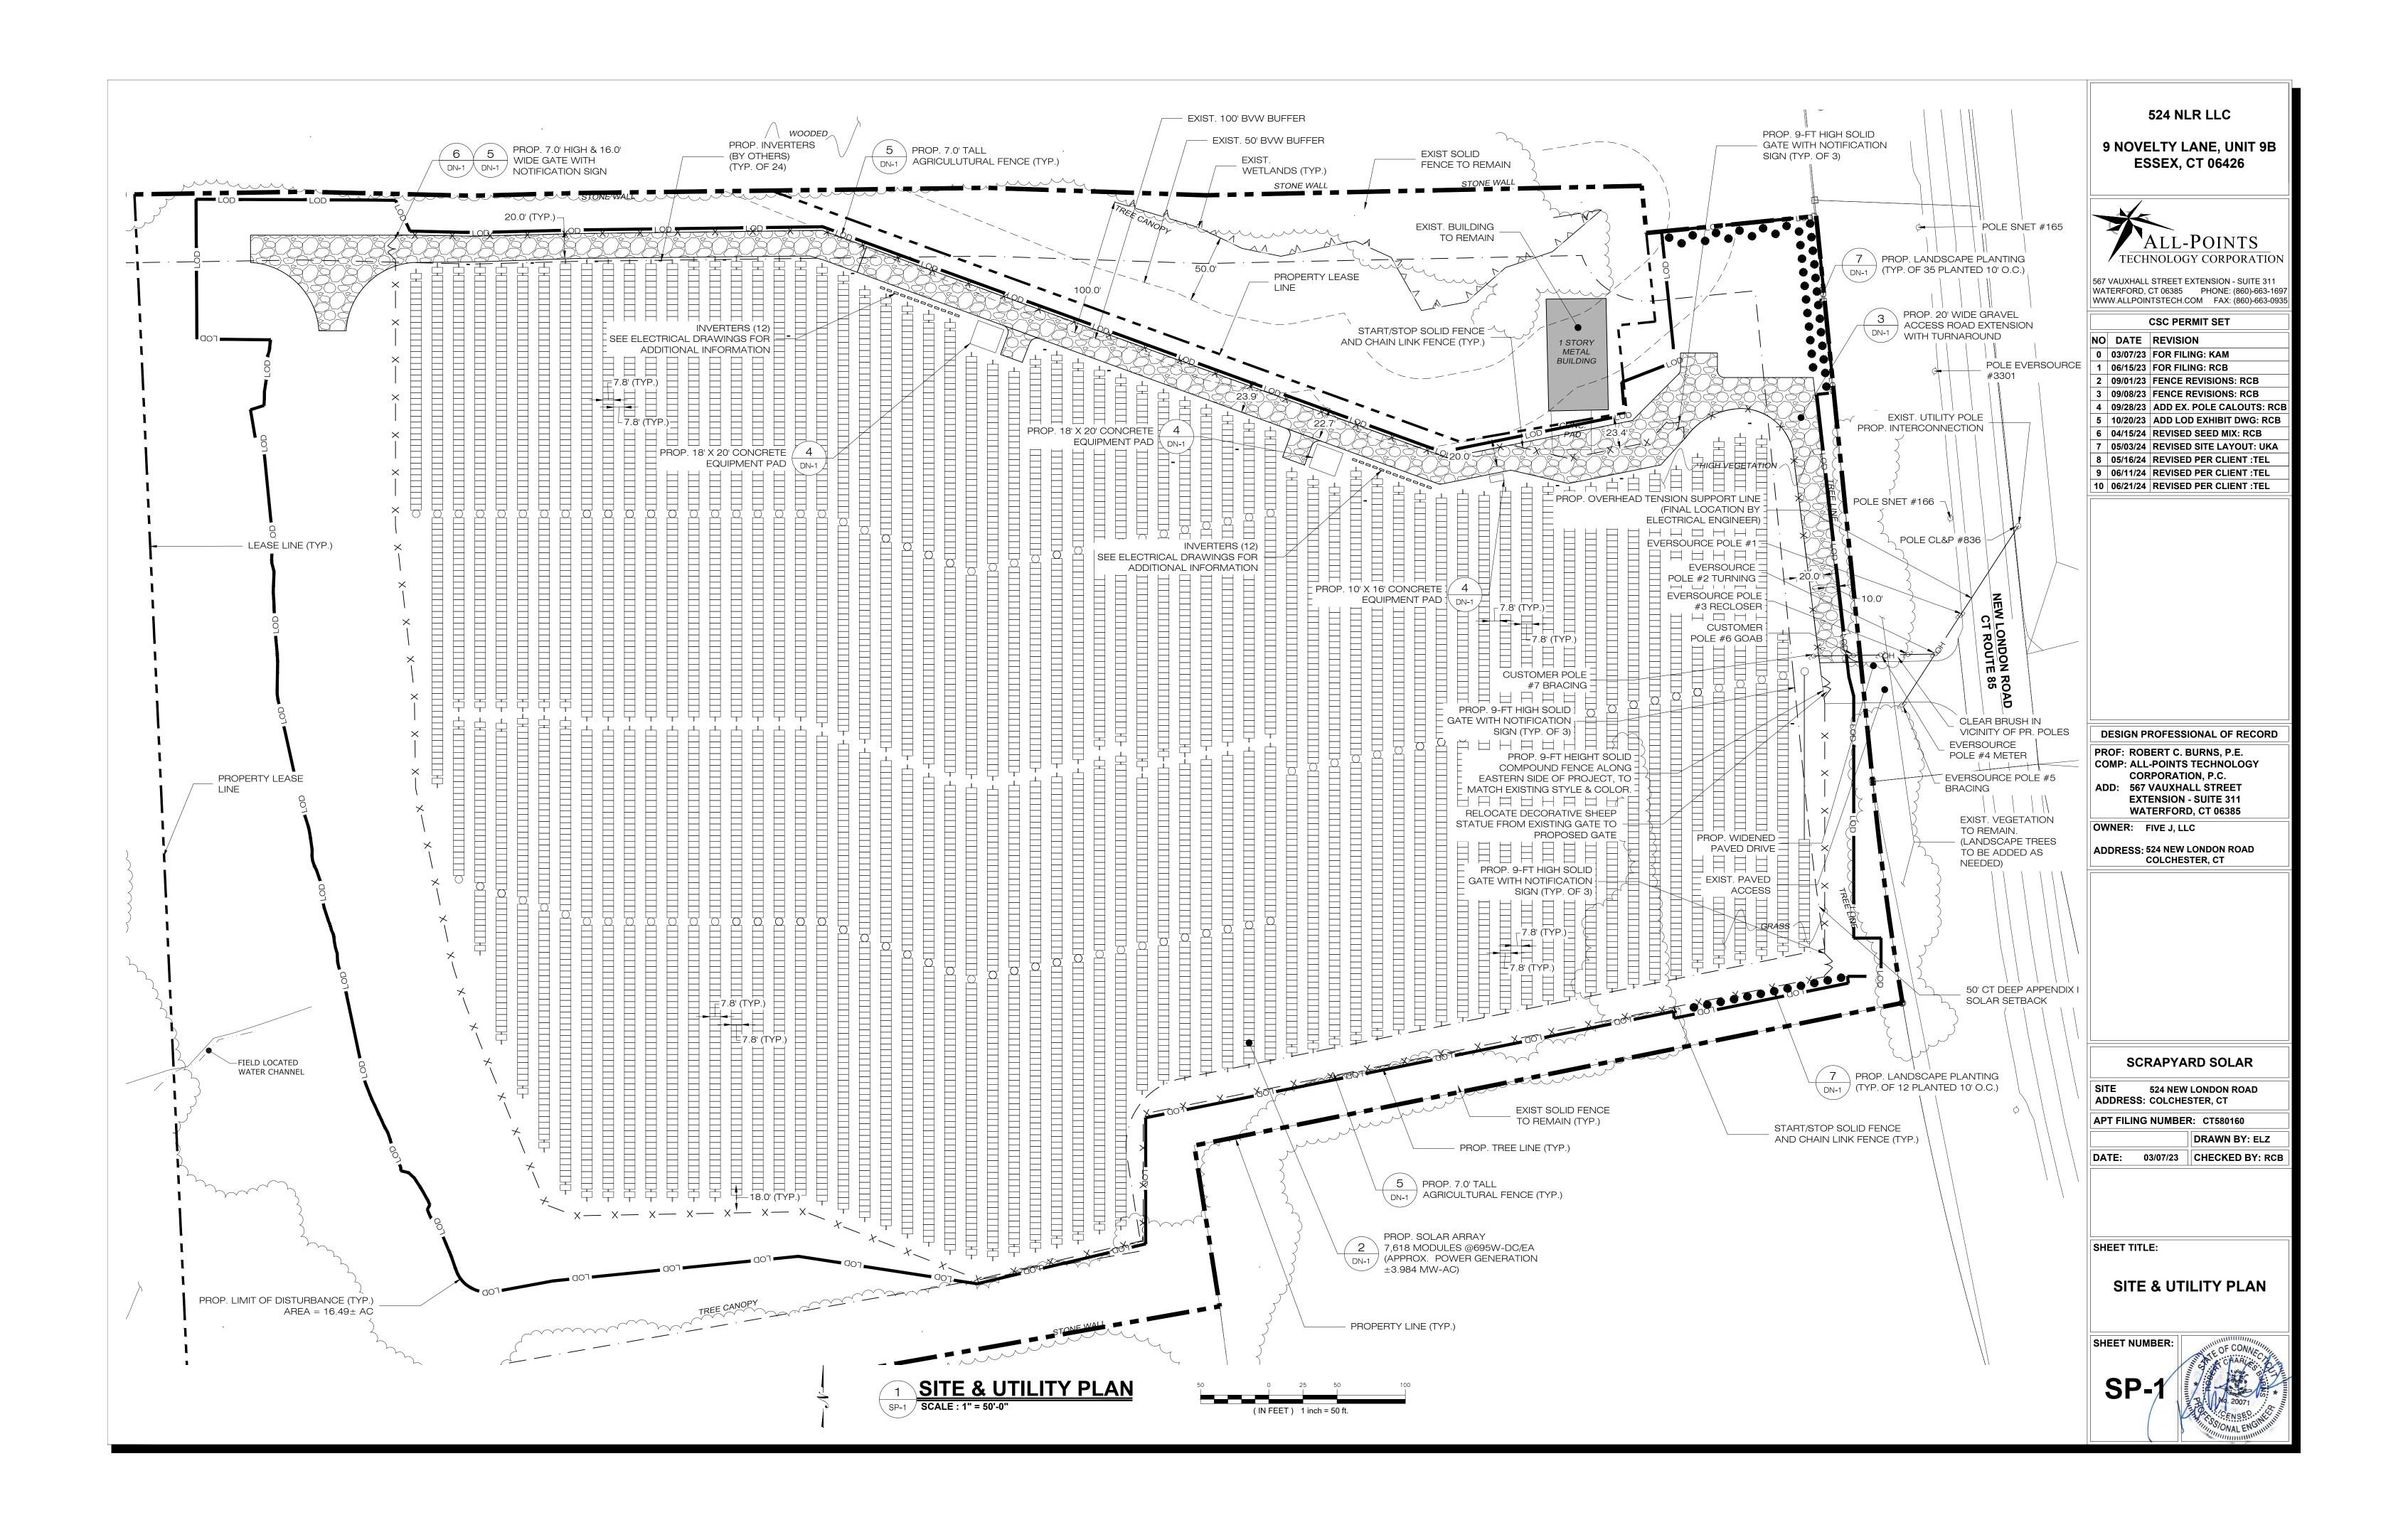

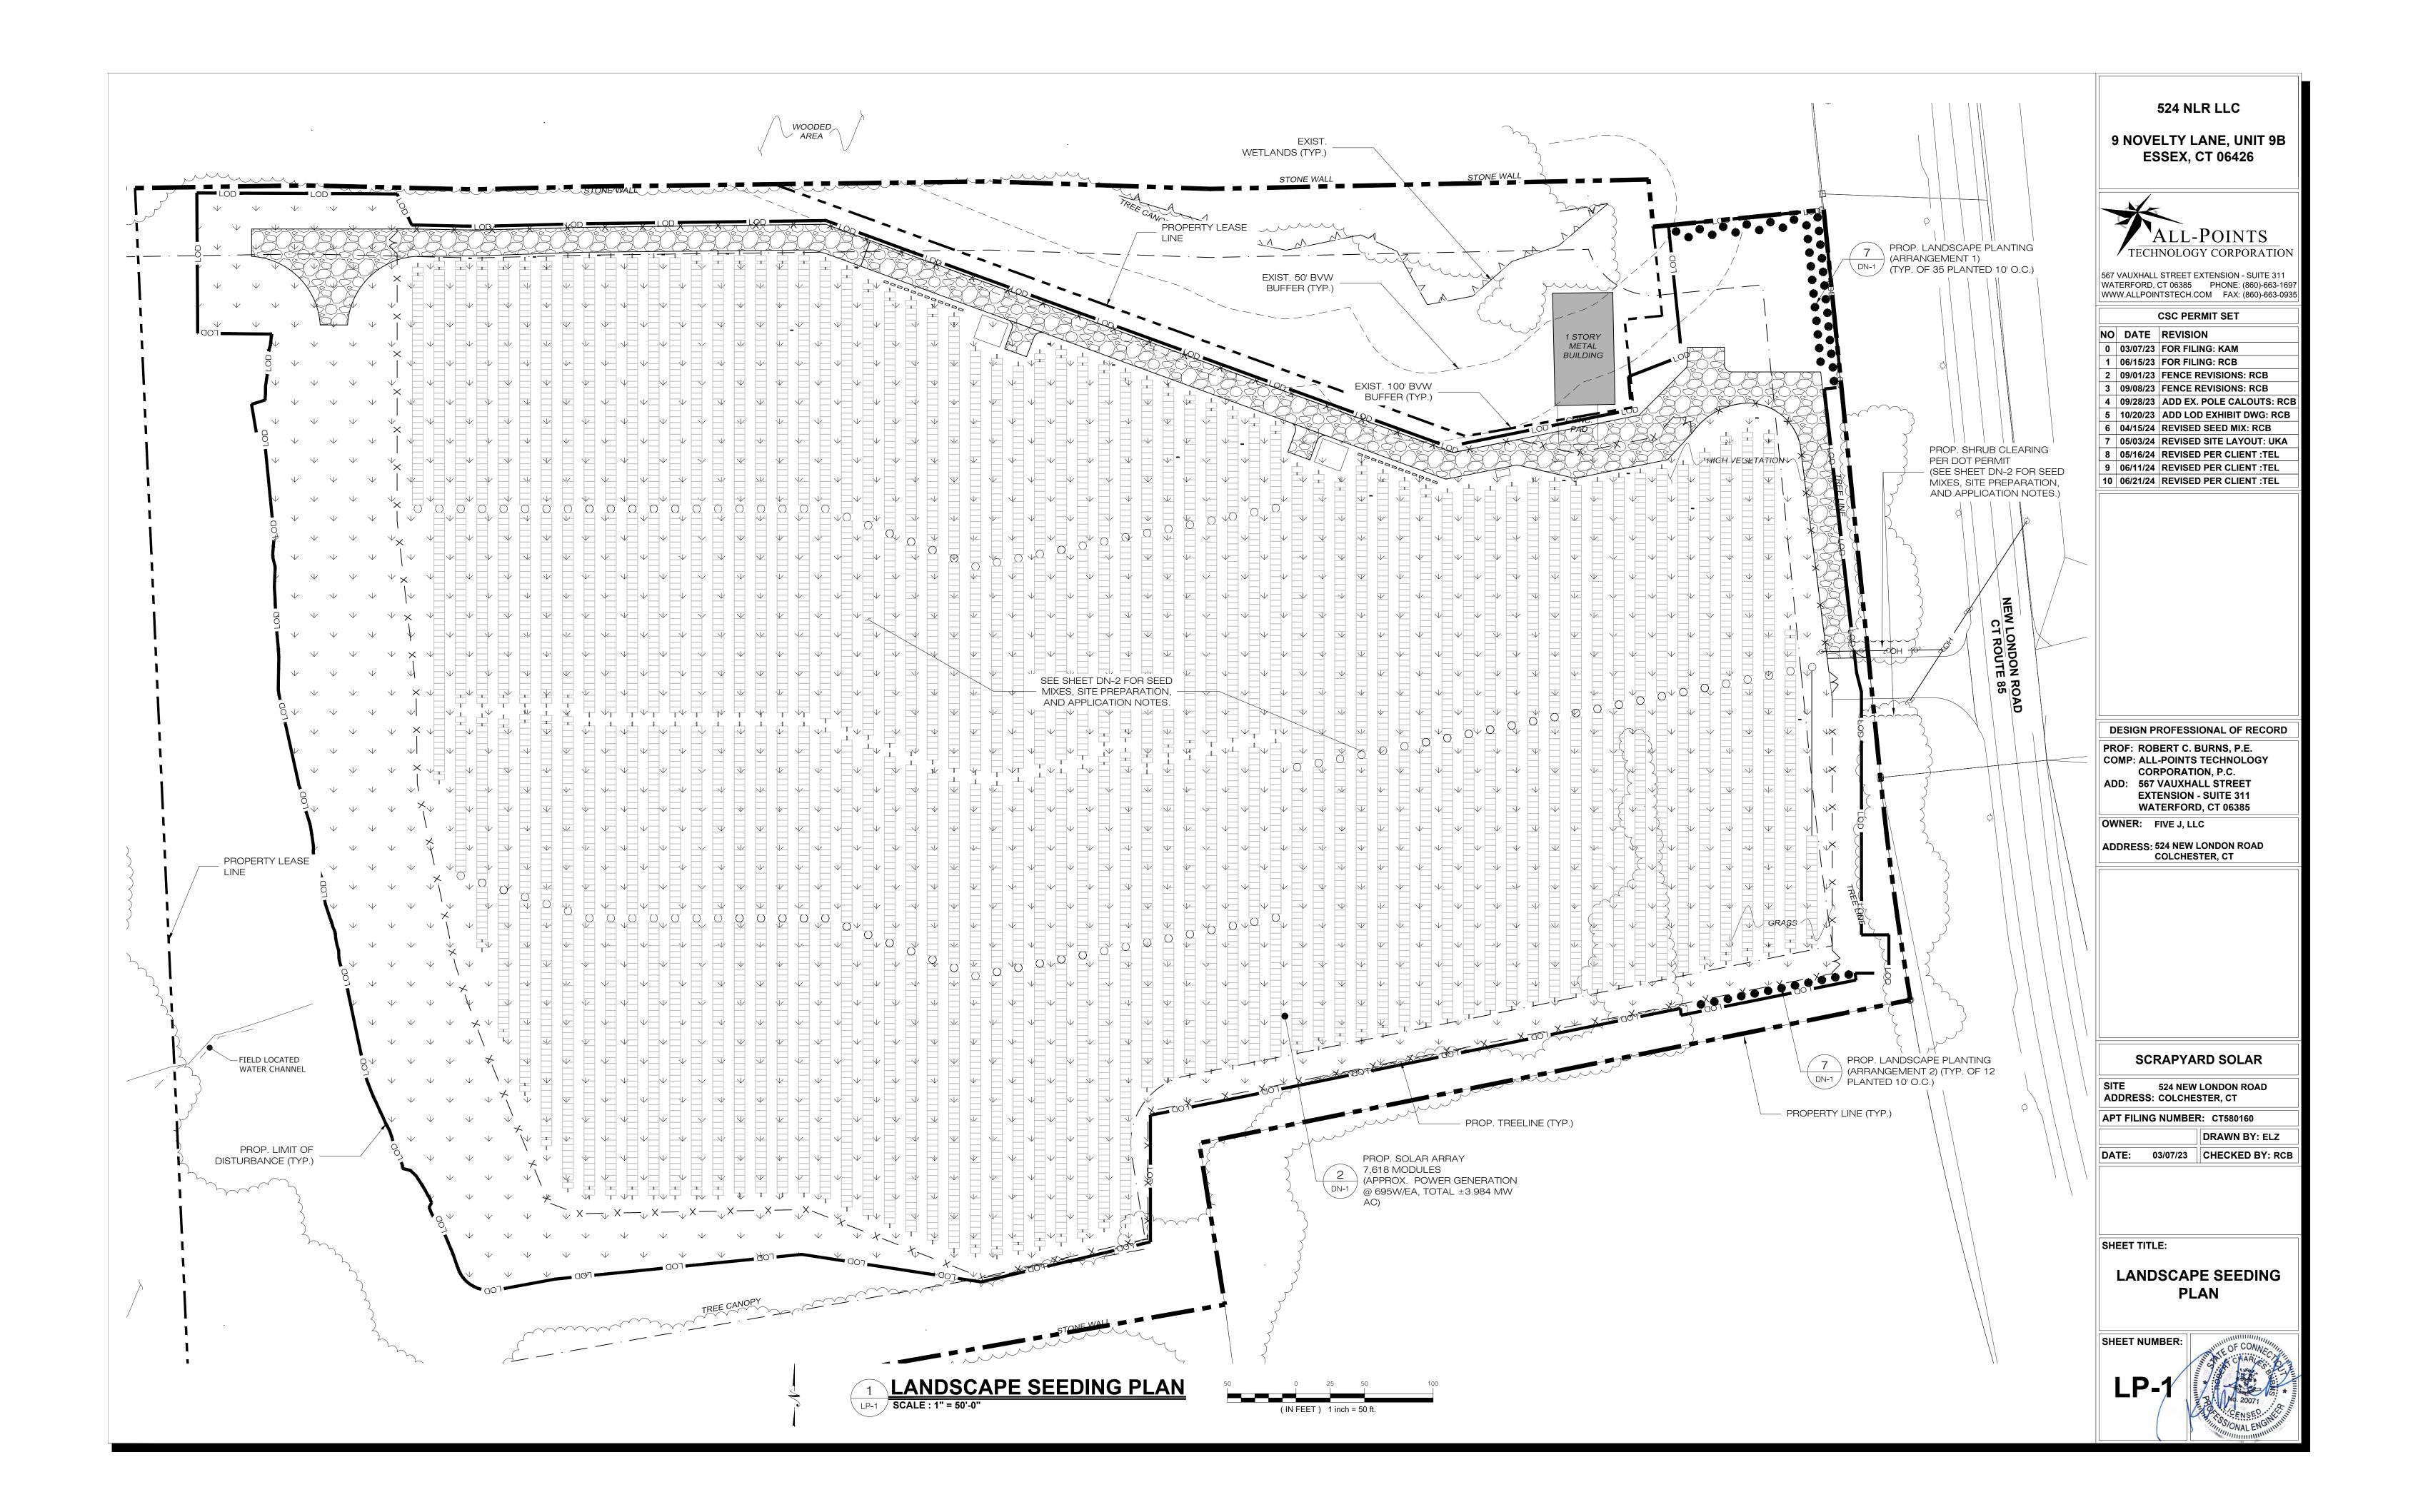

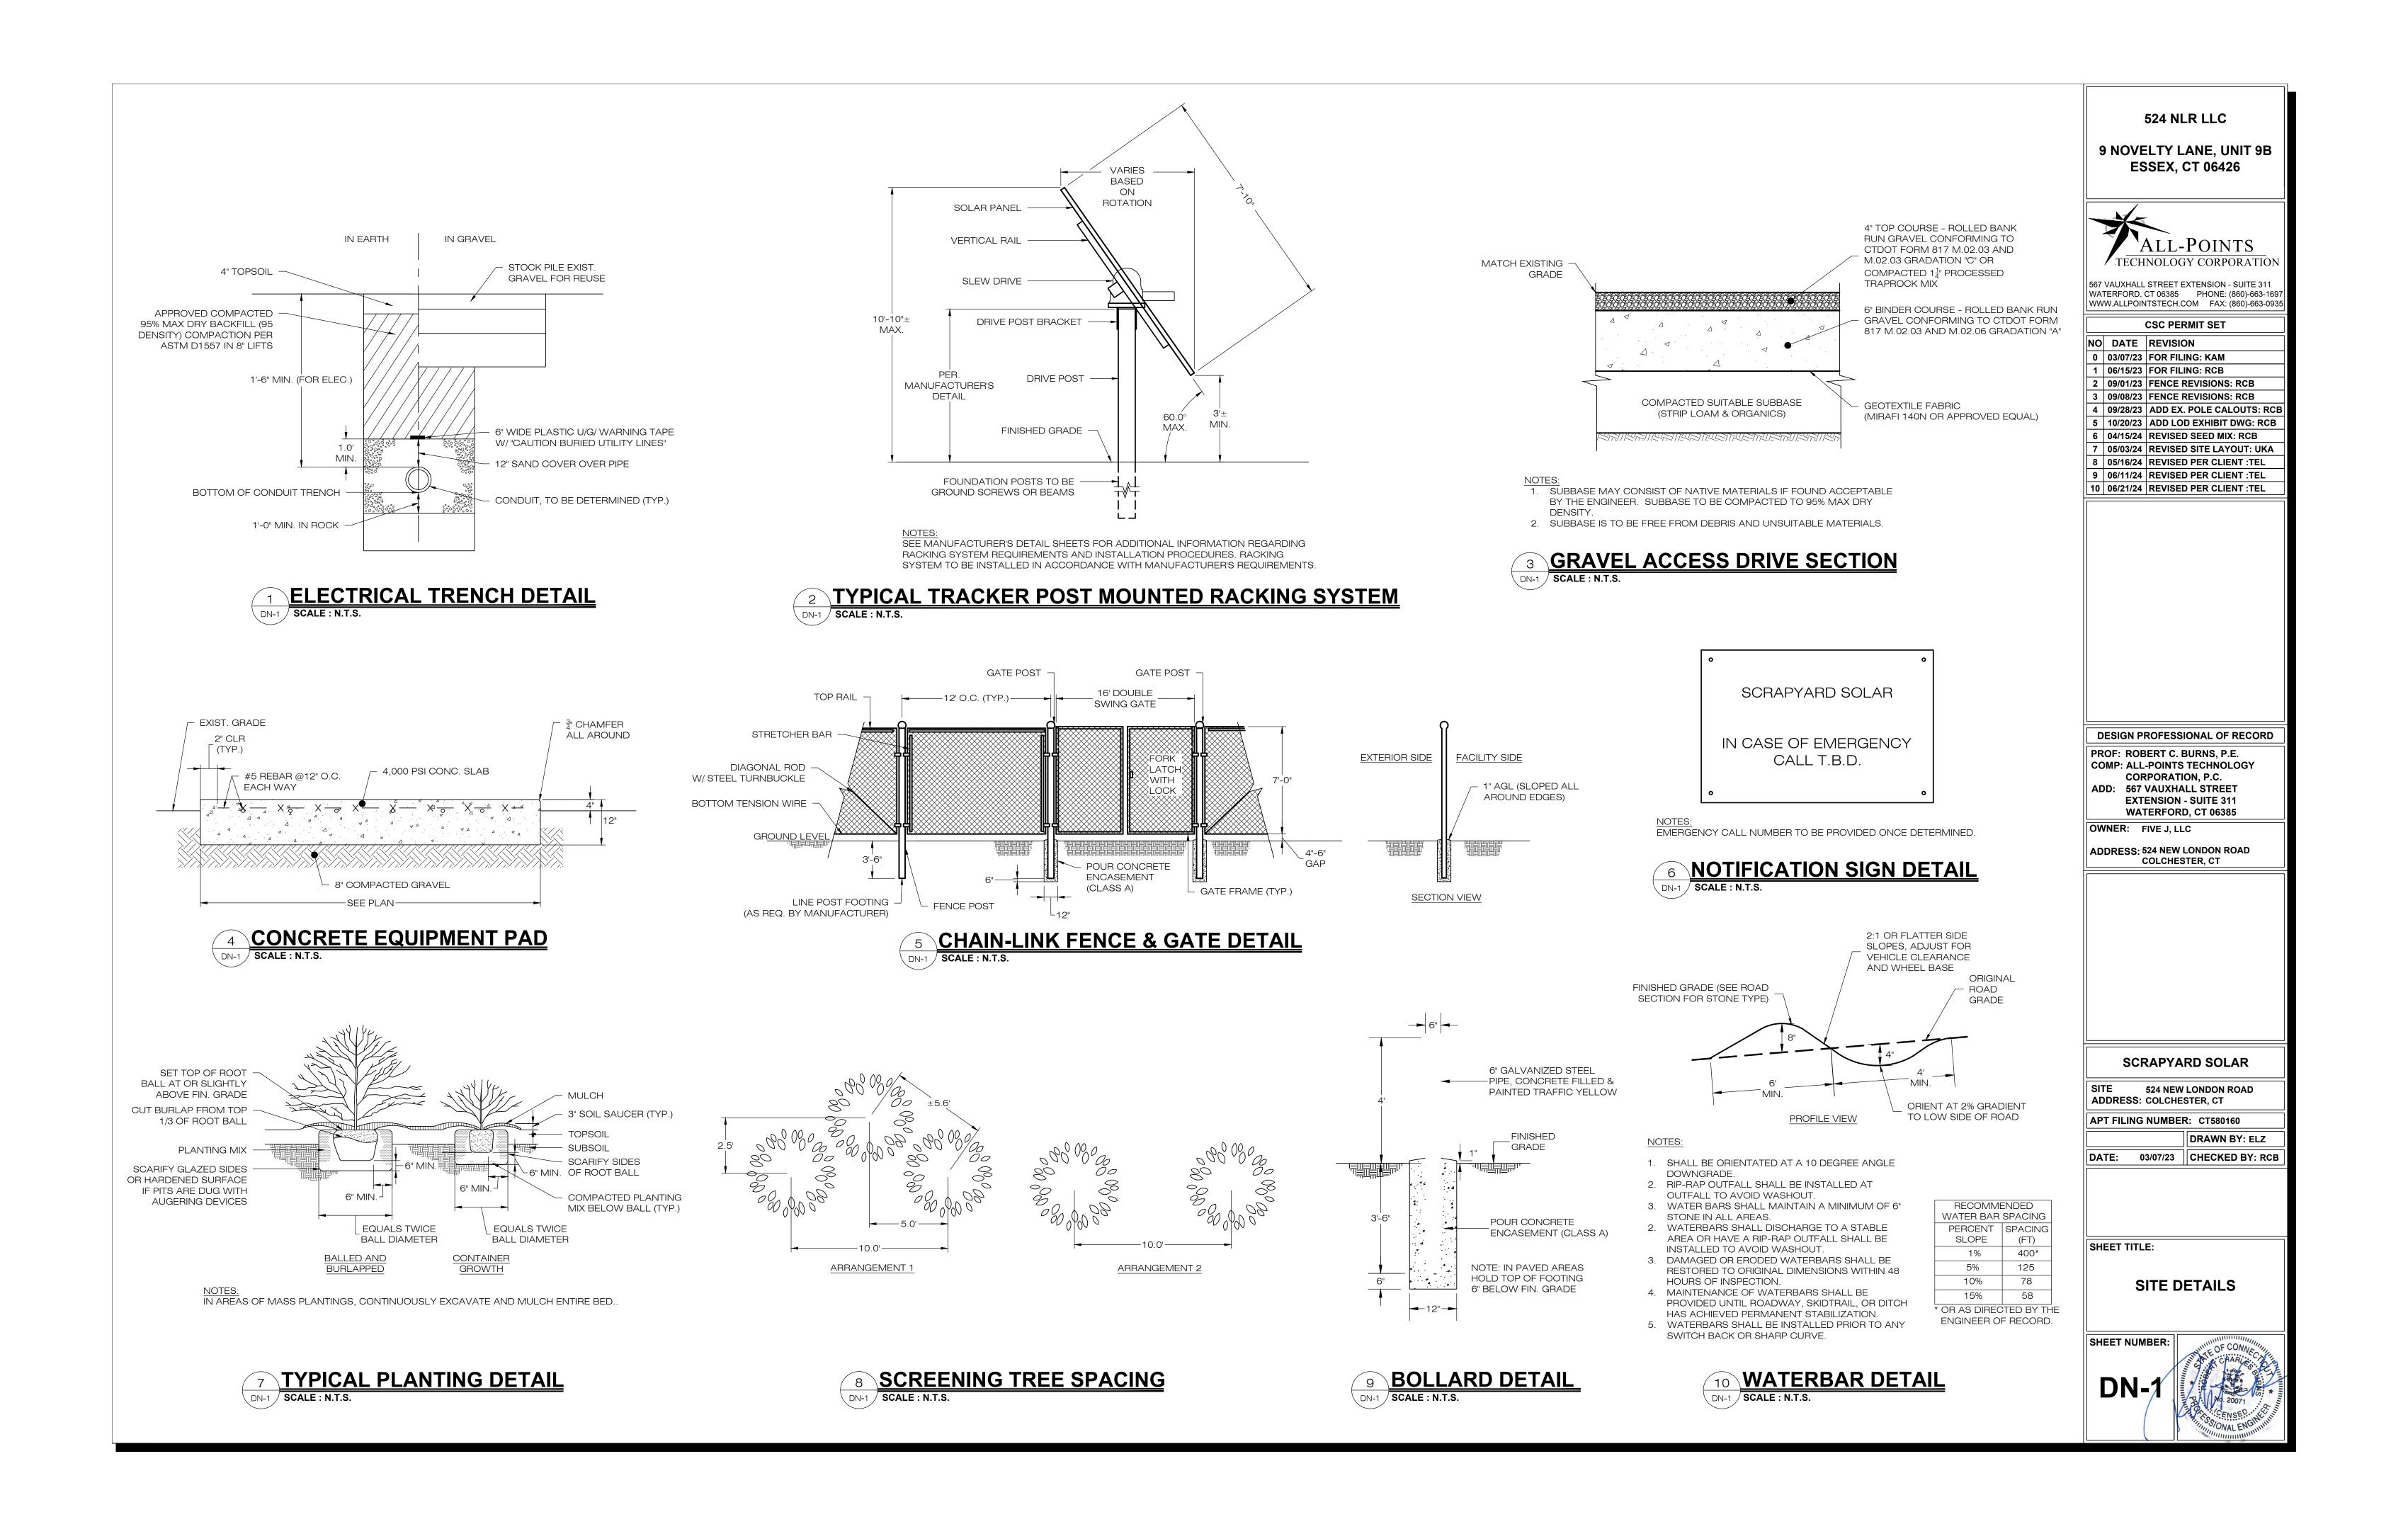

## **Quick Erosion Control Cover Mix - ERNMX-104**

	<b>Botanical Name</b>	Common Name	Price/Lb
50.00 %	Lolium multiflorum	Annual Ryegrass	1.20
50.00 %	Lolium perenne, 'Blackstone'	Perennial Ryegrass, 'Blackstone'	4.08
100.00 %		Mix Price/Lb Bulk:	\$2.64

**Seeding Rate:** 50 lb per acre Erosion Control & Revegetation

Designed to achieve that quick, green color and fast erosion control with strong, fibrous roots. Mix formulations are subject to change without notice depending on the availability of existing and new products. While the formula may change, the guiding philosophy and function of the mix will not.

# QUICK EROSION CONTROL COVER MIX (35%)

## **Ernst Native Habitat for Strip Mines Mix - ERNMX-111**

	<b>Botanical Name</b>	Common Name	Price/Lb
29.60 %	Andropogon gerardii, 'Niagara'	Big Bluestem, 'Niagara'	12.62
25.00 %	Panicum virgatum, 'Shelter'	Switchgrass, 'Shelter'	12.22
18.90 %	Sorghastrum nutans, NY4 Ecotype	Indiangrass, NY4 Ecotype	15.29
17.00 %	Elymus virginicus, Madison-NY Ecotype	Virginia Wildrye, Madison-NY Ecotype	10.16
3.00 %	Rudbeckia hirta	Blackeyed Susan	31.20
2.00 %	Chamaecrista fasciculata, PA Ecotype	Partridge Pea, PA Ecotype	7.20
2.00 %	Heliopsis helianthoides, PA Ecotype	Oxeye Sunflower, PA Ecotype	33.60
1.80 %	Desmodium canadense, PA Ecotype	Showy Ticktrefoil, PA Ecotype	48.00
0.30 %	Monarda fistulosa, Fort Indiantown Gap-PA Ecotype	Wild Bergamot, Fort Indiantown Gap-PA Ecotype	96.00
0.20 %	Asclepias syriaca	Common Milkweed	96.00
0.10 %	Pycnanthemum tenuifolium	Narrowleaf Mountainmint	168.00
0.10 %	Solidago canadensis, PA Ecotype	Canada Goldenrod, PA Ecotype	240.00
100.00 %		Mix Price/Lb Bulk:	\$14.91

**Seeding Rate:** 20 lbs/acre with 30 lbs/acre of a cover crop. For

a cover crop use either grain oats (1 Jan to 31 Jul) or grain rye (1 Aug to 31 Dec).

Erosion Control & Revegetation; Grasses & Grass-like Species - Herbaceous Perennial; Herbaceous Flowering Species - Herbaceous

A permanent meadow mix for wildlife cover and pollinator habitat on disturbed sites. Mix formulations are subject to change without notice depending on the availability of existing and new products. While the formula may change, the guiding philosophy and function of the mix will not.

3 ERNST NATIVE HABITAT FOR STRIP MINES MIX (25%)

# **SEEDING NOTES**

- 1. CONDUCT SOIL FERTILITY TESTING AND SHARE RESULTS WITH DESIGN TEAM TO CONFIRM THE FOLLOWING RECOMMENDATIONS.
- 2. THE NEED FOR ORGANIC MATTER SOIL AMENDMENT (E.G. COMPOST, COMPOSED LEAF LITTER,

ETC.) WILL BE DEPENDENT IN PART ON SOIL FERTILITY TESTING RESULTS.

- 3. APPLY SLOW RELEASE OR ORGANIC FERTILIZER AND LIME AT RATES RECOMMENDED FROM SOIL FERTILITY TESTING RESULTS.
- 4. TILL COMPOST, FERTILIZER, AND LIME IN TO TOP 4-6 INCHES OF SOIL TO PREPARE SEED BED.
- 5. APPLY A HYDROSEED BLEND OF THE FOLLOWING MIXES AT THE VOLUME PERCENTAGES NOTED WITH A BONDED FIBER MATRIX MULCH TO THE AMENDED SOIL.

Mix Price/Lb Bulk: \$12.47

#### **Ernst Native Biomass Mix for Strip Mines & Gas Production Sites - ERNMX-110**

	<b>Botanical Name</b>	Common Name	Price/Lb
30.00 %	Andropogon gerardii, 'Niagara'	Big Bluestem, 'Niagara'	12.62
26.00 %	Panicum amarum, Atlantic-VA Ecotype	Coastal Panicgrass, Atlantic-VA Ecotype	11.11
26.00 %	Panicum virgatum, 'Carthage', NC Ecotype	Switchgrass, 'Carthage', NC Ecotype	12.79
12.00 %	Elymus virginicus, Madison-NY Ecotype	Virginia Wildrye, Madison-NY Ecotype	10.16
4.00 %	Chamaecrista fasciculata, PA Ecotype	Partridge Pea, PA Ecotype	7.20
2.00 %	Desmodium canadense, PA Ecotype	Showy Ticktrefoil, PA Ecotype	48.00

100.00 % **Seeding Rate:** 15 lbs/acre with 30 lbs/acre of a cover crop. For

a cover crop use either grain oats (1 Jan to 31 Jul) or grain rye (1 Aug to 31 Dec).

Erosion Control & Revegetation; Grasses & Grass-like Species - Herbaceous Perennial

A biodiverse mix of warm and cool season grasses with forbs for maximum, sustainable biomass production. Mix formulations are subject to change without notice depending on the availability of existing and new products. While the formula may change, the guiding philosophy and function of the mix will not.



## Non-Native Ernst Best Strip Mine & Gas Production Mix - ERNMX-101

	<b>Botanical Name</b>	Common Name	Price/Lb
30.00 %	Festuca arundinacea, Fawn	Tall Fescue, Fawn	2.64
25.00 %	Lolium multiflorum	Annual Ryegrass	1.20
15.00 %	Phleum pratense, Climax	Timothy, Climax	3.72
10.00 %	Lotus corniculatus, 'Norcen'	Bird's Foot Trefoil, 'Norcen'	10.80
10.00 %	Trifolium hybridum	Alsike Clover	4.50
5.00 %	Agrostis alba	Redtop	12.00
5.00 %	Melilotus officinalis	Yellow Blossom Sweetclover	5.76
00.00 %		Mix Price/	Lb Bulk: \$4.07

**Seeding Rate:** 50 lb per acre Erosion Control & Revegetation; Grasses & Grass-like Species - Herbaceous Perennial

Designed for the toughest disturbed sites; tolerates low pH. Mix formulations are subject to change without notice depending on the availability of existing and new products. While the formula may change, the guiding philosophy and function of the mix will not.

4 NON-NATIVE ERNST BEST STRIP MINE & GAS PRODUCTION MIX (15%)

#### 524 NLR LLC

9 NOVELTY LANE, UNIT 9B **ESSEX, CT 06426** 



567 VAUXHALL STREET EXTENSION - SUITE 311 WATERFORD, CT 06385 PHONE: (860)-663-169 WWW.ALLPOINTSTECH.COM FAX: (860)-663-093

### **CSC PERMIT SET**

## NO DATE REVISION

- 0 03/07/23 FOR FILING: KAM
- 1 06/15/23 FOR FILING: RCB 2 09/01/23 FENCE REVISIONS: RCB
- 3 09/08/23 FENCE REVISIONS: RCB
- 4 09/28/23 ADD EX. POLE CALOUTS: RCB
- 5 | 10/20/23 | ADD LOD EXHIBIT DWG: RCB
- 6 04/15/24 REVISED SEED MIX: RCB
- 7 05/03/24 REVISED SITE LAYOUT: UKA
- 8 05/16/24 REVISED PER CLIENT :TEL 9 06/11/24 REVISED PER CLIENT :TEL

10 06/21/24 REVISED PER CLIENT :TEL

DESIGN PROFESSIONAL OF RECORD

PROF: ROBERT C. BURNS, P.E. **COMP: ALL-POINTS TECHNOLOGY** CORPORATION, P.C. ADD: 567 VAUXHALL STREET **EXTENSION - SUITE 311** 

WATERFORD, CT 06385 OWNER: FIVE J, LLC

ADDRESS: 524 NEW LONDON ROAD COLCHESTER, CT

# SCRAPYARD SOLAR

SITE 524 NEW LONDON ROAD ADDRESS: COLCHESTER, CT

APT FILING NUMBER: CT580160

DRAWN BY: ELZ

DATE: 03/07/23 | CHECKED BY: RCB

SHEET TITLE:

SITE DETAILS

SHEET NUMBER:

