

**STORMWATER MANAGEMENT PLAN WITH STORMWATER  
POLLUTION PREVENTION PLAN  
(SWPPP)  
VOLUME 1**

**WIND COLEBROOK SOUTH  
COLEBROOK, CONNECTICUT**

**Prepared for:**



**BNE Energy**  
29 South Main Street  
Town Center, Suite 200  
West Hartford, CT 06107

**by:**



**CIVIL 1**  
43 Sherman Hill Road  
Woodbury, CT 06798

**AUGUST 2011  
REVISED AUGUST 2012**

**TABLE OF CONTENTS**

<b>1.0</b>	<b>PROJECT INTRODUCTION.....</b>	<b>1-1</b>
1.1	SITE SUMMARY .....	1-1
1.1.1	Existing Conditions .....	1-1
1.1.2	Project Description .....	1-1
1.2	PROJECT OWNER AND OPERATOR.....	1-1
1.3	PERMIT COVERAGE AND ELIGIBILITY .....	1-2
1.4	CERTIFICATION REQUIREMENTS.....	1-2
1.5	COASTAL CONSISTENCY REVIEW .....	1-3
1.6	ENDANGERED OR THREATENED SPECIES.....	1-3
1.7	SOILS, SLOPES, VEGETATION, AND CURRENT DRAINAGE PATTERNS .....	1-3
1.7.1	Soil Type(s).....	1-3
1.7.2	Slopes .....	1-3
1.7.3	Drainage Patterns .....	1-3
1.7.4	Vegetation .....	1-3
1.8	SITE FEATURES AND SENSITIVE AREAS TO BE PROTECTED .....	1-4
1.8.1	Receiving Waters and TMDL Applicability .....	1-4
1.8.2	Wetlands.....	1-4
1.9	FINAL STABILIZATION AND TERMINATION OF COVERAGE.....	1-4
1.10	RETENTION OF RECORDS.....	1-4
<b>2.0</b>	<b>CONSTRUCTION ACTIVITIES .....</b>	<b>2-1</b>
2.1	DESCRIPTION OF CONSTRUCTION ACTIVITY.....	2-1
2.2	CONSTRUCTION SITE ESTIMATES .....	2-1
2.3	PROPOSED STORMWATER MANAGEMENT PRACTICES .....	2-1
2.3.1	Stormwater Treatment Practices .....	2-1
2.3.2	Flood Control and Peak Runoff Attenuation Management Practices .....	2-2
2.3.3	Pre- and Post Development Storm water Flows .....	2-2
<b>3.0</b>	<b>BEST MANAGEMENT PRACTICES .....</b>	<b>3-1</b>
3.1	STRUCTURAL CONTROL PRACTICES .....	3-1
3.2	TEMPORARY EROSION CONTROL PRACTICES .....	3-1
3.2.1	Sediment Fence (GSF) .....	3-1
3.2.2	Hay Bale Barrier (HB) .....	3-2
3.2.3	Stone Check Dam (SCD) .....	3-2
3.2.4	Temporary Pipe Slope Drain (TSD).....	3-2
3.2.5	Temporary Diversion (TD) .....	3-2
3.2.6	Temporary Fill Berm (TFB).....	3-3
3.2.7	Temporary Sediment Trap (TST).....	3-3
3.2.8	Construction Entrance (CE) .....	3-3
3.2.9	Tree Protection (TP).....	3-3

3.2.10	Temporary Erosion Control Blankets (ECB) .....	3-4
3.3	SOIL STABILIZATION PRACTICES .....	3-4
3.4	MAINTENANCE AND INSPECTIONS .....	3-4
3.5	FINAL STABILIZATION .....	3-4
3.5.1	Seeding .....	3-4
3.5.2	Fertilizer .....	3-5
3.5.3	Mulching .....	3-5
3.5.4	Topsoiling.....	3-5
3.5.5	Temporary Control Removal .....	3-5
<b>4.0</b>	<b>GOOD HOUSEKEEPING BMP'S .....</b>	<b>4-1</b>
4.1	POTENTIAL SOURCES OF POLLUTION .....	4-1
4.2	CONTROLS TO REDUCE POLLUTION FROM THE CONSTRUCTION SITE .....	4-1
4.2.1	Material Handling and Waste Management .....	4-1
4.2.2	Establish Proper Building Material Staging Areas .....	4-1
4.2.3	Allowable Non-Stormwater Discharge Management .....	4-1
4.2.4	Maintenance of Controls .....	4-1
<b>5.0</b>	<b>HAZARDOUS SUBSTANCE OR OIL SPILL REPORTING .....</b>	<b>5-1</b>
5.1	MATERIAL MANAGEMENT PRACTICES .....	5-1
5.2	NON-PETROLEUM PRODUCTS .....	5-1
5.3	PETROLEUM PRODUCTS.....	5-1
5.4	SPILL CONTROL AND CLEAN UP.....	5-2
<b>6.0</b>	<b>SWPPP APPENDICES .....</b>	<b>6-1</b>

**APPENDICES**

Appendix A	Permit Coverage
Appendix B	Certifications
Appendix C	Pre-Construction Meeting
Appendix D	Maps and Drawings
Appendix E	Construction Records
Appendix F	Inspection and Maintenance Records
Appendix G	Hazardous Material or Oil Spill Records
Appendix H	Update Records
Appendix I	Copy of CT DEP Notice of Termination
Appendix J	Connecticut General Permit for the Discharge of Stormwater and Dewatering Wastewaters Associated with Construction Activities (DEP-PED-GP-015)
Appendix K	Supporting Calculations

**Contact Information / Responsible Parties:**

Permitted:

BNE Energy  
29 South Main Street  
Town Center, Suite 200  
West Hartford, CT 06107  
(800) 450-0503

Contractor Co-Permittee:

To be determined

Contractor Operator(s):

To be determined

Stormwater Manager and SWPPP Contact(s):

BNE Energy  
29 South Main Street  
Town Center Suite 200  
West Hartford, CT 06107  
(800) 450-0503

This SWPPP was prepared by:

Shane Smith, PE  
Zapata Incorporated  
6302 Fairview Road, Suite 600  
Charlotte, North Carolina 28210

**Section 1.0  
PROJECT INTRODUCTION**

## **1.0 PROJECT INTRODUCTION**

### **Project/Site Information:**

Project/Site Name: Wind Colebrook South

Location: 29 Flagg Hill Road  
Colebrook, Connecticut

Latitude/Longitude:   Latitude:                   Longitude:  
                                  41° 57' 50" N                   73° 08' 46" W

Method for determining latitude/longitude: Google Earth

## **1.1 SITE SUMMARY**

### ***1.1.1 Existing Conditions***

The project is located at 17 and 29 Flagg Hill Road and consists of approximately 80 acres and is undeveloped with the exception of two existing houses at 17 and 29 Flagg Hill Road. The Property is located along the Norfolk town line and approximately 600 feet from the Winsted/Winchester town line. Though the surrounding land uses are mixed, consisting of both commercial and residential development, the property is located in the R-2 residential zone. The Colebrook zoning regulations do not address wind turbine installations. The Property is abutted by the undeveloped land owned by the Nature Conservancy to the west, land owned by the Gun Club to the north and residential properties to the east and south. The site is currently accessed via Flagg Hill Road. This access point will be maintained throughout the construction process. Currently, there are no structural stormwater discharge points. All stormwater flows over land to discharge points off site.

### ***1.1.2 Project Description***

The developer plans to install three GE 1.6 MW wind turbines at the Property: one in the northwest corner of the Property, one in the northeast corner of the Property and one in the southern area of the Property where the meteorological tower is currently located. In addition to the three turbines, the project will include construction of temporary equipment lay-down areas for each turbine, crane assembly area, access road, permanent support building and associated ground equipment including an electrical collector yard and associated utility infrastructure so that the turbines can be interconnected to the electrical grid. Following completion of the project, all temporary structures will be removed and the site returned to pre-construction conditions.

## **1.2 PROJECT OWNER AND OPERATOR**

The project owner and operator, BNE Energy, will be the responsible entity for completing the project. The address and telephone is:

BNE Energy  
29 South Main Street  
Town Center Suite 200  
West Hartford, CT 06107  
(800) 450-0503

### **1.3 PERMIT COVERAGE AND ELIGIBILITY**

The U.S. Environmental Protection Agency (EPA) requires a National Pollutant Discharge Elimination System (NPDES) General Permit for stormwater discharges from construction sites that disturb more than one acre of land or from smaller sites that are part of a larger, common plan of development. For the purposes of the NPDES program, construction activities are defined as clearing, excavating, grading, or other land disturbing activities.

The General Permit for the Discharge of Stormwater and dewatering Wastewaters associated with Construction Activities (CGP) authorizes stormwater discharges from construction activities which result in the disturbance of one or more acres of land area on a site regardless of project phasing. In the case of a larger plan of development, the estimate of total acres of site disturbance shall include, but is not limited to, road and utility construction, individual lot construction, and all other construction associated with the overall plan, regardless of the individual parties responsible for the construction of these various elements. These conditions are subject to the conditions outlined in DEP-PED-GP-015. The effective dates of this CGP are April 9, 2010 thru October 1, 2011, and cover all areas of Connecticut. This CGP includes provisions for the development of this Stormwater Pollution Prevention Plan (SWPPP) to maximize the potential benefits of pollution prevention and sediment and erosion control measures at a construction site.

CGP eligibility is limited to discharges from “large” and “small” construction activity as defined in Section 3 of 2010 Connecticut General Permit for the Discharge of Stormwater and Dewatering Wastewaters. A copy of DEP-PED-GP-015 is included in Appendix J of this document. The permittee has requested coverage under this CGP by submission of a complete and accurate General Permit Registration Form and Transmittal. Copies of these are included in Appendix A. A map detailing the limits of disturbance, for the disturbed area indicated on the registration form, and covered under this CGP, is included in Appendix D. The permittee is granted coverage under this CGP when they have received a Letter of Coverage (LOC) from DEP. A copy of the LOC is to be included in Appendix A.

### **1.4 CERTIFICATION REQUIREMENTS**

All permittees and operators are required to sign a SWPPP certification as a condition of the CGP. The signed certifications confirm that the contractor has been informed that a SWPPP has been prepared for the project and they will be required to perform necessary actions that have been identified to comply with both the SWPPP and the CGP. No permittee or operator shall commence work on this project site until they have familiarized themselves with this plan and signed the appropriate SWPPP certification. It may be necessary for the contractor to implement additional erosion control and pollution prevention measures not previously identified to maintain compliance with the CGP. The following signed SWPPP certifications are included in

Appendix B:

- Preparer
- Permittee and Co-Permittee
- Operator
- Inspector

## **1.5 COASTAL CONSISTENCY REVIEW**

After review of the applicable policies and standards in Connecticut's Coastal Management Act (CCMA), codified in Sections 22a-90 through 22a-112 of the Connecticut General Statutes (CGS), as amended, it has been determined that this project does not require a coastal consistency review.

## **1.6 ENDANGERED OR THREATENED SPECIES**

The existence and/or mitigation for endangered or threatened species is discussed within the comprehensive assessment of all potential environmental impacts associated with Wind Colebrook South.

## **1.7 SOILS, SLOPES, VEGETATION, AND CURRENT DRAINAGE PATTERNS**

### ***1.7.1 Soil Type(s)***

Based upon a review of typical geologic conditions and the National Soil Cooperative Survey, the soils have been classified as (1) Bice- Millsite complex soils slopes 3 to 45 percent slopes – very rocky; (2) Westminster- Millsite- Rock Outcrop complex 3 to 15 percent slopes; (3) Bice fine sandy loams ranging from 3 to 15 percent slopes – very stony; (4) Schroon fine sandy loams ranging from 2 to 15 percent slopes - very stony; (5) Shelburne fine sandy loam, 8 to 35 percent slopes – extremely stony; (6) Ashfield fine sandy loam, 8 to 15 percent slopes – very stony, (7) Wonsqueak mucky peat; and (8) Brayton-loonmeadow complex – extremely stony.

### ***1.7.2 Slopes***

The project site consists of varying slope conditions ranging from relatively flat conditions in the area of the meteorological tower to steep slopes along the eastern and western property boundary.

### ***1.7.3 Drainage Patterns***

Existing site topography is such that runoff migrates, typically via overland sheet flow, through the site to either the existing pond or to an existing ditch line along Flagg Hill Road. An unnamed perennial watercourse outlets from the pond in the vicinity of the southern property boundary, flowing south.

### ***1.7.4 Vegetation***

The property is generally characterized by second growth and upland hardwood forest. Forested uplands in the eastern portion of the Property are dominated by deciduous pole timber (trees 4.0 to 11.9 inches diameter at breast height [DBH]) and small sawtimber size trees (12 to 15 inches DBH). In the northwest and southwest corners of the property, vegetation is characterized as red oak-northern hardwood forest.



## **1.8 SITE FEATURES AND SENSITIVE AREAS TO BE PROTECTED**

### **1.8.1 Receiving Waters and TMDL Applicability**

There are currently zero impaired waterways on the most current 303(d) listing of impaired waterways within the vicinity of the project site.

### **1.8.2 Wetlands**

Within to the property boundary several wetland areas have been identified and delineated. Mitigation and impacts are discussed in the environmental assessment completed by VHB, Inc.

## **1.9 FINAL STABILIZATION AND TERMINATION OF COVERAGE**

At the completion of a construction project registered pursuant to Section 4 of the general permit, a Notice of Termination must be filed with the commissioner. A project shall be considered complete after the site has been stabilized for at least three months following the cessation of construction activities. A site is not considered stabilized until there is no active erosion or sedimentation present and no disturbed areas remain exposed.

The termination notice shall be filed on forms prescribed and provided by the commissioner and shall include the following: (1) The permit number as provided to the permittee on the permit certificate; (2) The name of the registrant as reported on the general permit registration form DEP-PED-REG-015; (3) The address of the completed construction site; (4) The date all storm drainage structures were cleaned of construction debris pursuant to Section 6(b)(6)(C)(iv) of the general permit, the date of completion of construction, and the date of the final inspections pursuant to Section 6(b)(6)(D) of this general permit; (5) A description of the post-construction activities at the site; and (6) Signature of the permittee. The termination form should be filed with the commissioner at the following address:

Water Permitting & Enforcement Division  
Bureau of Materials Management & Compliance Assurance  
Department of Environmental Protection  
79 Elm Street  
Hartford, CT 06106-5127

## **1.10 RETENTION OF RECORDS**

The SWPPP document will be maintained by the contractor in the appropriate construction office or location from the date the construction is initiated until the project is concluded. Records will be maintained during grading operations, construction activities either temporarily or permanently ceased, stabilization measures are initiated and final stabilization is achieved. The project owner will maintain the SWPPP for a period of three years following termination of coverage. Records to be maintained include but are not limited to:

- SWPPP and any amendments
- Copy of permit and/or certification of coverage
- General Permit Registration Form
- All reports and actions required

- Site inspection records
- Contractor certifications
- Notice of Termination

**Section 2.0  
CONSTRUCTION ACTIVITIES**

## **2.0 CONSTRUCTION ACTIVITIES**

### **2.1 DESCRIPTION OF CONSTRUCTION ACTIVITY**

Prior to construction BNE will complete all pre-construction planning activities. BNE will continue to consult with municipalities, state agencies and federal agencies, as applicable, and will conduct site surveys to determine construction methodologies and procedures to minimize adverse effects to the environment and public.

Construction will typically consist of activities such as:

- Surveys to stake access roads and structural locations
- Wetland delineation
- Geotechnical investigations
- Establishment of construction staging area
- Installation of sediment and erosion control devices
- Excavation and installation of access roads
- Excavation and installation of lay-down and equipment assembly areas
- Excavation and installation of foundations and erection of new structures
- Installation of conductors
- Restoration of site, including re-establishment of vegetative areas

### **2.2 CONSTRUCTION SITE ESTIMATES**

The following are estimates of the construction site:

Area to be disturbed: 12.91

Total Project area: 80.0 acres

Percentage impervious area before construction: 1.1%

Runoff coefficient before construction: 65

Percentage impervious area after construction: 3.45 %

Runoff coefficient after construction: 65

Summary of peak flows: See 2.3.3

Summary of groundwater recharge: 0.022 AC-FT

### **2.3 PROPOSED STORMWATER MANAGEMENT PRACTICES**

#### ***2.3.1 Stormwater Treatment Practices***

Permanent structural controls will not be required for the treatment of stormwater runoff. Following construction of the tower units, the site will be returned to pre-construction conditions. The constructed access road will remain in place; however the width will be reduced by approximately one-half. The diversion swale constructed as part of the Erosion and Sediment Control Plan will remain in place and will be converted to a water quality swale. Once site conditions and vegetation have been reestablished, stormwater discharges will return to the pre-construction state for quality and quantity.

**2.3.2 Flood Control and Peak Runoff Attenuation Management Practices**

Construction within the project area is such that flooding caused by an increase in impervious area or the reconfiguration of stormwater conveyance through the drainage area is not a primary concern. The total increase in impervious area is approximately one percent. Permanent stormwater conveyance structures such a storm drains, catch basin, and the like are not planned for this development. Upon completion of the construction of the three towers, the site will be returned to pre-construction conditions.

**2.3.3 Pre- and Post Development Stormwater Flows**

	Area (Acres)	Runoff Curve Number (CN)
Existing Drainage Area 1 -	10.61	60
Proposed Drainage Area 1 -	9.59	60
Existing Drainage Area 2 -	19.69	62
Proposed Drainage Area 2 -	19.45	63
Existing Drainage Area 3 -	6.02	57
Proposed Drainage Area 3 -	7.00	61
Existing Drainage Area 4 -	13.92	56
Proposed Drainage Area 4 -	15.08	58
Existing Drainage Area 5 -	6.71	55
Proposed Drainage Area 5 -	6.71	59

Storm Interval (DP-1)

	2yr.	10yr.	25yr.	50yr.	100yr
Existing Flow (cfs)	1.8	6.8	10.1	13.4	17.3
Proposed Flow (cfs)	1.7	6.5	9.7	12.7	16.5

Storm Interval (DP-2)

	2yr.	10yr.	25yr.	50yr.	100yr
Existing Flow (cfs)	5.0	16.5	24.1	31.2	39.7
Proposed Flow (cfs)	4.7	15.6	22.7	29.3	37.2

---

	Storm Interval (DL-3)				
	2yr.	10yr.	25yr.	50yr.	100yr
Existing Flow (cfs)	0.8	3.7	5.9	7.0	10.5
Proposed Flow (cfs)	1.1	3.6	5.4	7.1	9.5

	Storm Interval (DL-4)				
	2yr.	10yr.	25yr.	50yr.	100yr
Existing Flow (cfs)	1.5	7.5	12.1	16.5	22.0
Proposed Flow (cfs)	1.4	7.3	11.7	16.4	22.0

	Storm Interval (DL-5)				
	2yr.	10yr.	25yr.	50yr.	100yr
Existing Flow (cfs)	0.5	2.5	4.1	5.7	7.6
Proposed Flow (cfs)	0.5	2.4	4.0	5.4	7.2

**Section 3.0**  
**BEST MANAGEMENT PRACTICES**

### **3.0 BEST MANAGEMENT PRACTICES**

Soil erosion and sediment controls are measures that are used to reduce the amount of soil particles that are carried from a land area and deposited in receiving waters. This section provides a general description of the most appropriate control measures proposed for the Project. The permittee's construction contractor(s) and their subcontractors will be responsible for amending the erosion and sediment controls in the SWPPP for their portion(s) of the project. Based on field conditions at the time of construction, the contractors or subcontractors may adjust the locations and types of BMPs so that erosion and sedimentation are controlled to the maximum extent practicable. However, in no case will modifications to the SWPPP result in any less stringent erosion and sedimentation control measures than specified herein.

Any revision to the SWPPP will be recorded on the Record of Revisions form. The application of the techniques in the field will be determined by the professional judgment of the permittee's field construction personnel and will depend on site-specific conditions. All applicable soil erosion and sediment control measures will be implemented in accordance with this SWPPP and the Permit prior to commencement of field construction activities. Measures will be maintained during and after the construction activity, until final stabilization of the soil is accomplished. Upon final stabilization of disturbed areas, all temporary soil erosion and sediment control measures will be removed.

#### **3.1 STRUCTURAL CONTROL PRACTICES**

Structural control practices divert flows from exposed soils, store water flow, or otherwise limit runoff from exposed areas of the site. Such practices may include silt fences, drainage swales, sediment traps, check dams, subsurface drains, pipe slope drains, rock outlet protection (rip-rap), reinforced soil retaining systems, and temporary or permanent sediment basins. Some of these practices may be used as both temporary and permanent control measures. Structural control practices should be placed in upland areas to the degree practicable to prevent erosion and reduce sedimentation in lower elevation areas.

#### **3.2 TEMPORARY EROSION CONTROL PRACTICES**

Erosion and sediment control measures will be in place prior to the initiation of soil disturbing activities and will be maintained throughout construction. The contractor may need erosion control measures in other locations of the project as work progresses to keep sediment from leaving the construction site. These measures will be determined by the contractor in the field; if measures are changed in the field, the SWPPP must be modified accordingly. All temporary erosion controls will be removed after the protected area is finally stabilized. The minimum temporary erosion and sediment control practices that will be used for the Project are discussed in the following sections.

##### **3.2.1 Sediment Fence (GSF)**

Will retain sediment from small disturbed areas. Sediment fence will be placed along slopes as shown on construction details. The contractor will use his best judgment to install additional sediment fence as necessary to prevent loss of sediment. Refer to section 5-11 of 2002 Connecticut Guidelines for Soil Erosion and Sediment Control.



Maintenance: Inspect the silt fence at least once a week and within 24 hours of the end of a storm with a rainfall amount of 0.5 inches or greater to determine maintenance needs. When used for dewatering operations, inspect frequently before, during and after pumping operations. Remove the sediment deposits, or if room allows, install a second silt fence up slope from the existing fence when deposits reach approximately one half the height of the existing fence. Replace or repair within 24 hours of an observed failure. Refer to Connecticut Guidelines for Soil Erosion and Sediment Control figure GF-5 for troubleshooting failures. Maintain silt fence until the contributing area is stabilized.

### **3.2.2 Hay Bale Barrier (HB)**

Will retain sediment from small disturbed areas. Hay bales will be placed along slopes as shown on construction details. The contractor will use his best judgment to install additional hay bales as necessary to prevent loss of sediment. Refer to section 5-11 of 2002 Connecticut Guidelines for Soil and Sediment Control.

Maintenance: Inspect the hay bale barrier at least once a week and within 24 hours of the end of a storm with a rainfall amount of 0.5 inches or greater to determine maintenance needs. When used for dewatering operations, inspect frequently before, during and after pumping operations. Remove the sediment deposits, or if room allows, install a secondary barrier up slope from the existing barrier when deposits reach approximately one half the height of the barrier. Replace or repair within 24 hours of an observed failure. Refer to Connecticut Guidelines for Soil Erosion and Sediment Control figure HB-5 for troubleshooting failures. Maintain hay bale barrier until the contributing area is stabilized.

### **3.2.3 Stone Check Dam (SCD)**

Will be used to reduce velocity of concentrated flows, thus reducing of the drainage way.

Maintenance: Inspect the stone check dam at least once a week and within 24 hours of the end of a storm with a rainfall amount of 0.5 inches or greater to determine maintenance needs. Remove the sediment deposits when deposits reach approximately one half the height of the check dam. Replace or repair within 24 hours of an observed failure. Maintain until the contributing area is stabilized.

### **3.2.4 Temporary Pipe Slope Drain (TSD)**

Will be used to carry water over excessive changes in grade. TSD's will convey concentrated stormwater runoff flows without causing erosion problems either on or at the toe of the slope.

Maintenance: Inspect the temporary pipe slope drain at least once a week and within 24 hours of the end of a storm with a rainfall amount of 0.5 inches or greater to determine maintenance needs. Repair damage as necessary. Avoid the placement of any material on the top of the pipe and prevent vehicular traffic from crossing the slope drain.

### **3.2.5 Temporary Diversion (TD)**

Will be used to divert sediment laden runoff from a disturbed area to a sediment trapping facility.

Maintenance: When the temporary diversion is located within close proximity to on going construction activities, inspect the diversion at the end of each work day and immediately repair damage caused by construction equipment. Otherwise, inspect the temporary diversion and associated measures at least once a week and within 24 hours of the end of a storm with a rainfall amount of 0.5 inches or greater to determine maintenance needs. Repair within 24 hours of an observed failure.

### ***3.2.6 Temporary Fill Berm (TFB)***

Will be used to divert runoff from unprotected fill slopes during construction to a stabilized outlet or sediment trapping facility.

Maintenance: Inspect the temporary fill berm and associated controls at the end of each work day to ensure the criteria for installing the measures have been met. Determine if repair or modification is needed. This measure is temporary and under most situations will be covered the next work day. Maintenance requirements should be minimal. The contractor should avoid placing other material over the berm and construction traffic should not be allowed to cross.

### ***3.2.7 Temporary Sediment Trap (TST)***

Will be used to detain sediment laden runoff from small disturbed areas long enough to allow the majority of sediment to settle out.

Maintenance: Inspect the temporary sediment trap and associated controls at least once a week and within 24 hours of the end of a storm with a rainfall amount of 0.5 inches or greater to determine maintenance needs. Check the outlet to verify that it is structurally sound and has not been damaged by erosion or construction equipment. The height of the stone outlet should be maintained at least 1 foot below the crest of the embankment. When sediment has accumulated more than one quarter of the minimum wet storage volume, dewater and remove sediment as necessary to restore the trap to its original dimensions.

### ***3.2.8 Construction Entrance (CE)***

Will be used to reduce tracking of sediment off site to paved areas.

Maintenance: Maintain the entrance in a condition which will prevent tracking and washing of sediment onto paved surfaces. Provide periodic top dressing with additional stone or additional length as required. Immediately remove all sediment spilled, dropped, washed or tracked onto paved surfaces.

### ***3.2.9 Tree Protection (TP)***

Will be used to ensure the survival of existing desirable trees for their effectiveness in soil erosion and sediment control during construction.

Maintenance: Inspect tree protection zones weekly during site construction for damage to the tree crown, trunk and root system. When trees have been damaged or the protection zone has been compromised, consult an arborist licensed in CT to determine how damage should be addressed.

### **3.2.10 Temporary Erosion Control Blankets (ECB)**

Will be used to provide temporary surface protection to disturbed soils to absorb raindrop impact and to reduce sheet and rill erosion.

Maintenance: Inspect temporary erosion control blankets at least once a week and within 24 hours of the end of a storm with a rainfall amount of 0.5 inches or greater to determine maintenance needs. Repair any dislodged or failed blankets immediately.

### **3.3 SOIL STABILIZATION PRACTICES**

Soil stabilization involves covering disturbed soils with grass, mulch, straw, geotextiles, trees, vines, or shrubs. Stabilization practices for exposed disturbed soils are extremely important while conducting construction activities. Vegetative cover serves to reduce the erosion potential by absorbing the energy of raindrops, promoting infiltration in lieu of runoff, and reducing the velocity of runoff. Stabilization measures shall be initiated as soon as practicable, but no more than 14 days after construction activities have temporarily or permanently ceased on any portion of the site.

### **3.4 MAINTENANCE AND INSPECTIONS**

All erosion and sediment control devices shall be installed pursuant to the specifications in the construction details. They will be maintained so that they remain effective at all times.

Erosion and sediment control devices will be inspected by qualified personnel at least once every seven calendar days or at least once every 14 calendar days and within 24 hours of each 0.5-inch or greater rainfall event. During each inspection, the construction inspector will complete the Inspection and Maintenance Report Form located in the appendix. This form will be copied and used as necessary. Ineffective temporary erosion control measures will be repaired or replaced before the next storm event or as soon as practicable. The permittee will immediately install additional temporary erosion control devices in any area deemed in need of protection.

Following temporary or final stabilization, inspections must be conducted at least once a month. If construction has been halted due to frozen conditions, regular inspections are not mandatory until one month before the expected thaw. If vegetation establishment is not satisfactory, special steps to correct the problem will be implemented such as over seeding, mulching, sodding, or the use of erosion control blankets. Once a definable area of the construction site has been finally stabilized, no further inspection requirements apply to that area.

### **3.5 FINAL STABILIZATION**

#### **3.5.1 Seeding**

The contractor will be responsible for labor, materials, tools, equipment, and other related items required for preparing ground, providing for sowing of seeds, fertilizing, mulching and top dressing, and other management practices required for erosion control and to achieve final stabilization. It will be the contractor's responsibility to make sure that the soil seedbed is not blown, washed, or otherwise removed from the site. The contractor will make repairs (including replacement of lost topsoil and mulch) to the seedbed preparation site in the event of heavy rain,

wind, or other natural events that cause damage. When practicable, native plant species should be used for landscaping.

### ***3.5.2 Fertilizer***

Soil in areas of disturbance may need supplementation from fertilizer. Soil tests may be necessary to determine the most appropriate fertilizer for each location. Once applied, the fertilizer will be worked into the soil to limit exposure to stormwater. Fertilizer spills will be cleaned up immediately and will not be applied along or in a waterway.

### ***3.5.3 Mulching***

Mulching will be used in conjunction with both temporary and permanent seeding practices to enhance success by providing erosion protection prior to the onset of vegetative growth. Mulches enhance plant establishment by moderating soil temperatures and conserving moisture. After seeding, straw or hay mulch will be applied at a rate of two to three tons per acre on the disturbed areas. Other forms of mulch will be applied at a rate designated by the Project Engineer. Mulch will not be applied in wetlands, on lawns, and areas where hydro-mulch is used. Mulch will be anchored immediately after placement on steep slopes and stream banks. Mulch will be held in place by a very thin covering of topsoil, small brush, pins, stakes, wire mesh, asphalt binder, or other adhesive material approved by the project engineer.

### ***3.5.4 Topsoiling***

Topsoil should be applied in areas where the subsoil or existing surface soil does not provide an adequate growth medium for the desired vegetation, where soil is too shallow to provide adequate rooting depth, or where the soil contains substances toxic to the desired vegetation. Topsoil shall be reasonably free from subsoil and stumps, roots, brush, stones, and clay lumps or similar objects.

### ***3.5.5 Temporary Control Removal***

Temporary erosion controls will be left in place until the Project site is stabilized with a uniform vegetative cover of 70 percent density of the native background vegetative cover on all unpaved areas. Following re-vegetation, the permittee will conduct periodic site visits to make sure that vegetation establishment is satisfactory. If sufficient vegetative cover has not been achieved, additional restoration measures will be implemented. Inspection results will be documented using the Inspection and Maintenance Report Form found in the appendix. All temporary soil erosion and sediment control measures will be removed and disposed of after final site stabilization is achieved and before submitting the NOT.

**Section 4.0**  
**GOOD HOUSEKEEPING BMP'S**

## **4.0 GOOD HOUSEKEEPING BMP'S**

### **4.1 POTENTIAL SOURCES OF POLLUTION**

Potential exists for construction sediment to be contained in any runoff that occurs on the project site. This sediment is a result of clearing and grading activities.

### **4.2 CONTROLS TO REDUCE POLLUTION FROM THE CONSTRUCTION SITE**

Minimize Disturbed Area, Protect Natural Features, and Soil:

This project will not be mass graded. Only areas required for construction activities will be graded. This practice will reduce sediment transport into receiving bodies.

#### ***4.2.1 Material Handling and Waste Management***

The contractor will establish control measures to prevent discharge and dispose of construction and sanitary waste on site.

#### ***4.2.2 Establish Proper Building Material Staging Areas***

The contractor will establish a permanent staging area within the project site for materials and equipment storage.

#### ***4.2.3 Allowable Non-Stormwater Discharge Management***

Non-stormwater discharges are allowable provided the non-stormwater component of the discharge is in compliance applicable state regulation. Prior to any non storm discharge, the appropriate BMP will be installed and inspected.

#### ***4.2.4 Maintenance of Controls***

All erosion and sediment control practices will be checked for stability and operation following every runoff-producing rainfall, but in no case less than once every week. Any needed repairs will be made immediately to maintain all practices as designed.

All sediment control features shall be maintained until final stabilization has been obtained.

Contractor will maintain appropriate recording keepings as required by DEP-PED-GP-015. Maintenance records shall describe repair, replacement, and maintenance of BMPs undertaken based on the inspections and maintenance procedures described above and the individual requirements of the BMPs. Actions related to the findings of inspections should reference the specific inspection report. Records should describe actions taken, dates completed, and note the party that completed the work.

During construction the contractor will be responsible for maintaining integrity of all permanent and temporary structures. Prior to submittal of NOT, the contractor and owner will inspect permanent structures to remain in place and correct all noted deficiencies. Upon acceptance from contractor, the owner will maintain responsibility for inspection of the structure semi-annually.

**Section 5.0**  
**HAZARDOUS SUBSTANCE OR OIL SPILL REPORTING**

## **5.0 HAZARDOUS SUBSTANCE OR OIL SPILL REPORTING**

The Spill Prevention Control and Countermeasure Plan (SPCC), which describes measures to prevent, control, and minimize impacts from a spill of a hazardous, toxic, or petroleum substance during construction of the proposed project. This plan identifies the potentially hazardous materials to be used during this project, describes the transport, storage, and disposal procedures for these substances, and outlines the procedures to be followed in the event of a spill of a contaminating or toxic substance.

As per 40 CFR 112, a Spill Prevention Control and Countermeasures Plan (SPCC) must be prepared if the construction site will have 1,320 gallons of above ground storage capacity (or 42,000 gallons in underground storage not regulated by UST rules) or more in 55-gallon-sized (or larger) containers. This would include any temporary tanks or fueling trucks used to “store” petroleum on-site. The truck would be subject to the SPCC Plan rules when parked on the construction site and used for “storage.” If, at any time, a subcontractor’s cumulative above ground storage capacity on-site exceeds 1,320 gallons, the subcontractor shall maintain a certified SPCC Plan (40 CFR 112).

### **5.1 MATERIAL MANAGEMENT PRACTICES**

Properly managing materials on the construction site will greatly reduce the potential for stormwater pollution of materials. Good housekeeping, along with proper use and storage of construction materials, form the basis for proper management of potentially hazardous materials.

### **5.2 NON-PETROLEUM PRODUCTS**

Due to the chemical makeup of specific products, certain handling and storage procedures are required to promote the safety of handlers and prevent the possibility of pollution. Care shall be taken to follow all directions and warnings for products used on the site. All pertinent information can be found on the MSDS for each product. The MSDS will be kept on-site.

### **5.3 PETROLEUM PRODUCTS**

On-site vehicles will be monitored for leaks and receive regular maintenance to reduce the chance of leakage. Petroleum products will be stored in tightly sealed containers that are clearly labeled. Preferably, the containers will be stored in a covered truck or trailer that provides secondary containment for the products. Bulk storage tanks having a capacity of greater than 55 gallons will be provided with secondary containment. Containment can be provided by a temporary earthen berm or other means. After each rainfall event, the contractor shall inspect the contents of the secondary containment area for excess water. If no sheen is visible, the collected water can be pumped to the ground in a manner that does not cause scouring. If any sheen is present, it must be treated prior to discharging the water. Otherwise, the contaminated water must be transported and disposed off-site in accordance with local, state, and federal requirements. Bulk fuel or lubricating oil dispensers shall not have a self-locking mechanism that allows for unsupervised fueling. Fueling operations shall be observed to immediately detect and contain spills. No waste oil or other petroleum-based products will be disposed of on-site (e.g., buried, poured, etc.), but shall be taken off-site for proper disposal.



#### **5.4 SPILL CONTROL AND CLEAN UP**

In addition to the material management practices discussed previously, the following spill control and cleanup practices will be adhered to prevent stormwater pollution in the event of a spill:

- Personnel on-site will be made aware of cleanup procedures and the location of spill cleanup.
- Equipment spills will be contained and cleaned up immediately after discovery.
- Manufacturer methods for spill cleanup of a material will be followed as described on the material's MSDS.
- Materials and equipment needed for cleanup procedures will be kept readily available on the site, either at an equipment storage area or on contractor's trucks; equipment to be kept on the site will include, but not be limited to, brooms, dust pans, shovels, granular absorbents, sand, saw dust, absorbent pads and booms, plastic and metal trash containers, gloves, and goggles.
- Toxic, hazardous or petroleum product spills required to be reported by regulation will be documented to the appropriate federal, state, and local agencies.
- Spills will be documented and a record of the spills will be kept with this SWPPP.

The federal reportable spill quantity for petroleum products is defined in 40 CFR 110 as any oil spill that:

- violates applicable water quality standards;
- causes a film or sheen upon or discoloration of the water surface or adjoining shoreline; or
- causes a sludge or emulsion to be deposited beneath the surface of the water or adjoining shorelines.

**Section 6.0  
SWPPP APPENDICES**

## **6.0 SWPPP APPENDICES**

Attach the following documentation to the SWPPP in the following appendices.

### Appendix A – Permit Coverage

- Submitted General Permit Registration Form and Transmittal
- Issued CT Letter of Coverage
- Other applicable permits

### Appendix B – Certifications

- Preparer
- Permittee or Co-Permittee
- Operator
- Inspector

Appendix C – Pre-Construction Meeting – Items to be added upon completion of meeting includes:

- Agenda
- Attendees
- Minutes

### Appendix D – Maps and Drawings

- Site Maps
- Site Plan

### Appendix E – Construction Records

- Construction Activities and Control Installation Log

### Appendix F – Inspection and Maintenance Records

- Inspection & Maintenance Log
- Inspection Report
- Maintenance Report

### Appendix G – Hazardous Material or Oil Spill Records

- Spill Report

Appendix H – Update Records

- Plan Update Description
- Plan Update Log

Appendix I – Copy of CT DEP Notice of Termination (Form DHEC 2610, 04/1998)

Appendix J – Connecticut General Permit for the Discharge of Stormwater and Dewatering Wastewaters Associated with Construction Activities (DEP-PED-GP-015)

Appendix K – Supporting Calculations

**APPENDIX A  
PERMIT COVERAGE**



## General Permit Registration Form for the Discharge of Stormwater and Dewatering Wastewaters from Construction Activities

Please complete this form in accordance with the general permit (DEP-PED-GP-015) in order to ensure the proper handling of your registration. Print or type unless otherwise noted. You must submit the *Permit Application Transmittal Form* (DEP-APP-001) and the registration fee along with this form.

DEPUSEONLY
Application No. _____
Permit No. _____
Facility I. <input type="checkbox"/> _____

**Part 1: Registration Type**

Enter a check mark  in the appropriate box identifying the registration type.

This registration is for (check one): <input type="radio"/> A new general permit registration <input type="radio"/> A modification of an existing general permit	Please <input type="checkbox"/> identify any existing permit number in the space provided  Existing permit number: GSN
--	---

**Part II: Fee Information**

<input type="radio"/> <i>Registration only</i>	A registration fee of \$625.00 is to be submitted with <i>each</i> registration that you are submitting at least 30 days before the initiation of construction activities.
<input type="radio"/> <i>Registration and Plan Review</i>	All construction projects that result in the disturbance of ten or more acres require the submittal of a Stormwater Pollution Control Plan and a \$625.00 plan review fee. The plan and the fee must be submitted 30 days prior to initiation of the construction activity. \$625.00 registration fee + \$625.00 review fee = \$1,250.00 total fee
For municipalities, a 50% discount applies. The registration will not be processed without the fee. The fee shall be non-refundable and shall be paid by certified check or money order payable to the Department of Environmental Protection.	

**Part III: Registrant Information**

1. Fill in the name of the registrant(s) as indicated on the <i>Permit Application Transmittal Form</i> (DEP-APP-001) Registrant: Phone: _____ ext _____ Fax _____
<input type="radio"/> Check here if there are co-registrants. If so, label and attach additional sheet(s) with the required information as supplied above.

**Part III: Registrant Information (cont.)**

2. List primary contact for departmental correspondence and inquiries, if different than the registrant.			
Name:			
Mailing Address:			
City/Town:	State:	Zip Code:	
Business Phone:	ext.	Fax:	
Site Phone:	Emergency Phone:		
Contact Person:	Title:		
Association (e.g. developer, general or site contractor, etc.):			
3. List owner of the property on which the activity will take place, if different from registrant: Name:			
Mailing Address:			
City/Town:	State:	Zip Code:	
Business Phone:	ext.	Fax:	
Contact Person:	Title:		
4. List developer, if different from registrant or primary contact:			
Name:			
Mailing Address:			
City/Town:	State:	Zip Code:	
Business Phone:	ext.	Fax:	
Contact Person:	Title:		
5. Name and address of general contractor:			
Name:			
Mailing Address:			
City/Town:	State:	Zip Code:	
Business Phone:	ext.	Fax:	
Site Phone:	Off-hours Phone:		
Contact Person:	Title:		
6. List any engineer(s) or other consultant(s) employed or retained to assist in preparing the registration and Stormwater Pollution Plan.			
<input type="radio"/> Check here if additional sheets are necessary, and label and attach them to this sheet			
Name:			
Mailing Address:			
City/Town:	State:	Zip Code:	
Business Phone:	ext.	Fax:	
Contact Person:	Title:		
Service Provided:			

**Part IV: Site Information**

1. Site or Project Name (if any): Street Address or Description of Location:			
City/Town:	State:	Zip Code:	
2. Brief description of construction activity:			
3. Start Date:	Anticipated Completion Date:		
4. Estimated total number of acres to be disturbed:			

**Part V: Stormwater Discharge Information**

1. Where does stormwater discharge to: <input type="radio"/> Municipal Separate Storm System? <input type="radio"/> Yes <input type="radio"/> No (Name): <input type="radio"/> Surface water body or wetlands? <input type="radio"/> Yes <input type="radio"/> No (Name):	
2. Is the discharge located less than 500 feet from a tidal wetland, which is not a fresh-tidal wetland? <input type="radio"/> Yes <input type="radio"/> No	
3. Name of the watershed where the site is located OR nearest waterbody to which it discharges:	
4. Is construction in accordance with the Guidelines established under Section 22a-329 of the Soil Erosion and Sedimentation Act? <input checked="" type="radio"/> Yes <input type="radio"/> No	
5. Is construction in accordance with local soil erosion and sediment ordinances? <input checked="" type="radio"/> Yes <input type="radio"/> No Note: A copy of this registration and the Stormwater Pollution Control Plan must be available to the town wetlands enforcement officials, wetlands commission, or their equivalent.	
6. Will the construction project disturb over ten acres? <input type="radio"/> Yes <input type="radio"/> No If yes, enclose a copy of the Stormwater Pollution Control Plan and plan review fee.	
7. Has the construction project been reviewed for compliance with the following DEP programs? a. Coastal Management Act (Section 22a-92 of the Connecticut General Statutes) <input type="radio"/> Yes <input type="radio"/> No b. Endangered and Threatened Species (Section 26-306 of the Connecticut General Statutes) <input type="radio"/> Yes <input type="radio"/> No c. State and Federal Historic Preservation statutes? <input type="radio"/> Yes <input type="radio"/> No	



**Part VI: Supporting Documents**

Check the box by the attachments being submitted as verification that all applicable attachments have been submitted with this registration form. When submitting any supporting documents, please label the documents as indicated in this part (e.g., Attachment A, etc.) and be sure to include the registrant's name as indicated on the *Permit Application Transmittal Form*.

<b>D</b>	Attachment A:	An 8 1/2" x 11" copy of the relevant portion or a full-sized original of a USGS Quadrangle Map indicating the exact location of the facility or site. Indicate the quadrangle name on the map. (To obtain a copy of the relevant USGS Quadrangle Map, call your town hall or DEP Maps and Publications Sales at 860-424-3555)
<b>D</b>	Attachment 8:	A copy of the Stormwater Pollution Control Plan and plan review fee of \$500.00, if the construction project disturbs over 10 acres

**Part VII: Environmental Professional Certification**

The following certification must be signed by a professional engineer, licensed to practice in Connecticut.

<p>"I certify that I have thoroughly and completely reviewed the Stormwater Pollution Control Plan for the site. I further certify, based on such review and in my professional judgment, that the Stormwater Pollution Control Plan has been prepared in accordance with the Connecticut Guidelines for Soil Erosion and Sediment Control, as amended, and the conditions for the General Permit for the Discharge of stormwater and Dewatering Wastewaters from Construction Activities and the controls required for such Plan are appropriate for the site. I am aware that there are significant penalties for false statements in this certification, including the possibility of fine and imprisonment for knowingly making false statements."</p>	
Signature of Professional Engineer	Date
Name of Professional Engineer (print or type)	P. E. Number (if applicable)
Affix P. E. Stamp Here	
<div style="border: 1px solid black; width: 150px; height: 100px; margin: 0 auto;"></div>	

**Part VIII: Registrant Certification**

The registrant *and* the individual(s) responsible for actually preparing the registration must sign this part. A registration will be considered incomplete unless all required signatures are provided.

<p>"I have personally examined and am familiar with the information submitted in this document and all attachments thereto, and I certify that, based on reasonable investigation, including my inquiry of those individuals responsible for obtaining the information, the submitted information is true, accurate and complete to the best of my knowledge and belief. I certify that this general permit registration is on complete and accurate forms as prescribed by the commissioner without alteration of the text. I understand that a false statement made in the submitted information may be punishable as a criminal offense, in accordance with section 22a-6 of the Connecticut General Statutes, pursuant to section 53a-157b of the Connecticut General Statutes, and in accordance with any other applicable statute.</p> <p>I also certify under penalty of law that I have read and understand all conditions of the General Permit for the Discharge of Stormwater and Dewatering Wastewaters from Construction Activities, that all conditions for eligibility for authorization under the general permit are met, all terms and conditions of the general permit are being met for all discharges which have been initiated and are the subject of this registration, and that a system is in place to ensure that all terms and conditions of this general permit will continue to be met for all discharges authorized by this general permit at the site. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowingly making false statements."</p>	
<p>_____ Signature of Registrant</p>	<p>_____ Date</p>
<p>_____ Name of Registrant (print or type)</p>	<p>_____ Title (if applicable)</p>
<p>_____ Signature of Preparer (if different than above)</p>	<p>_____ Date</p>
<p>_____ Name of Preparer (print or type)</p>	<p>_____ Title (if applicable)</p>
<p><input type="checkbox"/> Check here if additional signatures are necessary.</p>	

If so, please reproduce this sheet and attach signed copies to this sheet.

Note: Please submit the *Permit Application Transmittal Form*, the Registration Form, Fee(s), and all Supporting Documents to:

CENTRAL PERMIT PROCESSING UNIT  
DEPARTMENT OF ENVIRONMENTAL PROTECTION  
79 ELM STREET  
HARTFORD, CT 06106-5127

Note: If discharging to municipal separate storm sewer, send a copy of this completed registration form to the owner or operator of that system.

If discharging to a public drinking water supply watershed or aquifer area, send a copy of this completed registration form to the appropriate water company.



STATE OF CONNECTICUT  
DEPARTMENT OF ENVIRONMENTAL PROTECTION  
Central Permit Processing Unit  
79 Elm Street  
Hartford, CT 06106-5127

CPPU USE ONLY
App#: _____
Doc#: _____
Check#: _____

## Permit Application Transmittal Form

*Please complete this transmittal form in accordance with the instructions in order to ensure the proper handling of your application(s) and the associated fee(s). Print legibly or type.*

### Part I: Applicant Information:

- *\*If an applicant is a corporation, limited liability company, limited partnership, limited liability partnership, or a statutory trust, it must be registered with the Secretary of State. If applicable, applicants name shall be stated exactly as it is registered with the Secretary of State.*
- *If an applicant is an individual, provide the legal name (include suffix) in the following format: First Name; Middle Initial; Last Name; Suffix (Jr, Sr, II, III, etc.).*

Applicant:				
Mailing Address:				
City/Town	State	Zip Code		
Business Phone:	ext.:	Fax:		
Contact Person:	Phone:	ext.		
E-Mail:				
Applicant (check one): <input type="radio"/> individual <input type="radio"/> *company <input type="radio"/> federal gov't <input type="radio"/> state agency <input type="radio"/> municipality				
*If a company, list company type (e.g., corporation, limited partnership, etc):				
<input type="checkbox"/> Check if any co-applicants. If so, attach additional sheet(s) with the required information as supplied				
above. Please provide the following information to be used for billing purposes only, if different				
Company/Individual Name:				
Mailing Address:				
City/Town	State	Zip Code		
Contact Person:	Phone:	ext.		

### Part II: Project Information

Brief Description of Project: <i>(Example: Development of a 50 slip marina on Long Island Sound)</i>					
Location (City/Town):					
Other Project Related Permits <i>(not included with this form)</i> :					
Permit Description	Issuing Authority	Submittal Date	Issuance Date	Denial Date	Permit#

Part III: Individual Permit Application and Fee Information

New, Mod. or Renew	Individual Permit Applications	Initial fees	No. of Permits Applied For	Total Initial Fess	Original + Required Copies
<b>AIR EMISSIONS</b>					
	New Source Review	\$940.00			1+0
	New Source Review	none			1+0
	Title V Operating Permits	none			1+0
	Clean Air Interstate Rule (CAIR)	none			1+0
<b>WATER DISCHARGES</b>					
	To Groundwater	\$1300.00			1+1
	To Sanitary Sewer (POTW)	\$1300.00			1+1
	To Surface Water (NPDES)	\$1300.00			1+2
<b>INLAND WATER RESOURCE-multiple permits 1+6 total copies</b>					
	Dam Construction	none			1+2
	Flood Management Certification	none			1+1
	Inland 401 Water Quality Certification	none			1+5
	Inland Wetlands and Watercourses	none			
	Stream channel Encroachment Lines	★			
	Water Diversion	★			1+5
<b>OFFICE OF LONG ISLAND SOUND PROGRAMS</b>					
	Certificate of Permission	\$375.00			1+3
	Coastal 401 Water Quality Certification	none			1+3
	Structures and Dredging/Tidal Wetlands	\$660.00			1+3
<b>WASTE MANAGEMENT</b>					
	Aerial Pesticide Applications	★			1+3
	Aquatic Pesticide Application	\$200.00			1+0
	CGS Section 22a-454 Waste Facilities	★			1+1
	Hazardous Waste Treatment, Storage and Disposal Facilities	★			1+1
	Marine Terminal License	\$125.00			1+0
	Stewardship	\$4000.00			1+1
	Solid Waste Facilities	★			1+1
	Waste Transportation	★			1+0
				Subtotals →	
GENERAL PERMITS and AUTHORIZATIONS		Subtotals Page 3 →			
Enter subtotals from Part IV, pages 3 & 4&5 of this form		Subtotals Page 4 →			
		Subtotals Page 5 →			
				Total →	
<input type="checkbox"/> Indicate whether municipal discount or state waiver applies. Less Applicable Discount →					
				AMOUNT REMITTED →	
CHECK # →	<input type="text"/>	Check or money order should be made payable to: "Department of Energy and Environmental Protection"			

★ See fee schedule on individual application.

**Part IV: General Permit Registrations and Requests for Other Authorizations  
Application and Fee Information**

v" General Permits and other Authorizations	Initial Fees	No. of Permits Applied For	Total Initial Fees	Original+ Required Copies
<b>AIR EMISSIONS</b>				
<input type="radio"/> Limit Potential to Emit from Major Stationary Sources of Air Pollution	\$5000.00			1+0
<input type="radio"/> Ionizing Radiation Registration	\$200.00			1+0
<input type="radio"/> Emergency/Temporary Authorization	<b>**</b>			<b>**</b>
<input type="radio"/> Other, (please specify):				
<b>WATER DISCHARGES</b>				
<input type="radio"/> Domestic Sewage	\$500.00			1+0
<input type="radio"/> Food Processing Wastewater	\$500.00			1+0
<input type="radio"/> Groundwater Remediation Wastewater to a Sanitary Sewer	\$500.00			1+0
<input type="radio"/> Groundwater Remediation Wastewater to a Surface Water Registration Only	\$625.00			1+0
<input type="radio"/> Approval of Registration by DEP	\$1250.00			
<input type="radio"/> Hydrostatic Pressure Testing Wastewater Registration Only	\$625.00			1+0
<input type="radio"/> Approval of Registration by DEP (natural gas pipelines)	\$1250.00			
<input type="radio"/> Miscellaneous Discharges of Sewer Compatible Wastewater Flow<5,000 gpd and fire sprinkler system test water	\$500.00			1+1
<input type="radio"/> Flow>5,000 gpd	\$1000.00			
<input type="checkbox"/> Non-Contact Cooling and Heat Pump Water (Minor)	\$625.00			1+1
<input type="radio"/> Photographic Processing Wastewater (Minor)	\$100.00			1+0
<input type="radio"/> Printing & Publishing Wastewater (Minor) Flow<40 gpd	\$500.00 \$100.00			1+0
<input type="radio"/> Stormwater Associated with Commercial Activities	\$500.00			1+0
<input type="radio"/> Stormwater Associated with Industrial Activities	\$500.00			1+0
<input type="radio"/> Stormwater & Dewatering Wastewaters-Construction Activities 5 -10 acres	\$625.00			1+0
<input type="radio"/> > 10 acres	\$1250.00			
<input type="radio"/> Stormwater from Small Municipal Separate Storm Sewer Systems (MS4)	\$250.00			1+0
<input type="radio"/> Swimming Pool Wastewater - Public Pools and Contractors	\$500.00			1+0
<input type="radio"/> Tumbling or Cleaning of Parts Wastewater (Minor)	\$1000.00			1+1
<input type="radio"/> Vehicle Maintenance Wastewater Registration Only	\$500.00			1+0
<input type="radio"/> Approval of Registration by DEP	\$1000.00			
<input type="radio"/> Water Treatment Wastewater	\$625.00			1+0
<input type="radio"/> Emergency/Temporary Authorization - Discharge to POTW	\$1500.00			1+0
<input type="radio"/> Emergency/Temporary Authorization - Discharge to Surface Water	\$1500.00			1+0
<input type="radio"/> Emergency/Temporary Authorization - Discharge to Groundwater	\$1500.00			1+0
<input type="radio"/> Other, (please specify):				

Note: Carry subtotals over to Part III, page 2 of this form. Subtotal - -

**\*\***

Contact the specific permit program for this information (Contact numbers are provided in the instructions).

Part IV: General Permit Registrations and Requests for Other Authorizations (continued)

./ General Permits and Other Authorizations	Initial Fees	No. of Permits Applied For	Total Initial Fee	Original+ Required Copies
<b>AQUIFER PROTECTION PROGRAM</b>				
<input type="radio"/> Registration for Regulated Activities	\$625.00			1+0
<input type="radio"/> Permit Application to Add a Regulated Activity	\$1250.00			1+0
<input type="radio"/> Exemption Application from Registration	\$1250.00			1+0
<b>INLAND WATER RESOURCES</b>				
<input type="radio"/> Dam Safety Repair and Alteration	\$1000.00			1+2
<input type="radio"/> Diversion of Water for Consumptive Use: Reauthorization Categories	\$1000.00			1+2
<input type="radio"/> Diversion of Water for Consumptive Use: Authorization Required	\$2500.00			1+5
<input type="radio"/> Diversion of Water for Consumptive Use: Filing Only	\$1500.00			1+4
<input type="radio"/> Habitat Conservation	\$1000.00			1+2
<input type="radio"/> Lake, Pond and Basin Dredging	\$1000.00			1+2
<input type="radio"/> Minor Grading	\$1000.00			1+2
<input type="radio"/> Minor Structures	\$1000.00			1+2
<input type="radio"/> Utilities and Drainage	\$1000.00			1+2
<input type="radio"/> Emergency/Temporary Authorization	**			**
<input type="radio"/> Other, (please specify):				
<b>OFFICE OF LONG ISLAND SOUND PROGRAMS</b>				
<input type="radio"/> 4/40 Docks	\$700.00			1+1
<input type="radio"/> Beach Grading	\$100.00			1+1
<input type="radio"/> Coastal Remedial Activities Required by Order	\$700.00			1+1
<input type="radio"/> Marina and Mooring Field Reconfiguration	\$700.00			1+1
<input type="radio"/> Non-harbor Moorings	\$100.00			1+1
<input type="radio"/> Osprey Platforms and Perch Poles	none			1+1
<input type="radio"/> Pump-out Facilities (no fee for Clean Vessel Act grant recipients)	\$100.00			1+1
<input type="radio"/> Removal of Derelict Structures	\$100.00			1+1
<input type="radio"/> Residential Flood Hazard Mitigation	\$100.00			1+1
<input type="radio"/> Swim Floats	\$100.00			1+1
<input type="radio"/> Emergency/Temporary Authorization	**			**
<input type="radio"/> Other, (please specify):				
Note: Carry subtotals over to Part III, page 2 of this form.		Subtotal ...		

\*See fee schedule on registration/application. \*\*Contact the specific permit program for this information.

Part IV: General Permit Registrations and Requests for Other Authorizations (continued)

General Permits and Other Authorizations	Initial Fees	No. of Permits Applied For	Total Initial Fee	Original + Required Copies
<b>WASTE MANAGEMENT</b>				
D Addition of Grass Clippings at Registered Leaf Composting Facilities	\$500.00			1+0
D Asbestos Disposal Authorization Certain Recycling Facilities	\$300.00			1+0
D Drop-site Recycling Facility	\$200.00			1+0
D Limited Processing Recycling Facility	\$500.00			1+0
D Recyclables Transfer Facility	\$500.00			1+0
D Single Item Recycling Facility	\$500.00			1+0
D Contaminated Solids and/or Staging Management (Staging/Transfer) Registration Only	\$250.00			1+0
D Approval of Registration by DEP	\$1500.00			1+0
D Connecticut Solid Waste Demonstration Project	\$1000.00			1+0
O Disassembling Used Electronics	\$400.00			1+0
D Leaf Composting Facility	none			1+1
O Municipal Transfer Station	\$800.00			1+1
O One Day Collection of Certain Wastes and Household Hazardous Waste	\$1000.00			1+0
D Special Waste Authorization	\$660.00			1+0
D storage and Distribution of 12 1/2 Inch Nominal Tire Chip Aggregate	\$500.00			1+0
D storage and Processing of Asphalt Roofing Shingle Waste and/or storage and Distribution of Ground Asphalt Aggregate	---			1+0
D storage and Processing of Scrap Tires for Beneficial Use	\$1000.00			1+0
O Emergency/Temporary Authorization	---			---
D Other (please specify):  Remediation				
D In Situ Groundwater Remediation: Enhance Aerobic Biodegradation	---			1+2

Note: Carry subtotals over to Part III, page 2 of this form. Subtotal ●

\*See fee schedule on registration/application.      \*\*Contact the specific permit program for this information.

In conformance with the ADA, individuals with disabilities who need information in an alternative format to allow them to benefit and/or participate in the agency's programs and services, should call 860-424-3051 or 860-418-5937, or e-mail Marcia Z. Bonitto, ADA Coordinator at Marcia.Bonitto@ct.gov.



## Applicant Compliance Information

DEP ONLY	
App. No.	-----
Co./Ind. No.	-----

Applicant Name:  
(as indicated on the *Permit Application Transmittal Form*)

If you answer yes to any of the questions below, you must complete the Table of Enforcement Actions on the reverse side of this sheet as directed in the instructions for your permit application.

- A. During the five years immediately preceding submission of this application, has the applicant been convicted in any jurisdiction of a criminal violation of any environmental law?
- Yes       No
- B. During the five years immediately preceding submission of this application, has a civil penalty been imposed upon the applicant in any state, including Connecticut or federal judicial proceeding for any violation of an environmental law?
- Yes       No
- C. During the five years immediately preceding submission of this application, has a civil penalty exceeding five thousand dollars been imposed on the applicant in any state, including Connecticut, or federal administrative proceeding for any violation of an environmental law?
- Yes       No
- D. During the five years immediately preceding submission of this application, has any state, including Connecticut, or federal court issued any order or entered any judgment to the applicant concerning a violation of any environmental law?
- Yes       No
- E. During the five years immediately preceding submission of this application, has any state, including Connecticut, or federal administrative agency issued any order to the applicant concerning a violation of any environmental law?
- Yes       No



Table of Enforcement Actions

(1) Type of Action	(2a) Date Commenced	(2b) Date Terminated	(3) Jurisdiction	(4) Case/Docket/ Order No.	(5) Description of Violation



## Applicant Background Information

Please enter a check mark by the entity which best describes the applicant and complete the requested information. **You must choose one of the following.**

**Corporation**

1. Parent Corporation

Name:

Mailing Address:

City/town:

State:

Zip Code:

Business Phone:

ext.

Fax:

Contact Person:

Phone:

2. Subsidiary Corporation:

Name:

Mailing Address:

City/town:

State:

Zip Code:

Business Phone:

ext.

fax:

Contact Person:

Phone:

3. Directors:

Name:

Mailing Address:

City/town:

State:

Zip Code:

Business Phone:

ext.

Fax:

Name:

Mailing Address:

City/town:

State:

Zip Code:

Business Phone:

ext.

Fax:

Please enter a check mark, if additional sheets are necessary. If so, label and attach additional sheet(s) to this sheet with the required information as supplied above.

4. Officers:

Name:

Mailing Address:

City/town:

State:

Zip Code:

Business Phone:

ext.

Fax:

Please enter a check mark, if additional sheets are necessary. If so, label and attach additional sheet(s) to this sheet with the required information as supplied above.

**Applicant Background Information (continued)**

**Limited Liability Company**

1. List each member.

Name:

Mailing Address:

City/Town:

State:  
ext.

Zip Code:

Business Phone:

Fax:

Name:

Mailing Address:

City/Town:

State:

Zip Code:

Business Phone:

ext.

Fax:

Name:

Mailing Address:

City/Town:

State:

Zip Code:

Business Phone:

ext.

Fax:

Please enter a check mark, if additional sheets are necessary. If so, label and attach additional sheet(s) to this sheet with the required information as supplied above.

2. List any manager(s) who, through the articles of organization, are vested the management of the business, property and affairs of the limited liability company.

Name:

Mailing Address:

City/Town:

State:

Zip Code:

Business Phone:

ext.

Fax:

Name:

Mailing Address:

City/Town:

State:

Zip Code:

Business Phone:

ext.

Fax:

Name:

Mailing Address:

City/Town:

State:

Zip Code:

Business Phone:

ext.

Fax:

Please enter a check mark, if additional sheets are necessary. If so, label and attach additional sheet(s) to this sheet with the required information as supplied above.

**Applicant Background Information (continued)**

**Limited Partnership**

1.	General Partners:		
	Name:		
	Mailing Address:		
	City/Town:	State:	Zip Code:
	Business Phone:	ext.	Fax:
	Name:		
	Mailing Address:		
	City/Town:	State:	Zip Code:
	Business Phone:	ext.	Fax:
	Name:		
	Mailing Address:		
	City/Town:	State:	Zip Code:
	Business Phone:	ext.	Fax:
	<input type="checkbox"/> Please enter a check mark, if additional sheets are necessary. If so, label and attach additional sheet(s) to this sheet with the required information as supplied above.		
2.	Limited Partners:		
	Name:		
	Mailing Address:		
	City/Town:	State:	Zip Code:
	Business Phone:	ext.	Fax:
	Name:		
	Mailing Address:		
	City/Town:	State:	Zip Code:
	Business Phone:	ext.	Fax:
	Name:		
	Mailing Address:		
	City/Town:	State:	Zip Code:
	Business Phone:	ext.	Fax:
	<input type="checkbox"/> Please enter a check mark, if additional sheets are necessary. If so, label and attach additional sheet(s) to this sheet with the required information as supplied above.		

**Applicant Background Information (continued)**

**General Partnership**

1.	General Partners:			
	Name:			
	Mailing Address:			
	City/Town:	State:	Zip Code:	
	Business Phone:	ext.	Fax:	
	Name:			
	Mailing Address:			
	City/Town:	State:	Zip Code:	
	Business Phone:	ext.	Fax:	
	Name:			
	Mailing Address:			
	City/Town:	State:	Zip Code:	
	Business Phone:	ext.	Fax:	
	Name:			
	Mailing Address:			
	City/Town:	State:	Zip Code:	
	Business Phone:	ext.	Fax:	
	Name:			
	Mailing Address:			
	City/Town:	State:	Zip Code:	
	Business Phone:	ext.	Fax:	
	Name:			
	Mailing Address:			
	City/Town:	State:	Zip Code:	
	Business Phone:	ext.	Fax:	
	<input type="checkbox"/> Please enter a check mark, if additional sheets are necessary. If so, label and attach additional sheet(s) to this sheet with the required information as supplied above.			

**Applicant Background Information (continued)**

**Voluntary Association**

1. List authorized persons of association or list all members of association.

Name:  
Mailing Address:  
City/Town: State: Zip Code:  
Business Phone: ext. Fax:

Name:  
Mailing Address:  
City/Town: State: Zip Code:  
Business Phone: ext. Fax:

Name:  
Mailing Address:  
City/Town: State: Zip Code:  
Business Phone: ext. Fax:

Name:  
Mailing Address:  
City/Town: State: Zip Code:  
Business Phone: ext. Fax:

Please enter a check mark, if additional sheets are necessary. If so, label and attach additional sheet(s) to this sheet with the required information as supplied above.

**Individual or Other Business Type**

1. Name:  
Mailing Address:  
City/Town: State: Zip Code:  
Business Phone: ext. Fax:

2. State other names by which the applicant is known, including business names.  
Name:

Please enter a check mark, if additional sheets are necessary. If so, label and attach additional sheet(s) to this sheet with the required information as supplied above.

**APPENDIX B  
CERTIFICATIONS**

**PREPARER'S CERTIFICATION**

Project:	Wind Colebrook South
Project Location:	29 Flagg Hill Road Colebrook, Connecticut
Permittee:	BNE Energy
	29 South Main Street Town Center Suite 200 West Hartford, CT 06107 (800) 450-0503
Contractor:	To Be Determined
Preparer:	Shane Smith, PE
	Zapata Incorporated 6302 Fairview Road, Suite 600 Charlotte, North Carolina 28210
Phone:	704-358-8240
Fax:	704-358-8342

**Certification Statement:**

I certify that I have thoroughly and completely reviewed the Stormwater Pollution Control Plan for the site. I further certify, based on such review and in my professional judgment, that the Stormwater Pollution Control Plan has been prepared in accordance with the Connecticut Guidelines for Soil Erosion and Sediment Control, as amended, and the conditions for the General Permit for the Discharge of Stormwater and Dewatering Wastewaters from Construction Activities issued on October 1, 2002 (or as reissued or modified), and the controls required for such Plan are appropriate for the site. I am aware that there are significant penalties for false statements in this certification, including the possibility of fine and imprisonment for knowingly making false statements.

Name:	Shane Smith, PE
Company:	Zapata Incorporated
Title:	Civil Engineer
Signature:	
Date:	



**CONTRACTOR / CO-PERMITTEE CERTIFICATION**

Project:	Wind Colebrook South
Project Location:	29 Flagg Hill Road Colebrook, Connecticut
Contractor:	
Address:	
Phone:	
Fax:	

**Certification Statement:**

I certify by my signature below that I participated in a pre-construction conference with the individual who is responsible for the operational control of this Stormwater Pollution Prevention Plan (SWPPP). I accept the terms and conditions of this SWPPP as required by the general National Pollutant Discharge Elimination System issued to the Owner/Operator of the construction activity for which I have been contracted to perform construction related professional services. Further, by my signature below, I understand that I am becoming a Co-permittee with the Owner/Operator and other contractors that have become Co-permittees to the general NPDES permit issued to the Owner/Operator of the facility for which I have been contracted to perform professional construction services. As a Co-permittee, I understand that I, and my company, as the case may be, am legally accountable to the Connecticut Department Environmental Protection to ensure compliance with the terms and conditions of this SWPPP. I also understand that DEP enforcement actions may be taken against any specific Co-permittee or combination of Co-permittees if the terms and conditions of this SWPPP are not met. Therefore, having understood the above information, I am signing this certification and am receiving Co-permittee status to the aforementioned general NPDES permit.

**Company Official's Signature:**

Name: \_\_\_\_\_ Title: \_\_\_\_\_  
               (Please print)   (Please print)

Signature: \_\_\_\_\_ Date: \_\_\_\_\_

**CONTRACTOR / OPERATOR CERTIFICATION**

Project:	Wind Colebrook South
Project Location:	29 Flagg Hill Road Colebrook, Connecticut
Contractor:	
Address:	
Phone:	
Fax:	

**Certification Statement:**

I have personally examined and am familiar with the information submitted in this document and all attachments thereto, and I certify that, based on reasonable investigation, including my inquiry of those individuals responsible for obtaining the information, the submitted information is true, accurate and complete to the best of my knowledge and belief. I certify that this permit registration is on complete and accurate forms as prescribed by the commissioner without alteration of the text. I understand that a false statement made in the submitted information may be punishable as a criminal offense, in accordance with Section 22a-6 of the Connecticut General Statutes, pursuant to Section 53a-157b of the Bureau of Materials Management & Compliance Assurance DEP-PED-GP-015 10 of 24 Connecticut General Statutes, and in accordance with any other applicable statute. I also certify under penalty of law that I have read and understand all conditions of the General Permit for the Discharge of Stormwater and Dewatering Wastewaters from Construction Activities issued on October 1, 2002 (or as reissued or modified), that all conditions for eligibility for authorization under the general permit are met, all terms and conditions of the general permit are being met for all discharges which have been initiated and are the subject of this registration, and that a system is in place to ensure that all terms and conditions of this general permit will continue to be met for all discharges authorized by this general permit at the site. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowingly making false statements.

**Corporate Official's Signature:**

Name: \_\_\_\_\_ Title: \_\_\_\_\_  
(Please print) (Please print)

Signature: \_\_\_\_\_ Date: \_\_\_\_\_

**INSPECTOR CERTIFICATION**

Project:	Wind Colebrook South
Project Location:	29 Flagg Hill Road Colebrook, Connecticut
Contractor:	
Address:	
Phone:	
Fax:	

**Certification Statement:**

I certify that I have thoroughly and completely reviewed the Stormwater Pollution Control Plan for the site. I further certify, based on such review and in my professional judgment, that the Stormwater Pollution Control Plan has been prepared in accordance with the Connecticut Guidelines for Soil Erosion and Sediment Control, as amended, and the conditions for the General Permit for the Discharge of Stormwater and Dewatering Wastewaters from Construction Activities issued on October 1, 2002 (or as reissued or modified), and the controls required for such Plan are appropriate for the site. I am aware that there are significant penalties for false statements in this certification, including the possibility of fine and imprisonment for knowingly making false statements.

**Inspector's Signature:**

Name: \_\_\_\_\_ Title: \_\_\_\_\_  
(Please print) (Please print)

Signature: \_\_\_\_\_ Date: \_\_\_\_\_

**APPENDIX C  
PRE-CONSTRUCTION MEETING**


Although a pre-construction meeting is not a requirement for this CGP, a meeting will be conducted. A copy of this documentation should be kept in this appendix.

**APPENDIX D MAPS  
AND DRAWINGS**







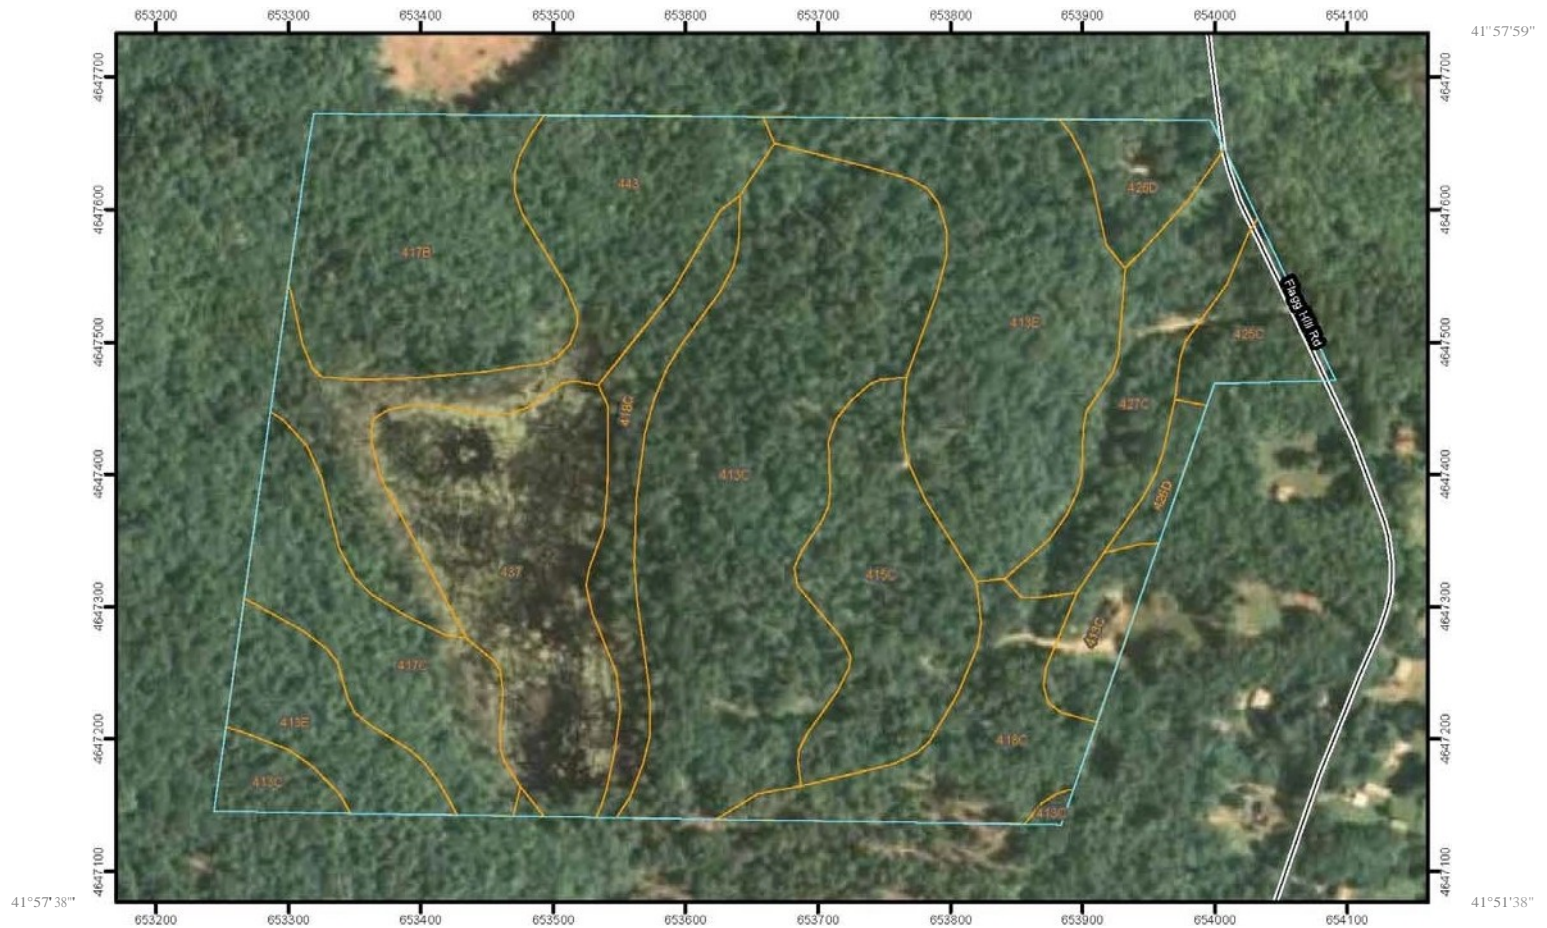






























Stormwater Management Pkm with  
Stormwater Pollution Prevention Plan (SWPPP)  
Wind Colebrook South  
Colebrook, Connecticut



Soil Map-State of Connecticut  
(Wind Colebrook South)



Soil Map-State of Connecticut  
(Wind Colebrook South)

<h3 style="text-align: center;">MAP LEGEND</h3> <p><b>Area of Interest (AOI)</b>   Area of Interest (AOI)</p> <p><b>Soils</b>   Soil Map Units</p> <p><b>Special Point Features</b>   Blowout   Borrow Pit   Clay Spot   Closed Depression   Gravel Pit   Gravelly Spot   Landfill   Lava Flow   Marsh or swamp   Mine or Quarry   Miscellaneous Water   Perennial Water   Rock Outcrop   Saline Spot   Sandy Spot   Severely Eroded Spot   Sinkhole   Slide or Slip   Sodic Spot   Spoil Area   Stony Spot</p>	<p> Very Stony Spot   Wet Spot   Other</p> <p><b>Special Line Features</b>   Gully   Short Steep Slope   Other</p> <p><b>Political Features</b>   Cities</p> <p><b>Water Features</b>   Oceans   Streams and Canals</p> <p><b>Transportation</b>   Rails   Interstate Highways   US Routes   Major Roads   Local Roads</p>
<h3 style="display: inline-block; width: 45%;">MAP INFORMATION</h3>	
<p>Map Scale: 1:4,700 if printed on A size (8.5" x 11") sheet.</p> <p>The soils surveys that comprise your AOI were mapped at 1:12,000.</p> <p>Please rely on the bar scale on each map sheet for accurate map measurements.</p> <p>Source of Map: Natural Resources Conservation Service          Web Soil Survey URL: <a href="http://websoilsurvey.nrcs.usda.gov">http://websoilsurvey.nrcs.usda.gov</a>          Coordinate System: UTM Zone 18N NAD83</p> <p>This product is generated from the USDA-NRCS certified data as of the version date(s) listed below.</p> <p>Soil Survey Area: State of Connecticut          Survey Area Data: Version 7, Dec 3, 2009</p> <p>Date(s) aerial images were photographed: 8/14/2006</p> <p>The orthophoto or other base map on which the soil lines were compiled and digitized probably differs from the background imagery displayed on these maps. As a result, some minor shifting of map unit boundaries may be evident.</p>	





Soil Map-state of Connecticut


Wind Colebrook South

## Map Unit Legend

State of Connecticut (CT600)			
Map Unit Symbol	Map Unit Name	Acres In AOI	Percent of AOI
413C	Bice-Millsite complex, 3 to 15 percent slopes, very rocky	20.1	22.0%
413E	Bice-Millsite complex, 15 to 45 percent slopes, very rocky	14.5	15.8%
415C	Westminster Millsite-Rock outcrop complex, 3 to 15 percent slopes	6.4	7.0%
4178	Bice fine sandy loam, 3 to 8 percent slopes, very stony	8.9	9.7%
417C	Bice fine sandy loam, 8 to 15 percent slopes, very stony	5.5	6.0%
418C	Schroon fine sandy loam, 2 to 15 percent slopes, very stony	8.3	9.0%
425C	Shelburne fine sandy loam, 8 to 15 percent slopes, very stony	2.0	2.2%
4260	Shelburne fine sandy loam, 15 to 35 percent slopes, extremely stony	2.6	2.9%
427C	Ashfield fine sandy loam, 8 to 15 percent slopes, very stony	4.6	5.0%
437	Wonsqueak mucky peat	9.1	9.9%
443	Brayton-loon meadow complex, extremely stony	9.5	10.4%
Totals for Area of Interest		91.8	100.0%

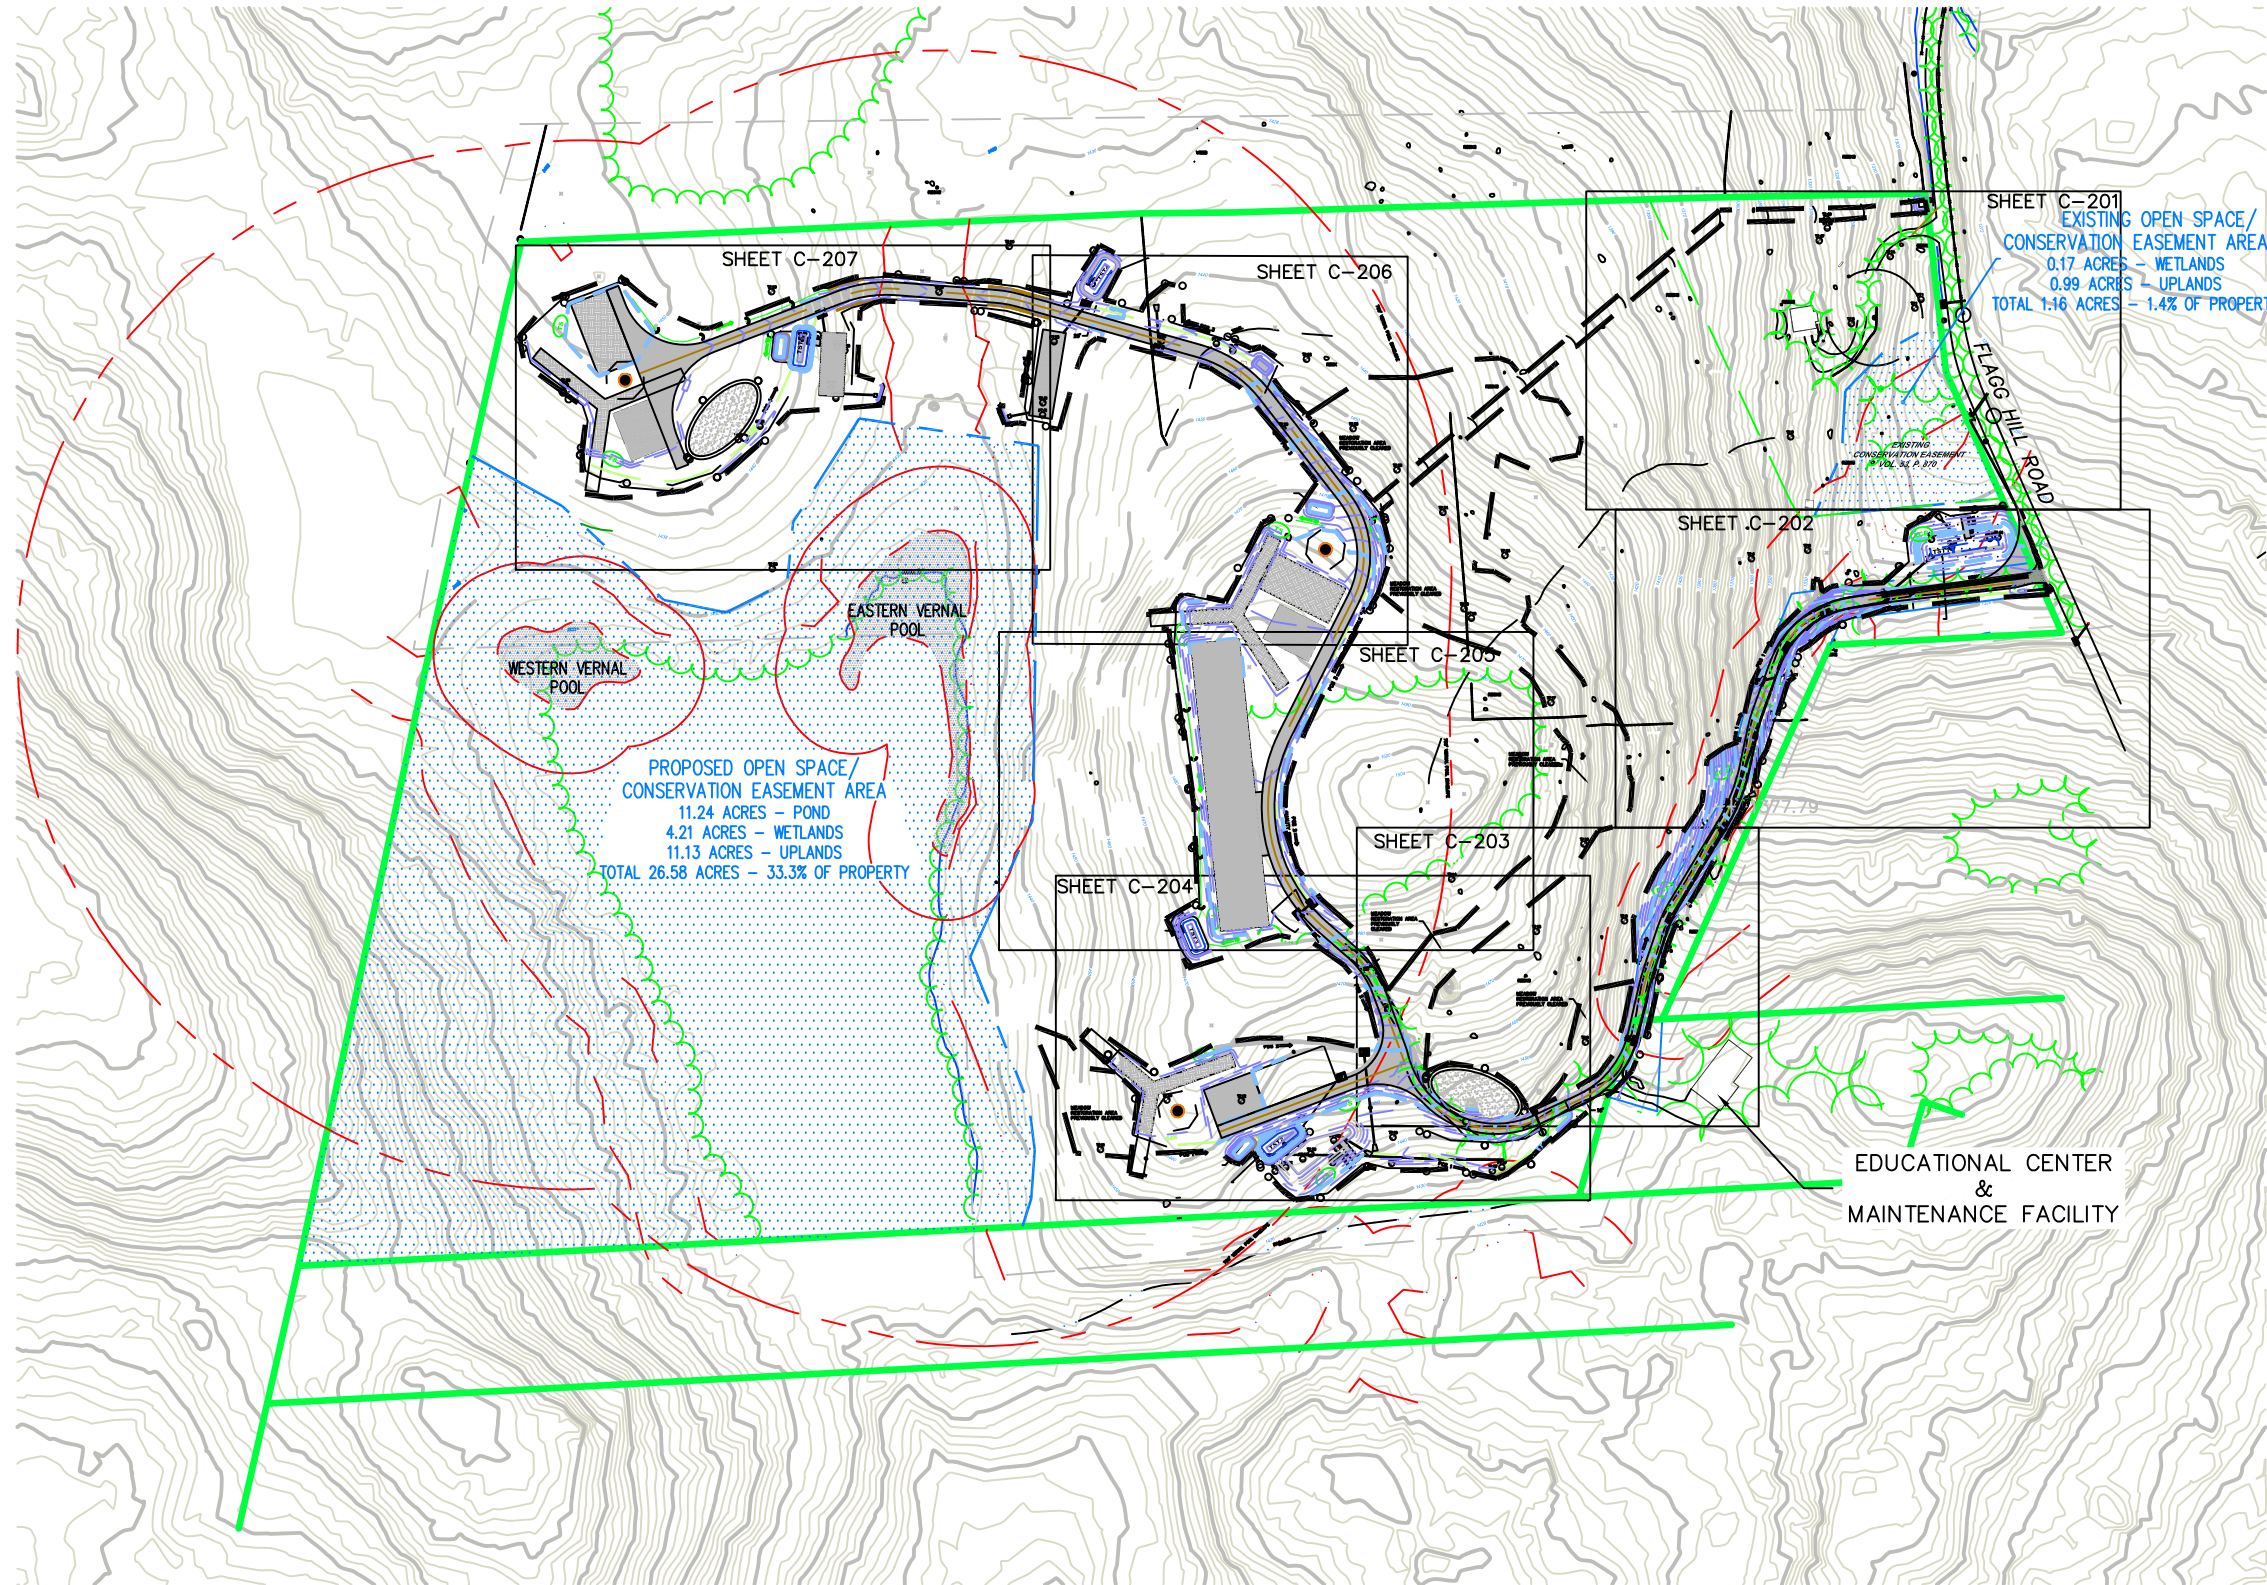

NO.	REVISION	DATE
1	REVISED PER SITING COUNCIL	24 OCT 11
2	REVISED ROAD ALIGNMENT	29 JUN 12
3	CLEARING AREA REVISED	23 JUL 12
4	EXISTING BUILDINGS ADDED	28 AUG 12
<i>Previous Editions Obsolete</i>		



**BNE ENERGY, INC.**  
 29 SOUTH MAIN STREET  
 TOWN CENTER SUITE 200  
 WEST HARTFORD, CT 06107

**EROSION CONTROL PLAN**

**WIND COLEBROOK SOUTH**  
 FLAGG HILL ROAD

COLEBROOK CONNECTICUT




CORNERSTONE PROFESSIONAL PARK, SUITE D-101  
 43 SHERMAN HILL ROAD  
 WOODBURY CONNECTICUT (203) 266-0778


DRAWN BY: BB  
 SCALE: 1" = 300'  
 DATE: 26 AUG 11  
 PWD NO.: 3092  
 CAD FILE NAME: 3092  
 DRAWING NO.:

**C200**


**LEGEND**

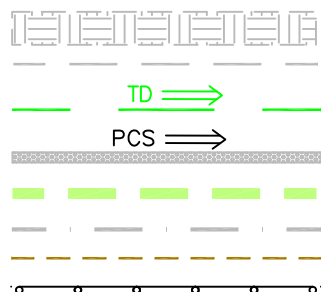


COMPACTED EARTH  
 LIMITS OF CLEARING  
 TEMP. WATER DIVERSION SWALE  
 PERM. RIPRAP DIVERSION/CONVEYANCE  
 DRY WATER QUALITY SWALE  
 SOIL TYPE BOUNDARY  
 STAKED HAY BALES  
 SILT FENCE

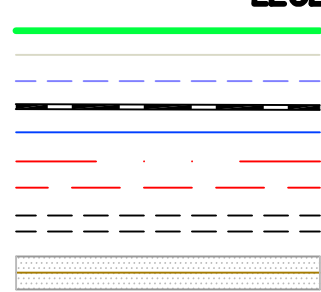



PROPERTY LINE  
 EXISTING CONTOUR  
 PROPOSED CONTOUR  
 PROPOSED STORM DRAINAGE  
 EDGE OF WATER  
 WETLANDS/WATERCOURSE BOUNDARY  
 100' WETLANDS REVIEW AREA  
 EXISTING ROADWAY  
 PROPOSED ACCESS DRIVE




BALED FILTER  
 TEMPORARY SOIL STOCKPILE  
 TEMPORARY SEDIMENT TRAP  
 TEMPORARY SEEDING  
 EROSION CONTROL BLANKET  
 STONE CHECK DAM  
 WATER BAR WITH STAKED HAYBALES



2' x 2' STONE INFILTRATION TRENCH  
 MEADOW RESTORATION  
 VERNAL POOL AREA  
 100' VERNAL POOL SETBACK  
 750' VERNAL POOL ENVELOPE

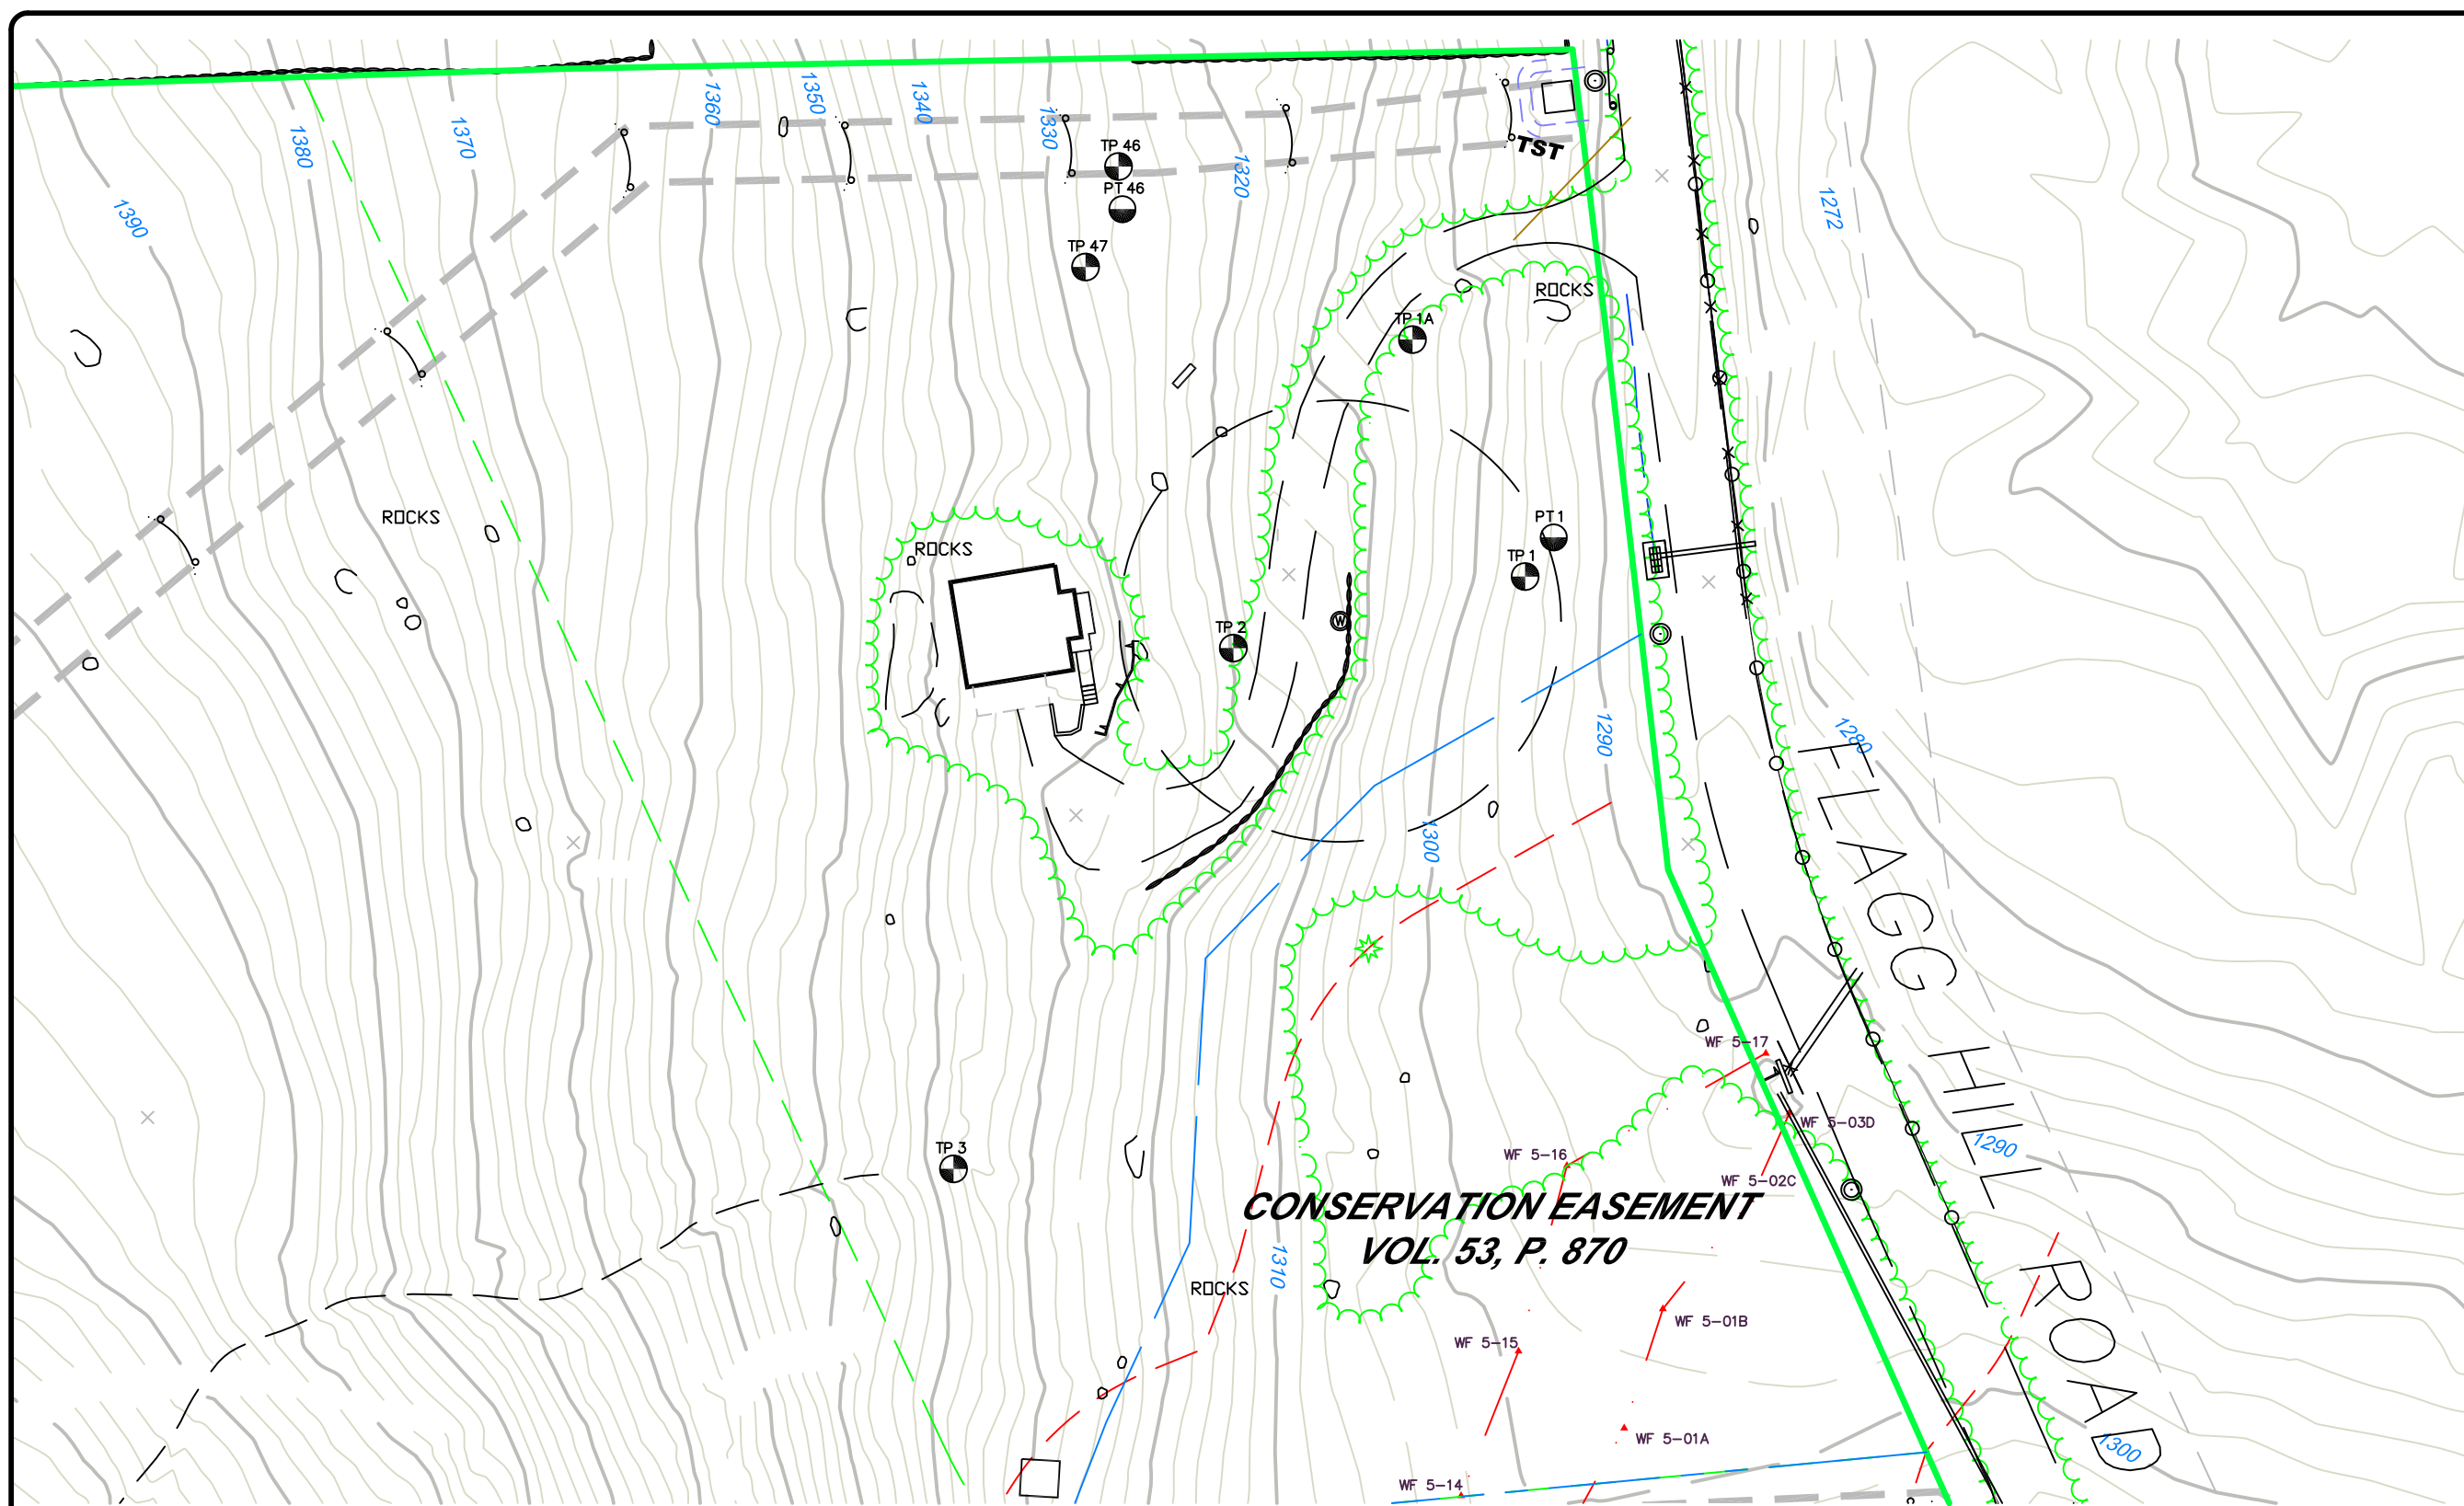

NO.	REVISION	DATE
1	REVISED PER SITING COUNCIL	24 OCT 11
2	REVISED ROAD ALIGNMENT	29 JUN 12
<i>Previous Editions Obsolete</i>		



**BNE ENERGY, INC.**  
 29 SOUTH MAIN STREET  
 TOWN CENTER SUITE 200  
 WEST HARTFORD, CT 06107

**EROSION CONTROL PLAN**  
 COLLECTOR YARD

**WIND COLEBROOK SOUTH**  
 FLAGG HILL ROAD  
 COLEBROOK CONNECTICUT

**LEGEND**



- |  |                                   |  |                               |  |                                |  |                           |
|--|-----------------------------------|--|-------------------------------|--|--------------------------------|--|---------------------------|
|  | COMPACTED EARTH                   |  | PROPERTY LINE                 |  | BALED FILTER                   |  | MEADOW RESTORATION        |
|  | LIMITS OF CLEARING                |  | EXISTING CONTOUR              |  | TEMPORARY SOIL STOCKPILE       |  | VERNAL POOL AREA          |
|  | TEMP. WATER DIVERSION SWALE       |  | PROPOSED CONTOUR              |  | TEMPORARY SEDIMENT TRAP        |  | 100' VERNAL POOL SETBACK  |
|  | PERM. RIPRAP DIVERSION/CONVEYANCE |  | PROPOSED STORM DRAINAGE       |  | TEMPORARY SEEDING              |  | 750' VERNAL POOL ENVELOPE |
|  | DRY WATER QUALITY SWALE           |  | EDGE OF WATER                 |  | EROSION CONTROL BLANKET        |  |                           |
|  | SOIL TYPE BOUNDARY                |  | WETLANDS/WATERCOURSE BOUNDARY |  | STONE CHECK DAM                |  |                           |
|  | STAKED HAY BALES                  |  | 100' WETLANDS REVIEW AREA     |  | WATER BAR WITH STAKED HAYBALES |  |                           |
|  | SILT FENCE                        |  | EXISTING ROADWAY              |  |                                |  |                           |
|  |                                   |  | PROPOSED ACCESS DRIVE         |  | TST                            |  |                           |
|  |                                   |  | TS                            |  | ECB                            |  |                           |

**CIVIL C1**


CORNERSTONE PROFESSIONAL PARK, SUITE D-101  
 43 SHERMAN HILL ROAD  
 WOODBURY CONNECTICUT (203) 266-0778

DRAWN BY: BB      APPROVED BY: CJ  
 SCALE: 1" = 60'  
 DATE: 26 AUG 11  
 PROJ. NO.: 3092  
 CADD FILE NAME: 3092  
 DRAWING NO.: **C201**



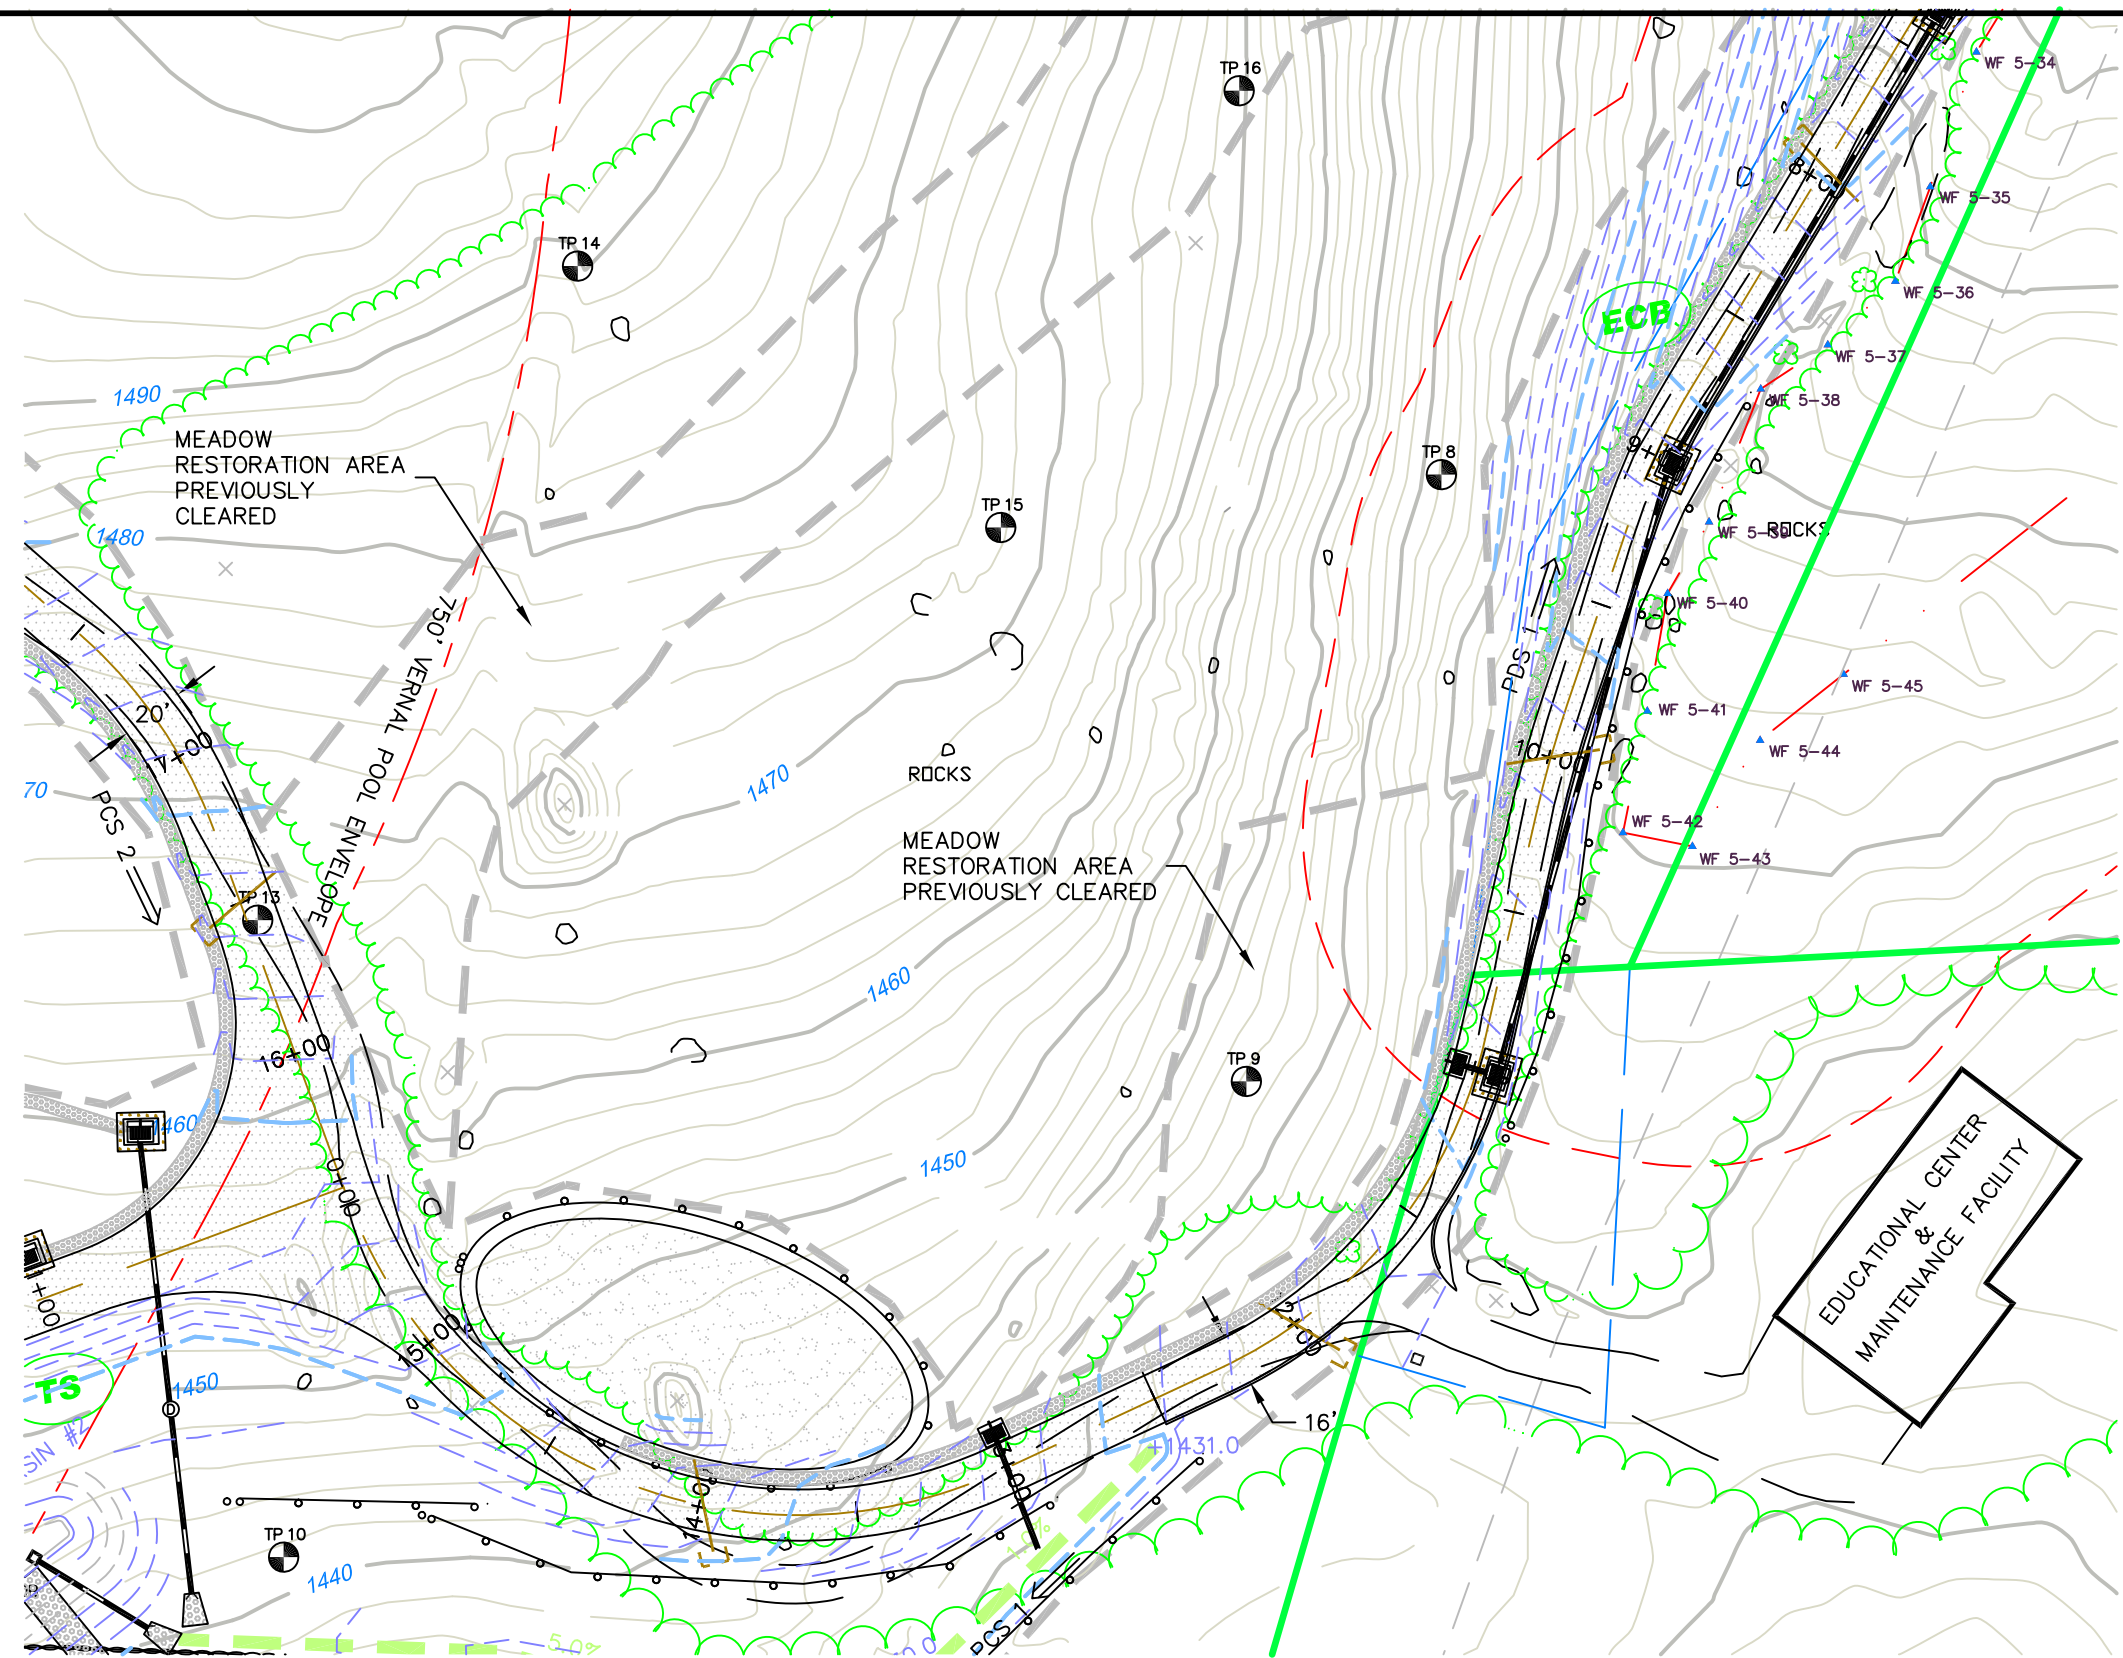

NO.	REVISION	DATE
1	REVISED PER SITING COUNCIL	24 OCT 11
2	REVISED ROAD ALIGNMENT	29 JUN 12
3	CLEARING AREA REVISED	23 JUL 12
4	EXISTING BUILDINGS ADDED	28 AUG 12
<i>Previous Editions Obsolete</i>		



**BNE ENERGY, INC.**  
 29 SOUTH MAIN STREET  
 TOWN CENTER SUITE 200  
 WEST HARTFORD, CT 06107

**EROSION CONTROL PLAN**  
**MAIN ACCESS DRIVE**  
 7+50 TO 17+50

**WIND COLEBROOK SOUTH**  
 FLAGG HILL ROAD

COLEBROOK CONNECTICUT



CORNERSTONE PROFESSIONAL PARK, SUITE D-101  
 43 SHERMAN HILL ROAD  
 WOODBURY (203) 266-0778 CONNECTICUT

DRAWN: BB APPROVED: CJ  
 SCALE: 1" = 60'  
 DATE: 26 AUG 11  
 PROJ. NO.: 3092  
 CAD FILE NAME: 3092  
 DRAWING NO.:

**C203**


**LEGEND**

- |  |                                   |  |                               |  |                                |  |                           |
|--|-----------------------------------|--|-------------------------------|--|--------------------------------|--|---------------------------|
|  | COMPACTED EARTH                   |  | PROPERTY LINE                 |  | BALED FILTER                   |  | MEADOW RESTORATION        |
|  | LIMITS OF CLEARING                |  | EXISTING CONTOUR              |  | TEMPORARY SOIL STOCKPILE       |  | VERNAL POOL AREA          |
|  | TEMP. WATER DIVERSION SWALE       |  | PROPOSED CONTOUR              |  | TEMPORARY SEDIMENT TRAP        |  | 100' VERNAL POOL SETBACK  |
|  | PERM. RIPRAP DIVERSION/CONVEYANCE |  | PROPOSED STORM DRAINAGE       |  | TEMPORARY SEEDING              |  | 750' VERNAL POOL ENVELOPE |
|  | DRY WATER QUALITY SWALE           |  | EDGE OF WATER                 |  | EROSION CONTROL BLANKET        |  |                           |
|  | SOIL TYPE BOUNDARY                |  | WETLANDS/WATERCOURSE BOUNDARY |  | STONE CHECK DAM                |  |                           |
|  | STAKED HAY BALES                  |  | 100' WETLANDS REVIEW AREA     |  | WATER BAR WITH STAKED HAYBALES |  |                           |
|  | SILT FENCE                        |  | EXISTING ROADWAY              |  |                                |  |                           |
|  |                                   |  | PROPOSED ACCESS DRIVE         |  |                                |  |                           |

- 
- 
-






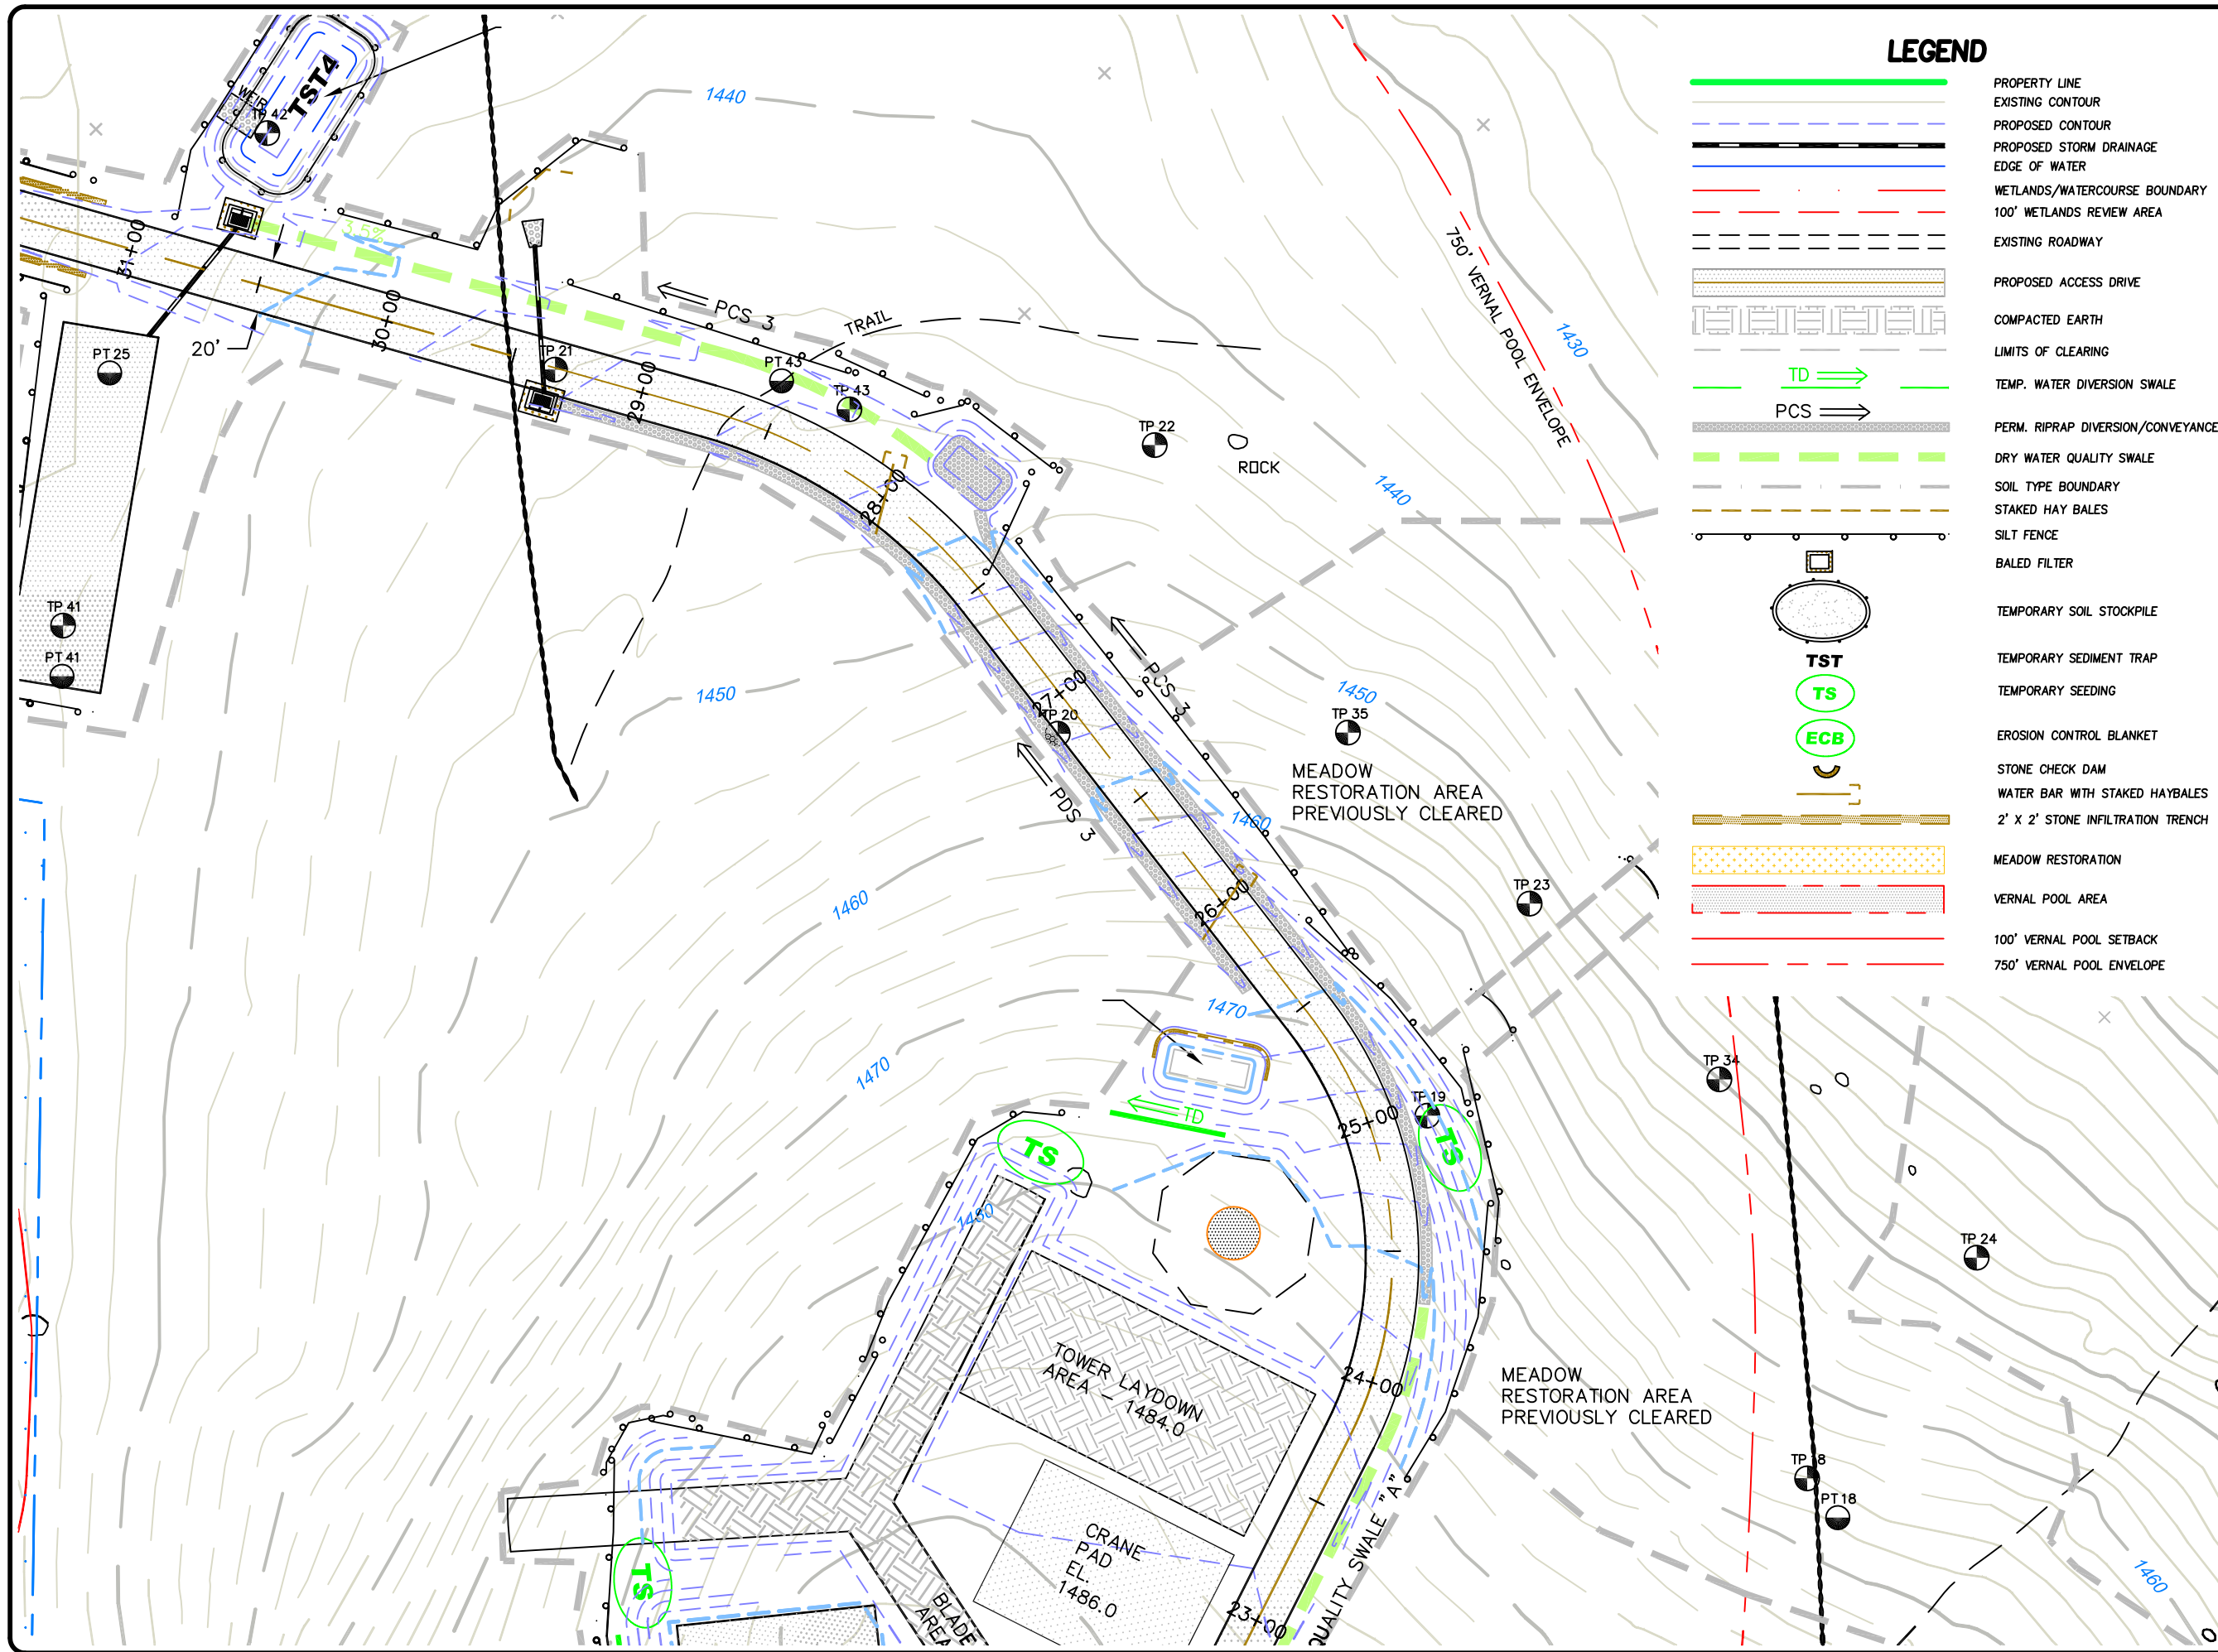


**LEGEND**

- PROPERTY LINE
- EXISTING CONTOUR
- PROPOSED CONTOUR
- PROPOSED STORM DRAINAGE
- EDGE OF WATER
- WETLANDS/WATERCOURSE BOUNDARY
- 100' WETLANDS REVIEW AREA
- EXISTING ROADWAY
- PROPOSED ACCESS DRIVE
- COMPACTED EARTH
- LIMITS OF CLEARING
- TEMP. WATER DIVERSION SWALE
- PERM. RIPRAP DIVERSION/CONVEYANCE
- DRY WATER QUALITY SWALE
- SOIL TYPE BOUNDARY
- STAKED HAY BALES
- SILT FENCE
- BALED FILTER
- TEMPORARY SOIL STOCKPILE
- TEMPORARY SEDIMENT TRAP
- TEMPORARY SEEDING
- EROSION CONTROL BLANKET
- STONE CHECK DAM
- WATER BAR WITH STAKED HAYBALES
- 2' X 2' STONE INFILTRATION TRENCH
- MEADOW RESTORATION
- VERNAL POOL AREA
- 100' VERNAL POOL SETBACK
- 750' VERNAL POOL ENVELOPE



NO.	REVISION	DATE
1	REVISED PER SITING COUNCIL	24 OCT 11
2	FEDERAL WL DELINEATION ADDED	22 NOV 11
3	REVISED ROAD ALIGNMENT	29 JUN 12
4	CLEARING AREA REVISED	23 JUL 12
<i>Previous Editions Obsolete</i>		



**BNE ENERGY, INC.**  
 29 SOUTH MAIN STREET  
 TOWN CENTER SUITE 200  
 WEST HARTFORD, CT 06107

**EROSION CONTROL PLAN**  
 TURBINE TWO AND  
 MAIN ACCESS DRIVE  
 23+00 TO 31+30

**WIND COLEBROOK SOUTH**  
 FLAGG HILL ROAD



COLEBROOK CONNECTICUT

CORNERSTONE PROFESSIONAL PARK, SUITE D-101  
 43 SHERMAN HILL ROAD  
 WOODBURY (203) 266-0778 CONNECTICUT


DRAWN BY	BB	APPROVED BY	CJ
SCALE	1" = 80'		
DATE	26 AUG 11		
PROJ. NO.	3092		
CHD. FILE NAME	3092		
DRAWING NO.			

**C206**



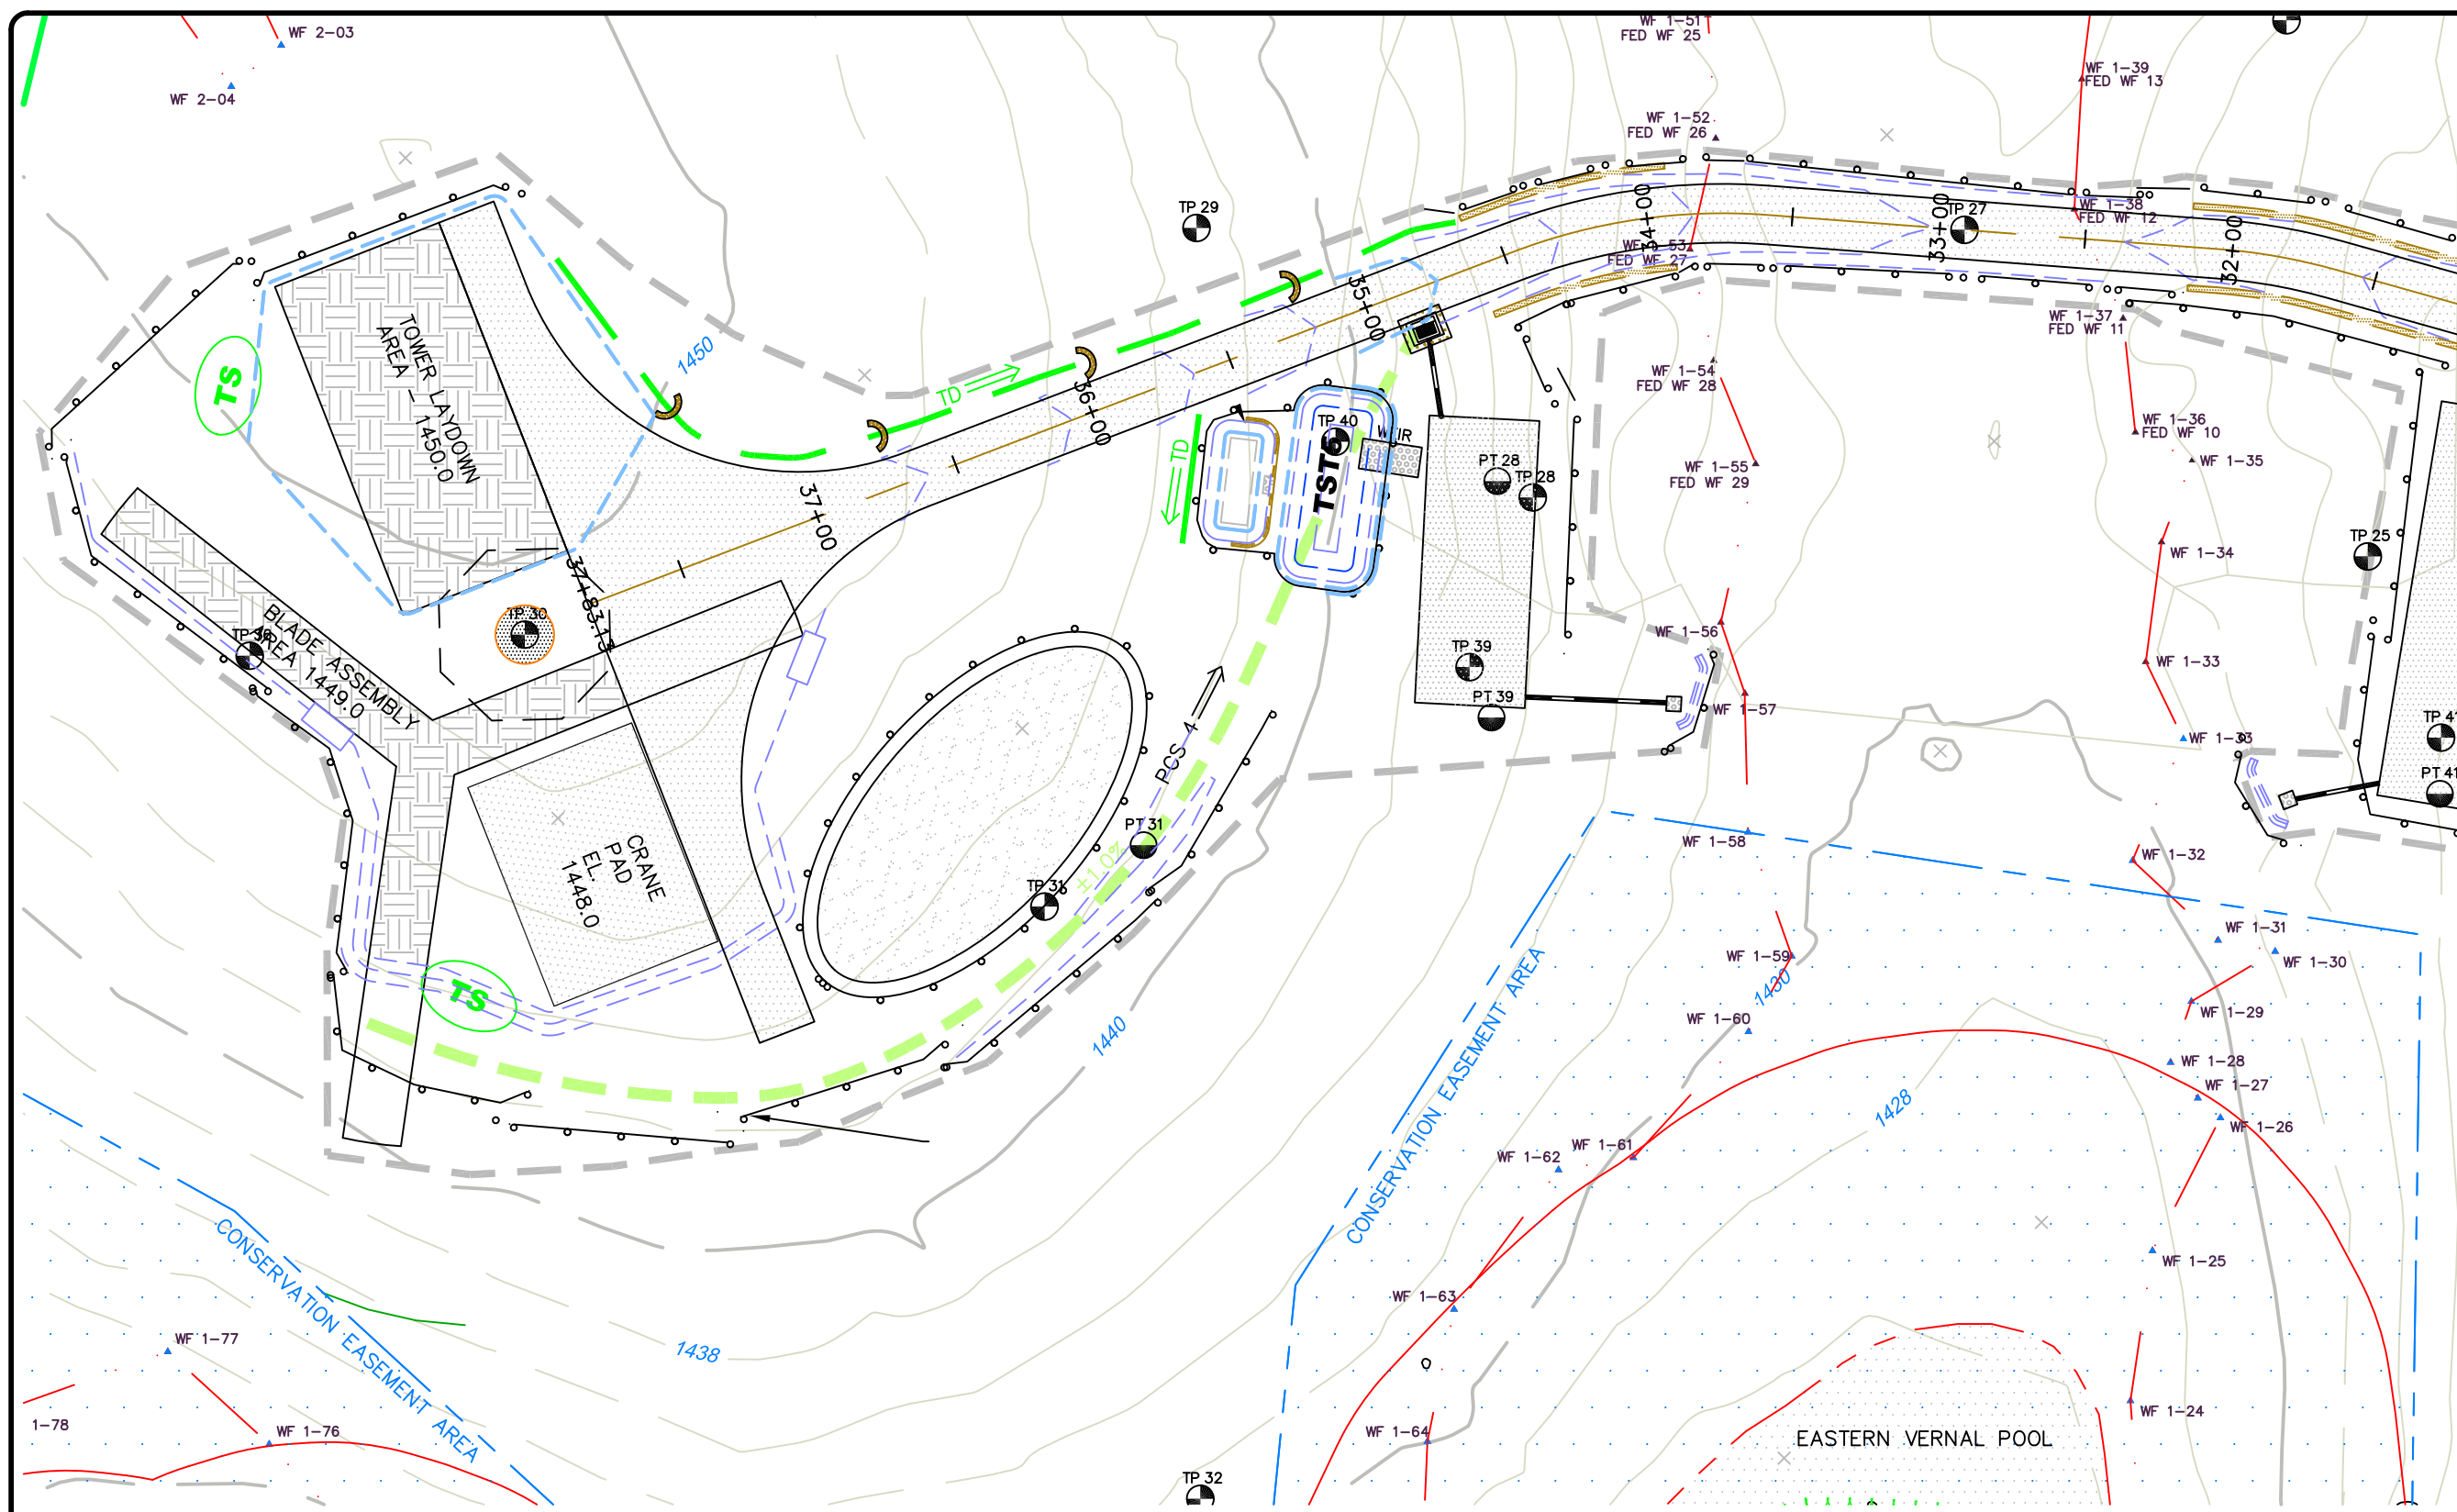

NO.	REVISION	DATE
1	REVISED PER SITING COUNCIL	24 OCT 11
2	FEDERAL WL DELINEATION ADDED	22 NOV 11
3	REVISED ROAD ALIGNMENT	29 JUN 12
<i>Previous Editions Obsolete</i>		



**BNE ENERGY, INC.**  
 29 SOUTH MAIN STREET  
 TOWN CENTER SUITE 200  
 WEST HARTFORD, CT 06107

**EROSION CONTROL PLAN**  
 TURBINE THREE AND  
 MAIN ACCESS DRIVE  
 31+50 TO 37+83

**WIND COLEBROOK SOUTH**  
 FLAGG HILL ROAD  
 COLEBROOK CONNECTICUT





CORNERSTONE PROFESSIONAL PARK, SUITE D-101  
 43 SHERMAN HILL ROAD  
 WOODBURY (203) 266-0778 CONNECTICUT


DATE: 26 AUG 11  
 PROJ. NO.: 3092  
 CADD FILE NAME: 3092  
 DRAWING NO.: **C207**

**LEGEND**

- |  |                                   |  |                               |  |                          |  |                                   |
|--|-----------------------------------|--|-------------------------------|--|--------------------------|--|-----------------------------------|
|  | COMPACTED EARTH                   |  | PROPERTY LINE                 |  | BALED FILTER             |  | WATER BAR WITH STAKED HAYBALES    |
|  | LIMITS OF CLEARING                |  | EXISTING CONTOUR              |  | TEMPORARY SOIL STOCKPILE |  | 2' X 2' STONE INFILTRATION TRENCH |
|  | TEMP. WATER DIVERSION SWALE       |  | PROPOSED CONTOUR              |  | TEMPORARY SEDIMENT TRAP  |  | MEADOW RESTORATION                |
|  | PERM. RIPRAP DIVERSION/CONVEYANCE |  | PROPOSED STORM DRAINAGE       |  | TEMPORARY SEEDING        |  | VERNAL POOL AREA                  |
|  | DRY WATER QUALITY SWALE           |  | EDGE OF WATER                 |  | EROSION CONTROL BLANKET  |  | 100' VERNAL POOL SETBACK          |
|  | SOIL TYPE BOUNDARY                |  | WETLANDS/WATERCOURSE BOUNDARY |  | STONE CHECK DAM          |  | 750' VERNAL POOL ENVELOPE         |
|  | STAKED HAY BALES                  |  | 100' WETLANDS REVIEW AREA     |  | TST                      |  |                                   |
|  | SILT FENCE                        |  | EXISTING ROADWAY              |  | TS                       |  |                                   |
|  |                                   |  | PROPOSED ACCESS DRIVE         |  | ECB                      |  |                                   |

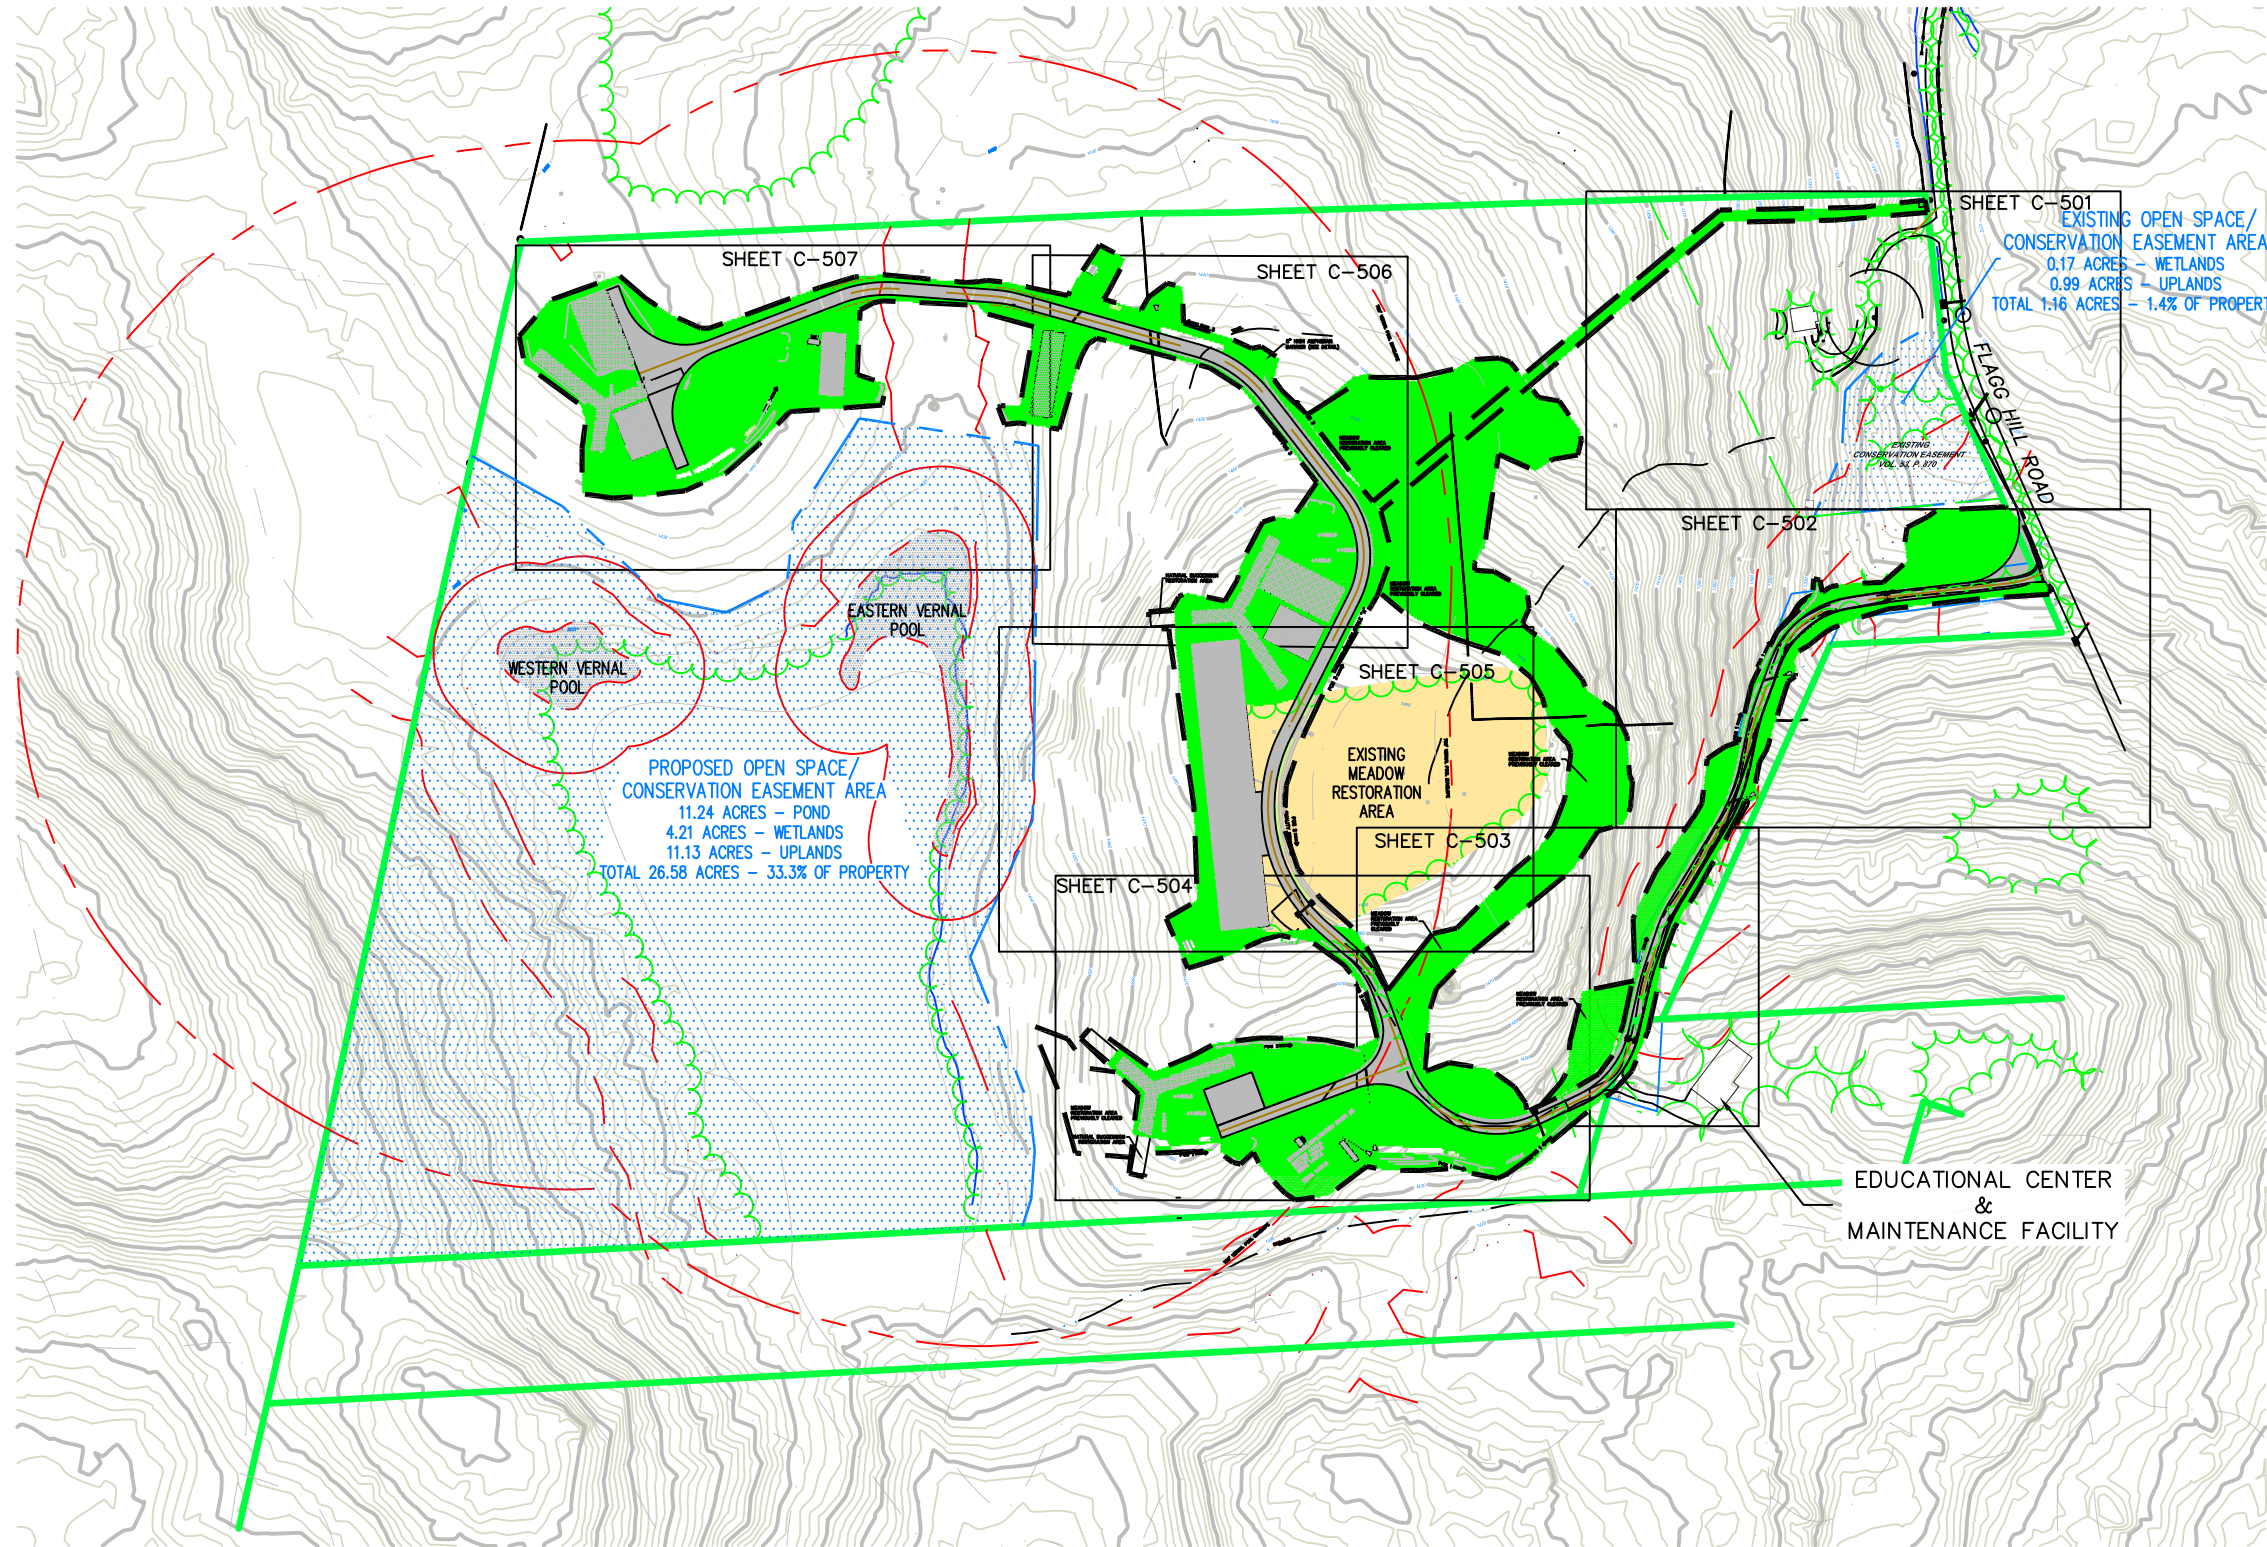

NO.	REVISION	DATE
1	REVISED PER SITING COUNCIL	24 OCT 11
2	REVISED ROAD ALIGNMENT	29 JUN 12
3	CLEARING AREA REVISED	23 JUL 12
4	EXISTING BUILDINGS ADDED	28 AUG 12
Previous Editions Obsolete		



**BNE ENERGY, INC.**  
 29 SOUTH MAIN STREET  
 TOWN CENTER SUITE 200  
 WEST HARTFORD, CT 06107

**POST CONSTRUCTION  
 GRADING PLAN**

**WIND COLEBROOK  
 SOUTH**  
 FLAGG HILL ROAD

COLEBROOK CONNECTICUT





CORNERSTONE PROFESSIONAL PARK, SUITE D-101  
 43 SHERMAN HILL ROAD  
 WOODBURY (203) 266-0778 CONNECTICUT

DRAWN BY	BB	APPROVED BY	CJ
SCALE	1" = 300'		
DATE	26 AUG 11		
PROJECT NO.	3092		
CADD FILE NAME	3092		
DRAWING NO.			


**C500**

**LEGEND**

	PROPERTY LINE		PROPOSED UPLAND MEADOW RESTORATION AREA
	EXISTING CONTOUR		DRY WATER QUALITY SWALE
	CONTOUR FROM CONSTRUCTION GRADING TO REMAIN		EXISTING MEADOW
	CONTOUR FROM CONSTRUCTION GRADING TO BE MODIFIED		VERNAL POOL AREA
	PROPOSED CONTOUR		100' VERNAL POOL SETBACK
	PROPOSED STORM DRAINAGE		750' VERNAL POOL ENVELOPE
	EDGE OF WATER		
	WETLANDS/WATERCOURSE BOUNDARY		
	100' WETLANDS REVIEW AREA		
	EXISTING ROADWAY		
			PROPOSED ACCESS DRIVE
			PERM. RIPRAP DIVERSION/CONVEYANCE SWALE
			LIMITS OF CLEARING

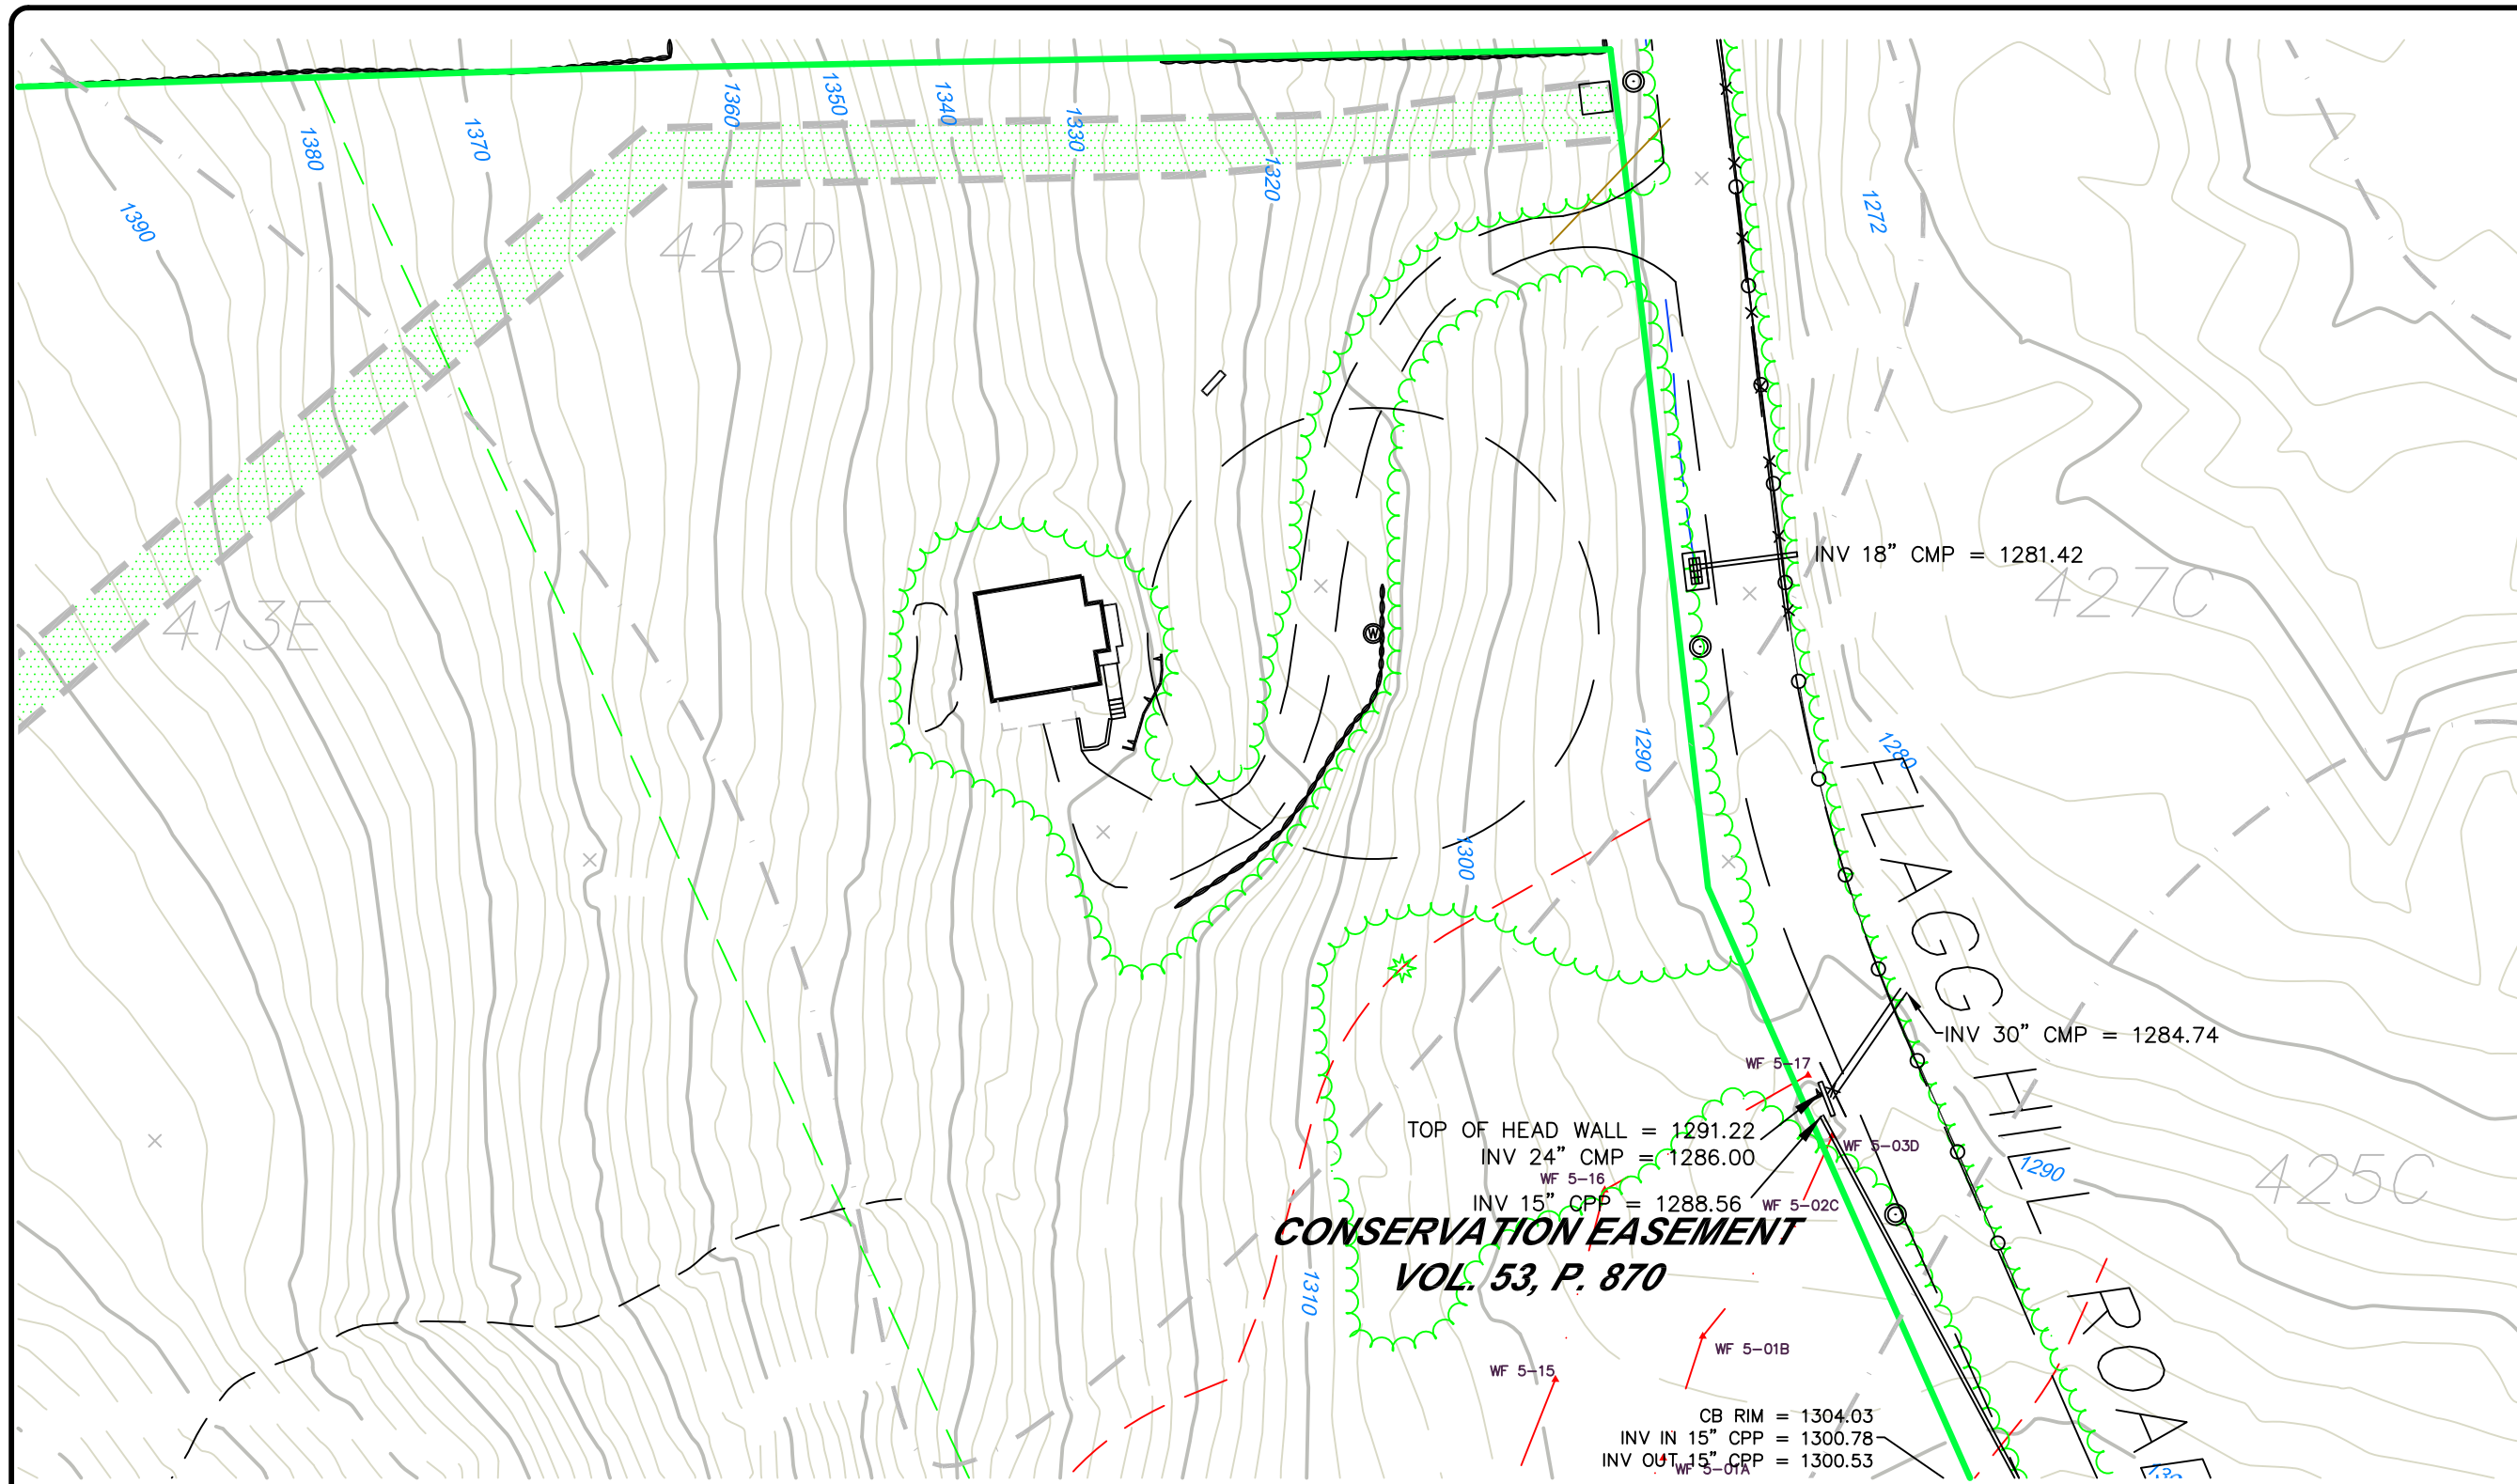

NO.	REVISION	DATE
1	REVISED PER SITING COUNCIL	24 OCT 11
2	REVISED ROAD ALIGNMENT	29 JUN 12



BNE ENERGY, INC.  
 29 SOUTH MAIN STREET  
 TOWN CENTER SUITE 200  
 WEST HARTFORD, CT 06107

POST CONSTRUCTION  
 GRADING PLAN  
 COLLECTOR YARD

WIND COLEBROOK  
 SOUTH  
 FLAGG HILL ROAD  
 COLEBROOK CONNECTICUT

**LEGEND**



- PROPERTY LINE
- EXISTING CONTOUR
- CONTOUR FROM CONSTRUCTION GRADING TO REMAIN
- CONTOUR FROM CONSTRUCTION GRADING TO BE MODIFIED
- PROPOSED CONTOUR
- PROPOSED STORM DRAINAGE
- EDGE OF WATER
- WETLANDS/WATERCOURSE BOUNDARY
- 100' WETLANDS REVIEW AREA
- EXISTING ROADWAY
- PROPOSED ACCESS DRIVE
- PERM. RIPRAP DIVERSION/CONVEYANCE SWALE
- LIMITS OF CLEARING
- PROPOSED UPLAND MEADOW RESTORATION AREA
- DRY WATER QUALITY SWALE
- EXISTING MEADOW
- VERNAL POOL AREA
- 100' VERNAL POOL SETBACK
- 750' VERNAL POOL ENVELOPE

**CIVIL**


CORNERSTONE PROFESSIONAL PARK, SUITE D-101  
 43 SHERMAN HILL ROAD  
 WOODBURY (203) 266-0778 CONNECTICUT

DRAWN BY	BB	APPROVED BY	CJ
SCALE	1" = 80'		
DATE	26 AUG 11		
PROJ. NO.	3092		
CHD. FILE NAME	3092		
DRAWING NO.			

**C501**

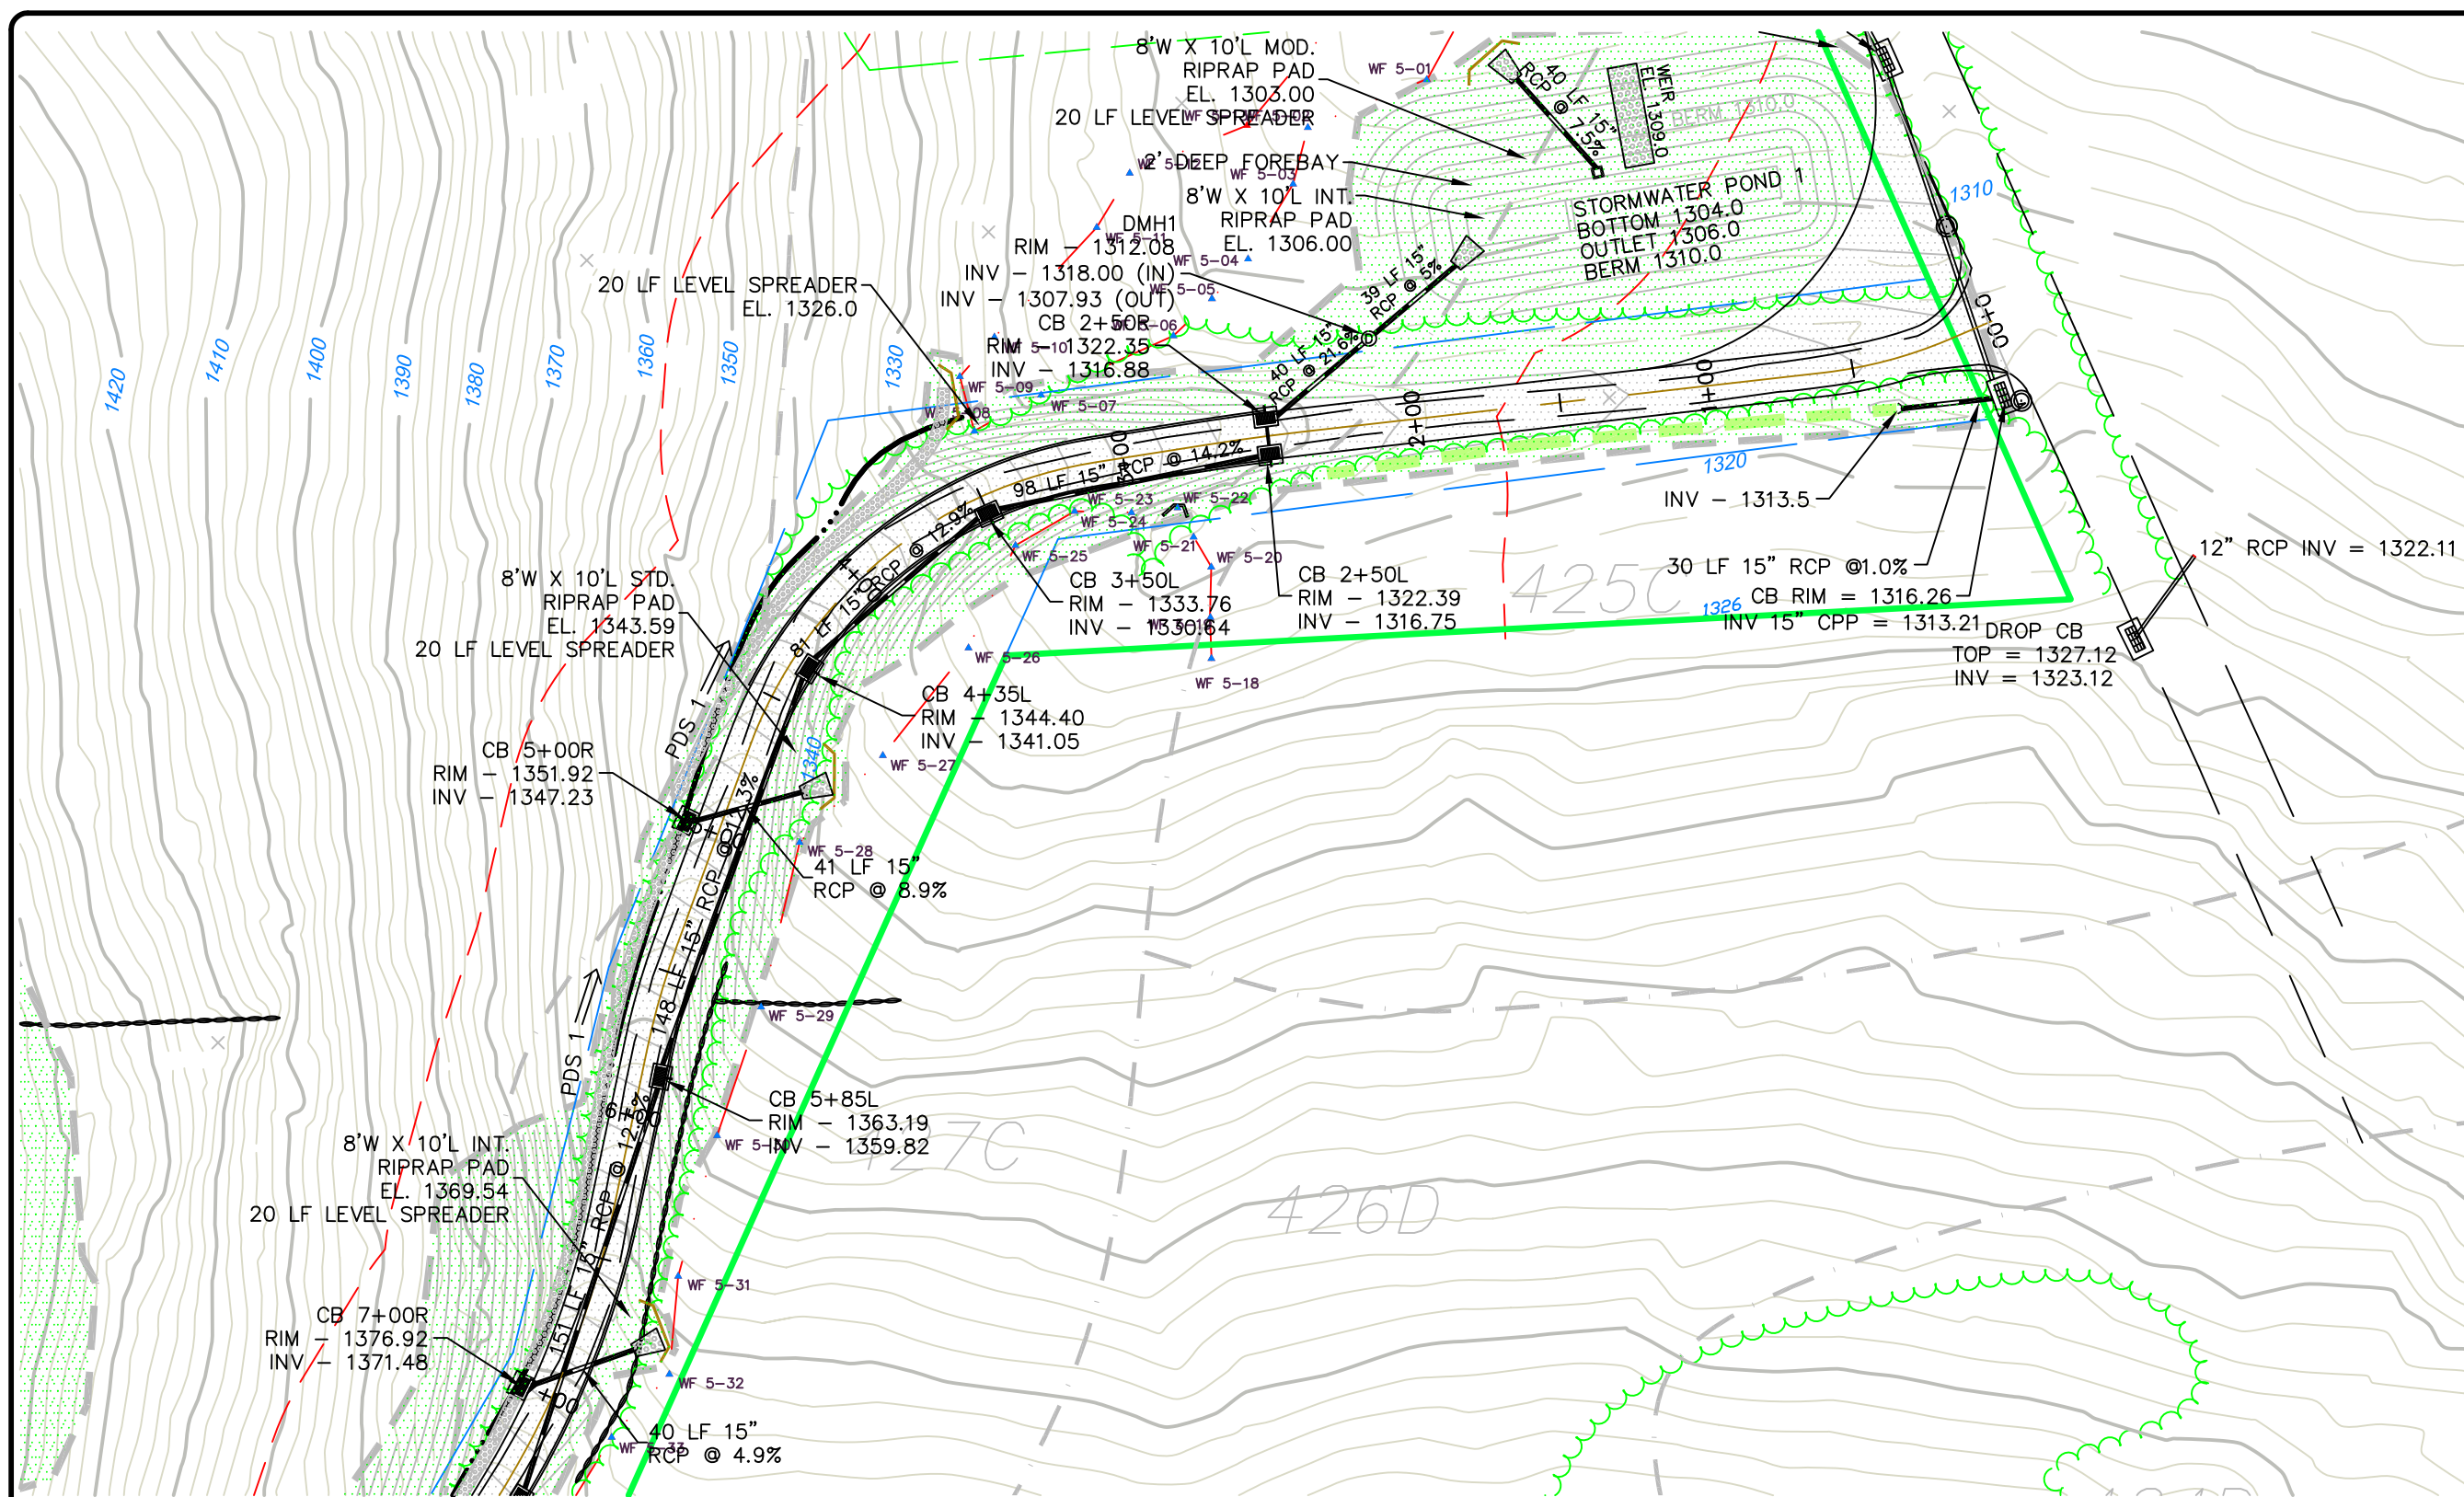

NO.	REVISION	DATE
1	REVISED PER SITING COUNCIL	24 OCT 11
2	REVISED ROAD ALIGNMENT	29 JUN 12



BNE ENERGY, INC.  
 29 SOUTH MAIN STREET  
 TOWN CENTER SUITE 200  
 WEST HARTFORD, CT 06107

POST CONSTRUCTION  
 GRADING PLAN  
 MAIN ACCESS DRIVE  
 0+00 TO 7+50

WIND COLEBROOK  
 SOUTH  
 FLAGG HILL ROAD


COLEBROOK CONNECTICUT

CORNERSTONE PROFESSIONAL PARK, SUITE D-101  
 43 SHERMAN HILL ROAD  
 WOODBURY CONNECTICUT (203) 266-0778


**LEGEND**

	PROPERTY LINE		PERM. RIPRAP DIVERSION/CONVEYANCE SWALE
	EXISTING CONTOUR		LIMITS OF CLEARING
	CONTOUR FROM CONSTRUCTION GRADING TO REMAIN		PROPOSED UPLAND MEADOW RESTORATION AREA
	CONTOUR FROM CONSTRUCTION GRADING TO BE MODIFIED		DRY WATER QUALITY SWALE
	PROPOSED CONTOUR		EXISTING MEADOW
	PROPOSED STORM DRAINAGE		VERNAL POOL AREA
	EDGE OF WATER		100' VERNAL POOL SETBACK
	WETLANDS/WATERCOURSE BOUNDARY		750' VERNAL POOL ENVELOPE
	100' WETLANDS REVIEW AREA		
	EXISTING ROADWAY		
	PROPOSED ACCESS DRIVE		

DRAWN BY:	BB	APPROVED BY:	CJ
SCALE:	1" = 80'	DATE:	26 AUG 11
PROJ. NO.:	3092	CADD FILE NAME:	3092
DRAWING NO.:	C502		



NO.	REVISION	DATE
1	REVISED PER SITING COUNCIL	24 OCT 11
2	REVISED ROAD ALIGNMENT	29 JUN 12
3	CLEARING AREA REVISED	23 JUL 12
4	EXISTING BUILDINGS ADDED	28 AUG 12
<i>Previous Editions Obsolete</i>		



BNE ENERGY, INC.  
 29 SOUTH MAIN STREET  
 TOWN CENTER SUITE 200  
 WEST HARTFORD, CT 06107

POST CONSTRUCTION  
 GRADING PLAN  
 MAIN ACCESS DRIVE  
 7+50 TO 17+50

WIND COLEBROOK  
 SOUTH  
 FLAGG HILL ROAD


COLEBROOK CONNECTICUT



CORNERSTONE PROFESSIONAL PARK, SUITE D-101  
 43 SHERMAN HILL ROAD  
 WOODBURY (203) 266-0778 CONNECTICUT


DRAWN BY: BB  
 SCALE: 1" = 60'  
 DATE: 26 AUG 11  
 PROJECT NO.: 3092  
 CAD FILE NAME: 3092  
 DRAWING NO.:

**C503**

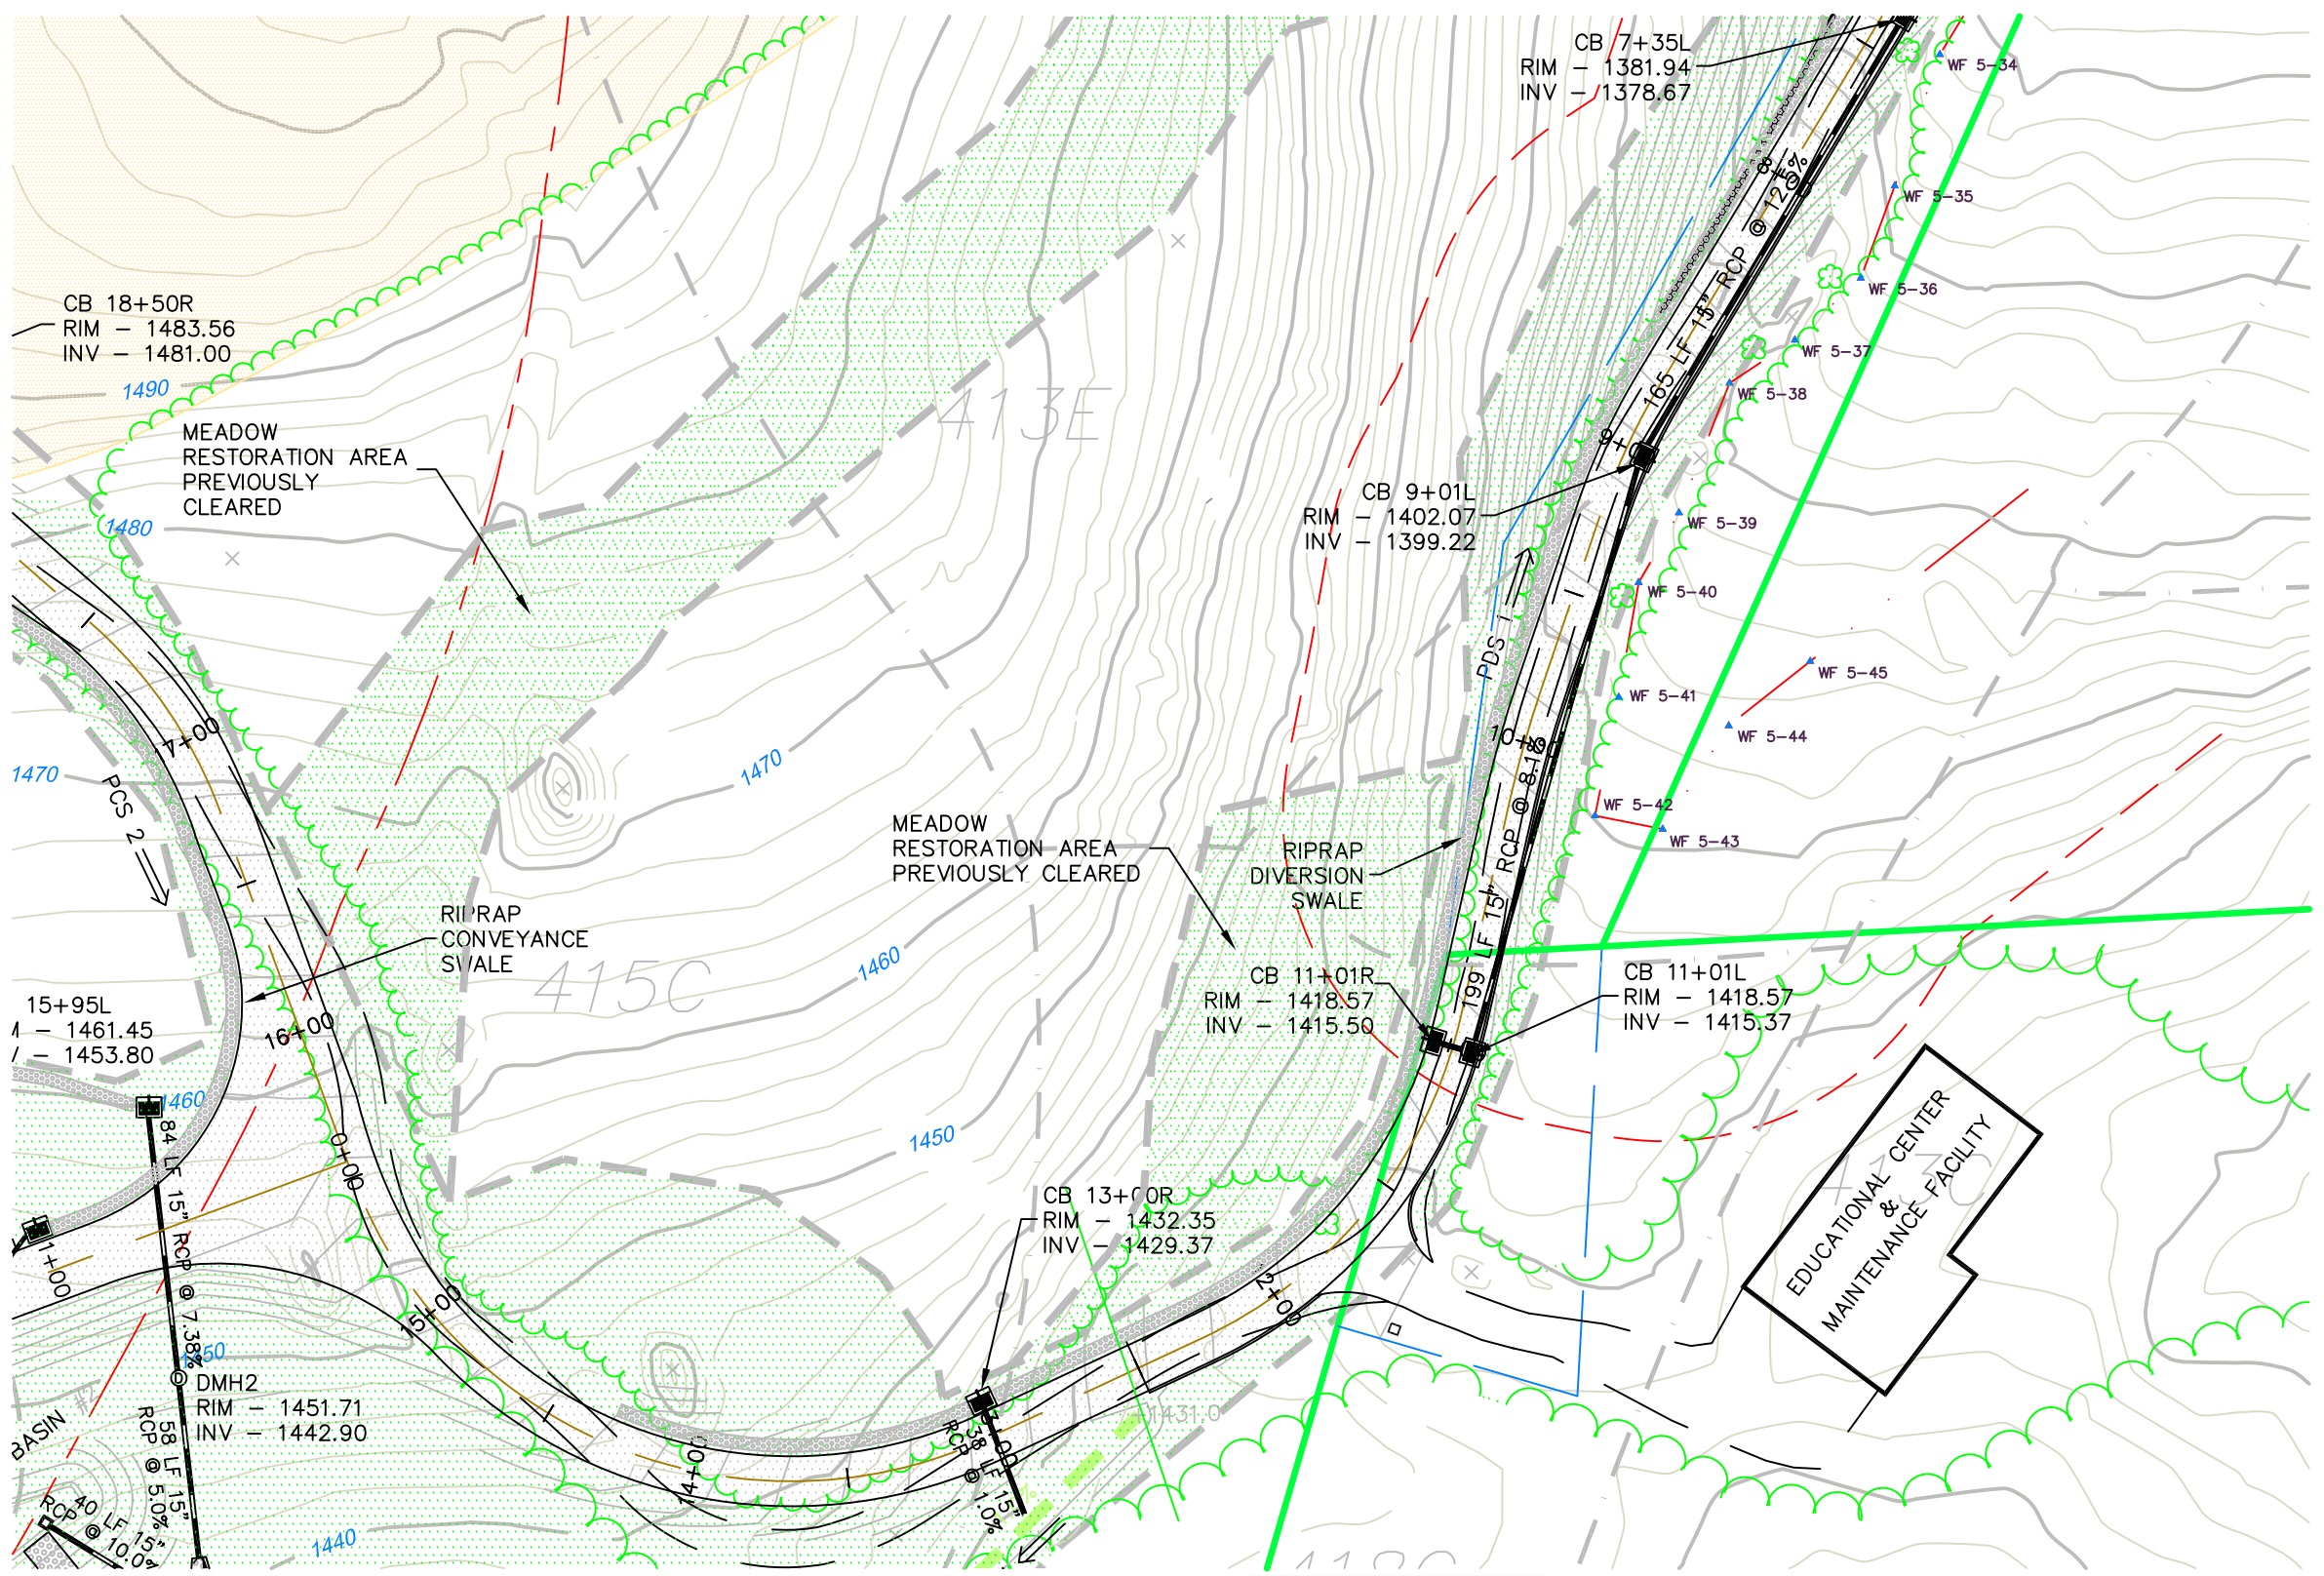


**LEGEND**

- |  |  |  |   |
|--|--|--|---|
|  | PROPERTY LINE                                    |  | PROPOSED UPLAND MEADOW RESTORATION AREA |
|  | EXISTING CONTOUR                                 |  | DRY WATER QUALITY SWALE                 |
|  | CONTOUR FROM CONSTRUCTION GRADING TO REMAIN      |  | EXISTING MEADOW                         |
|  | CONTOUR FROM CONSTRUCTION GRADING TO BE MODIFIED |  | VERNAL POOL AREA                        |
|  | PROPOSED CONTOUR                                 |  | 100' VERNAL POOL SETBACK                |
|  | PROPOSED STORM DRAINAGE                          |  | 750' VERNAL POOL ENVELOPE               |
|  | EDGE OF WATER                                    |  |   |
|  | WETLANDS/WATERCOURSE BOUNDARY                    |  |   |
|  | 100' WETLANDS REVIEW AREA                        |  |   |
|  | EXISTING ROADWAY                                 |  |   |
|  | PROPOSED ACCESS DRIVE                            |  |   |
|  | PROPOSED ACCESS DRIVE                            |  |   |



NO.	REVISION	DATE
1	REVISED PER SITING COUNCIL	24 OCT 11
2	REVISED ROAD ALIGNMENT	29 JUN 12
3	CLEARING AREA REVISED	23 JUL 12
<i>Previous Editions Obsolete</i>		



**BNE ENERGY, INC.**  
 29 SOUTH MAIN STREET  
 TOWN CENTER SUITE 200  
 WEST HARTFORD, CT 06107

**POST CONSTRUCTION  
 GRADING PLAN  
 TURBINE ONE AND MAIN  
 ACCESS DRIVE  
 13+00 TO 18+50**


**WIND COLEBROOK  
 SOUTH  
 FLAGG HILL ROAD**

**CIVIL C1**

CORNERSTONE PROFESSIONAL PARK, SUITE D-101  
 43 SHERMAN HILL ROAD  
 WOODBURY CONNECTICUT (203) 266-0778


DESIGNER: BB	APPROVER: CJ
SCALE: 1" = 80'	
DATE: 26 AUG 11	
PROJ. NO.: 3092	
CHD FILE NAME: 3092	
DRAWING NO.:	

**C504**

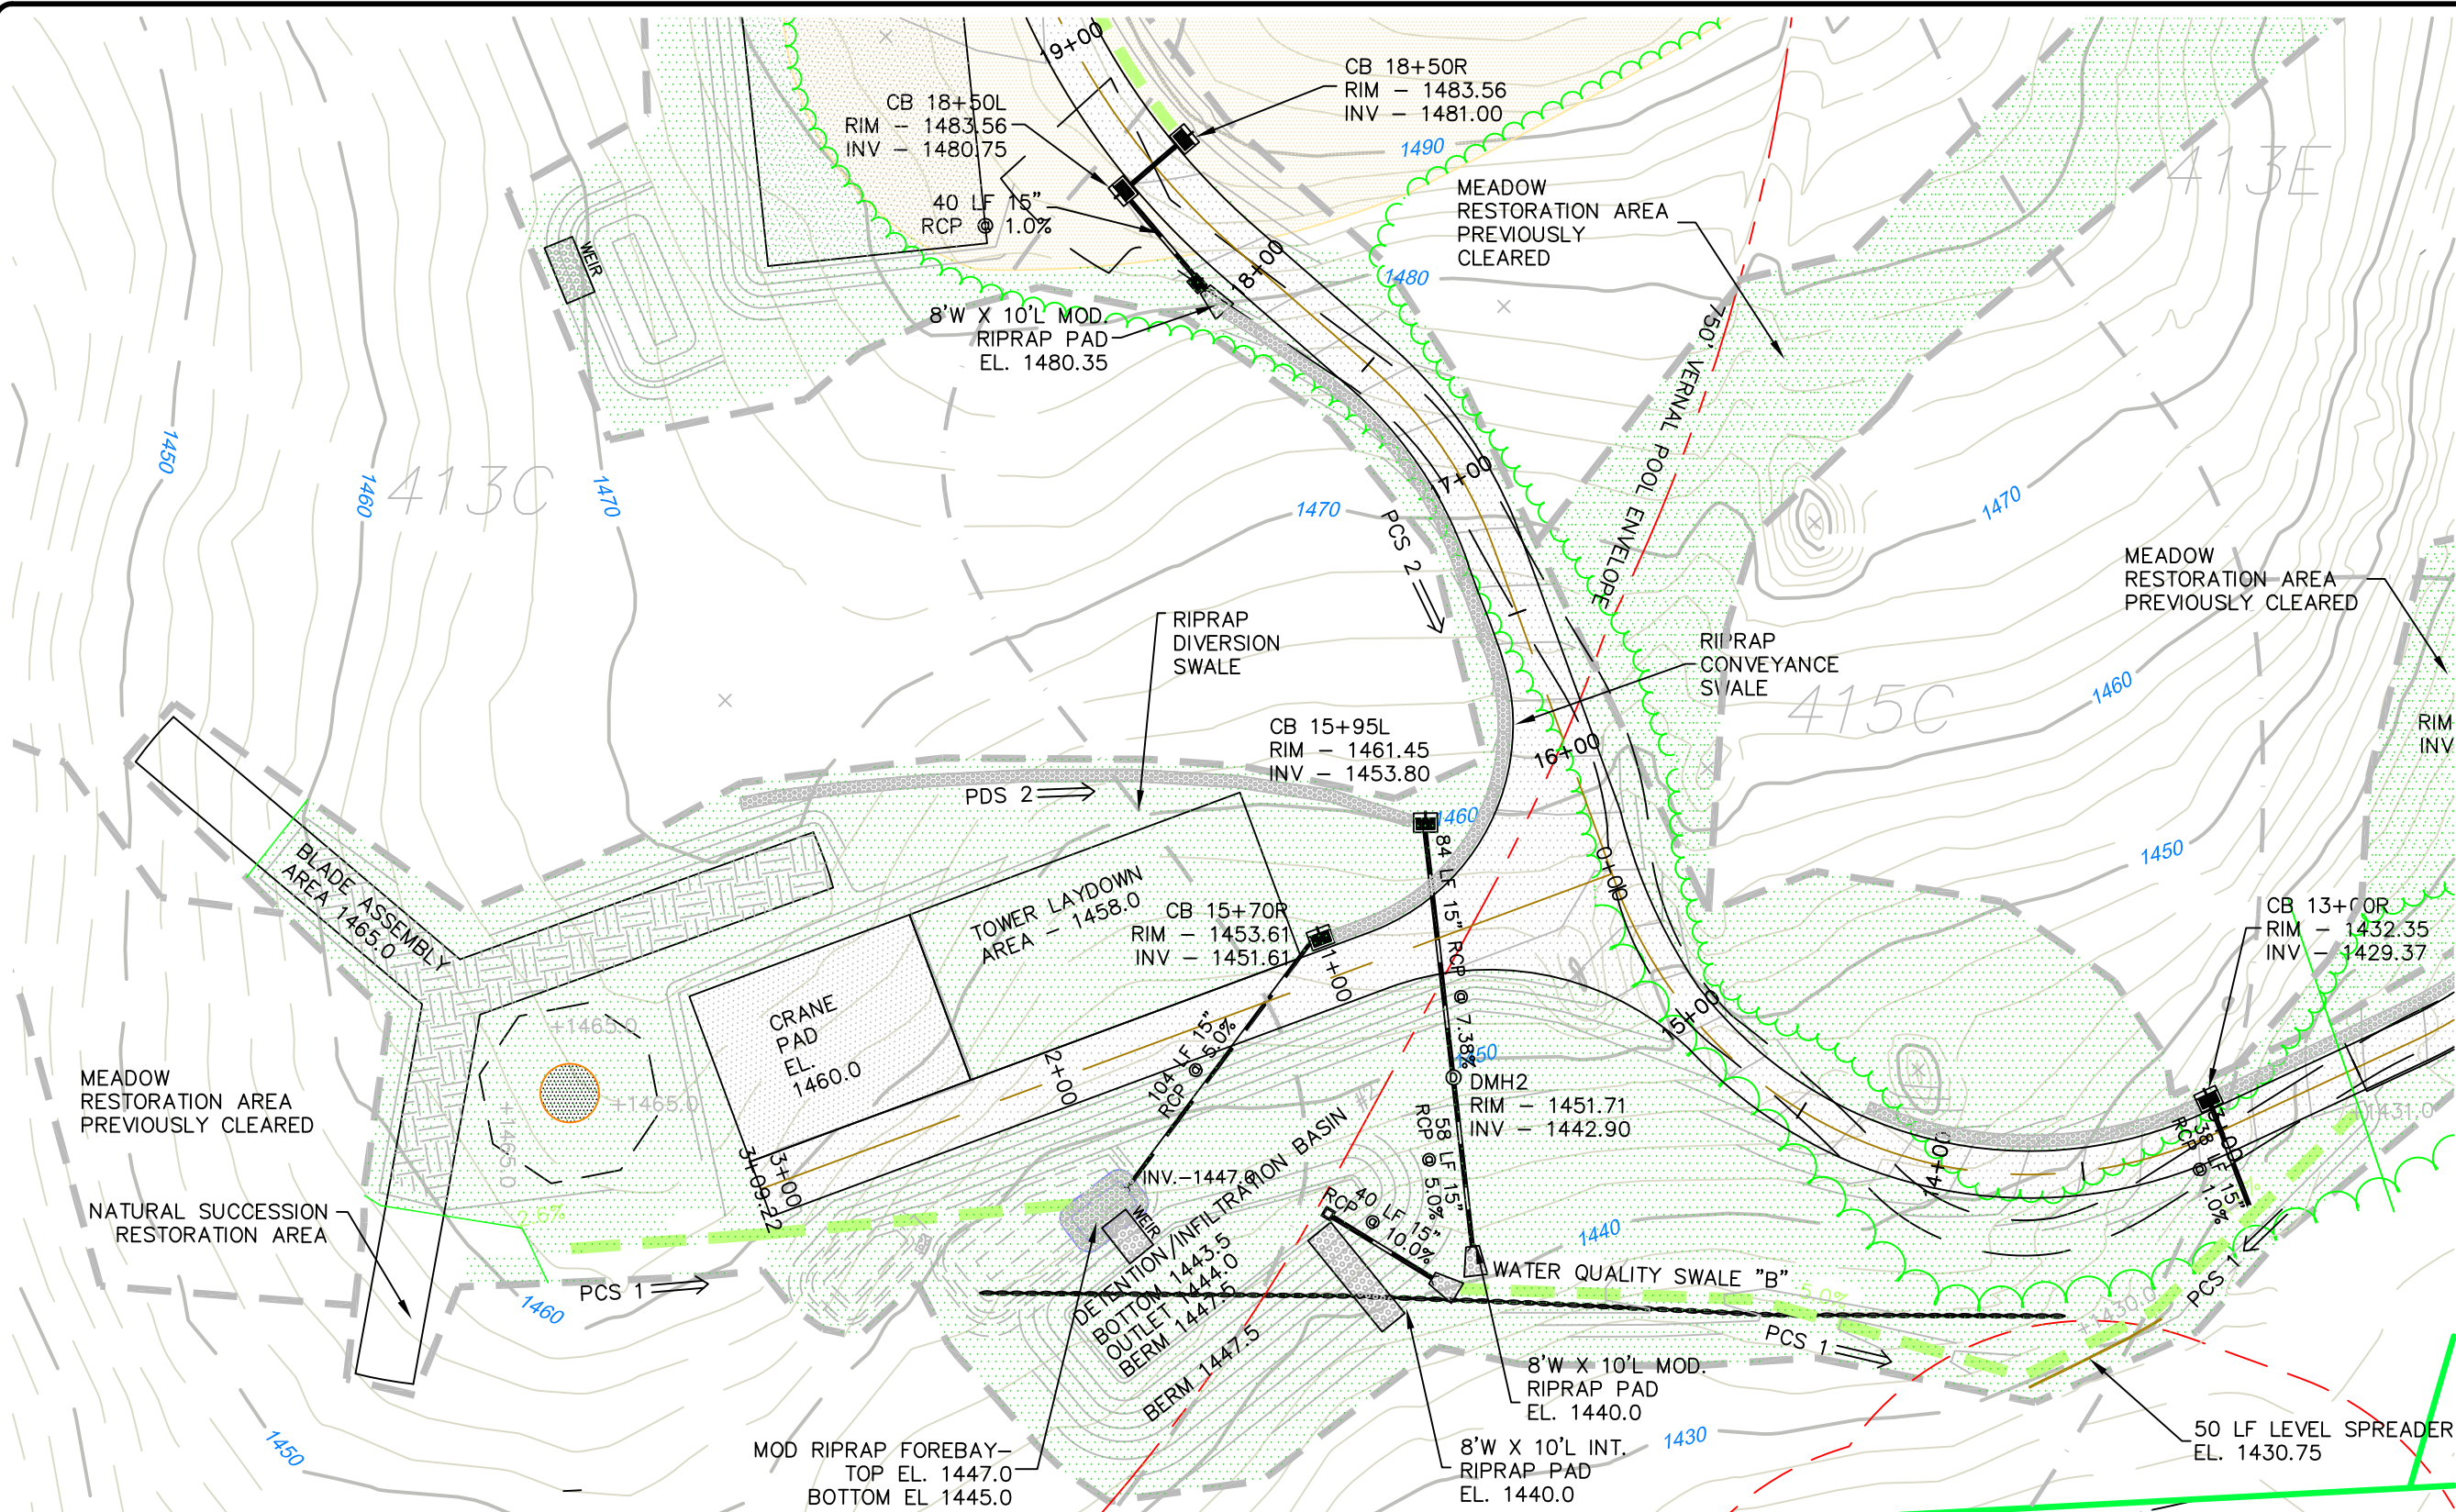


**LEGEND**

- |  |                           |  |  |  |   |
|--|---------------------------|--|--|--|---|
|  | DRY WATER QUALITY SWALE   |  | PROPERTY LINE                                    |  | EXISTING ROADWAY                        |
|  | EXISTING MEADOW           |  | EXISTING CONTOUR                                 |  | PROPOSED ACCESS DRIVE                   |
|  | VERNAL POOL AREA          |  | CONTOUR FROM CONSTRUCTION GRADING TO REMAIN      |  | PERM. RIPRAP DIVERSION/CONVEYANCE SWALE |
|  | 100' VERNAL POOL SETBACK  |  | CONTOUR FROM CONSTRUCTION GRADING TO BE MODIFIED |  | LIMITS OF CLEARING                      |
|  | 750' VERNAL POOL ENVELOPE |  | PROPOSED CONTOUR                                 |  | PROPOSED UPLAND MEADOW RESTORATION AREA |
|  |                           |  | PROPOSED STORM DRAINAGE                          |  |   |
|  |                           |  | EDGE OF WATER                                    |  |   |
|  |                           |  | WETLANDS/WATERCOURSE BOUNDARY                    |  |   |
|  |                           |  | 100' WETLANDS REVIEW AREA                        |  |   |



NO.	REVISION	DATE
1	REVISED PER SITING COUNCIL	24 OCT 11
2	REVISED ROAD ALIGNMENT	29 JUN 12
<i>Previous Editions Obsolete</i>		

MEADOW RESTORATION PREVIOUSLY




**BNE ENERGY, INC.**  
 29 SOUTH MAIN STREET  
 TOWN CENTER SUITE 200  
 WEST HARTFORD, CT 06107

**POST CONSTRUCTION GRADING PLAN**  
 MAIN ACCESS DRIVE  
 18+50 TO 23+50

**WIND COLEBROOK SOUTH**  
 FLAGG HILL ROAD  
 COLEBROOK CONNECTICUT


**CIVIL C1**  
 CORNERSTONE PROFESSIONAL PARK, SUITE D-101  
 43 SHERMAN HILL ROAD  
 WOODBURY (203) 266-0778 CONNECTICUT

DESIGNER: BB  
 SCALE: 1" = 80'  
 DATE: 26 AUG 11  
 PROJ. NO.: 3092  
 CADD FILE NAME: 3092  
 DRAWING NO.: **C505**

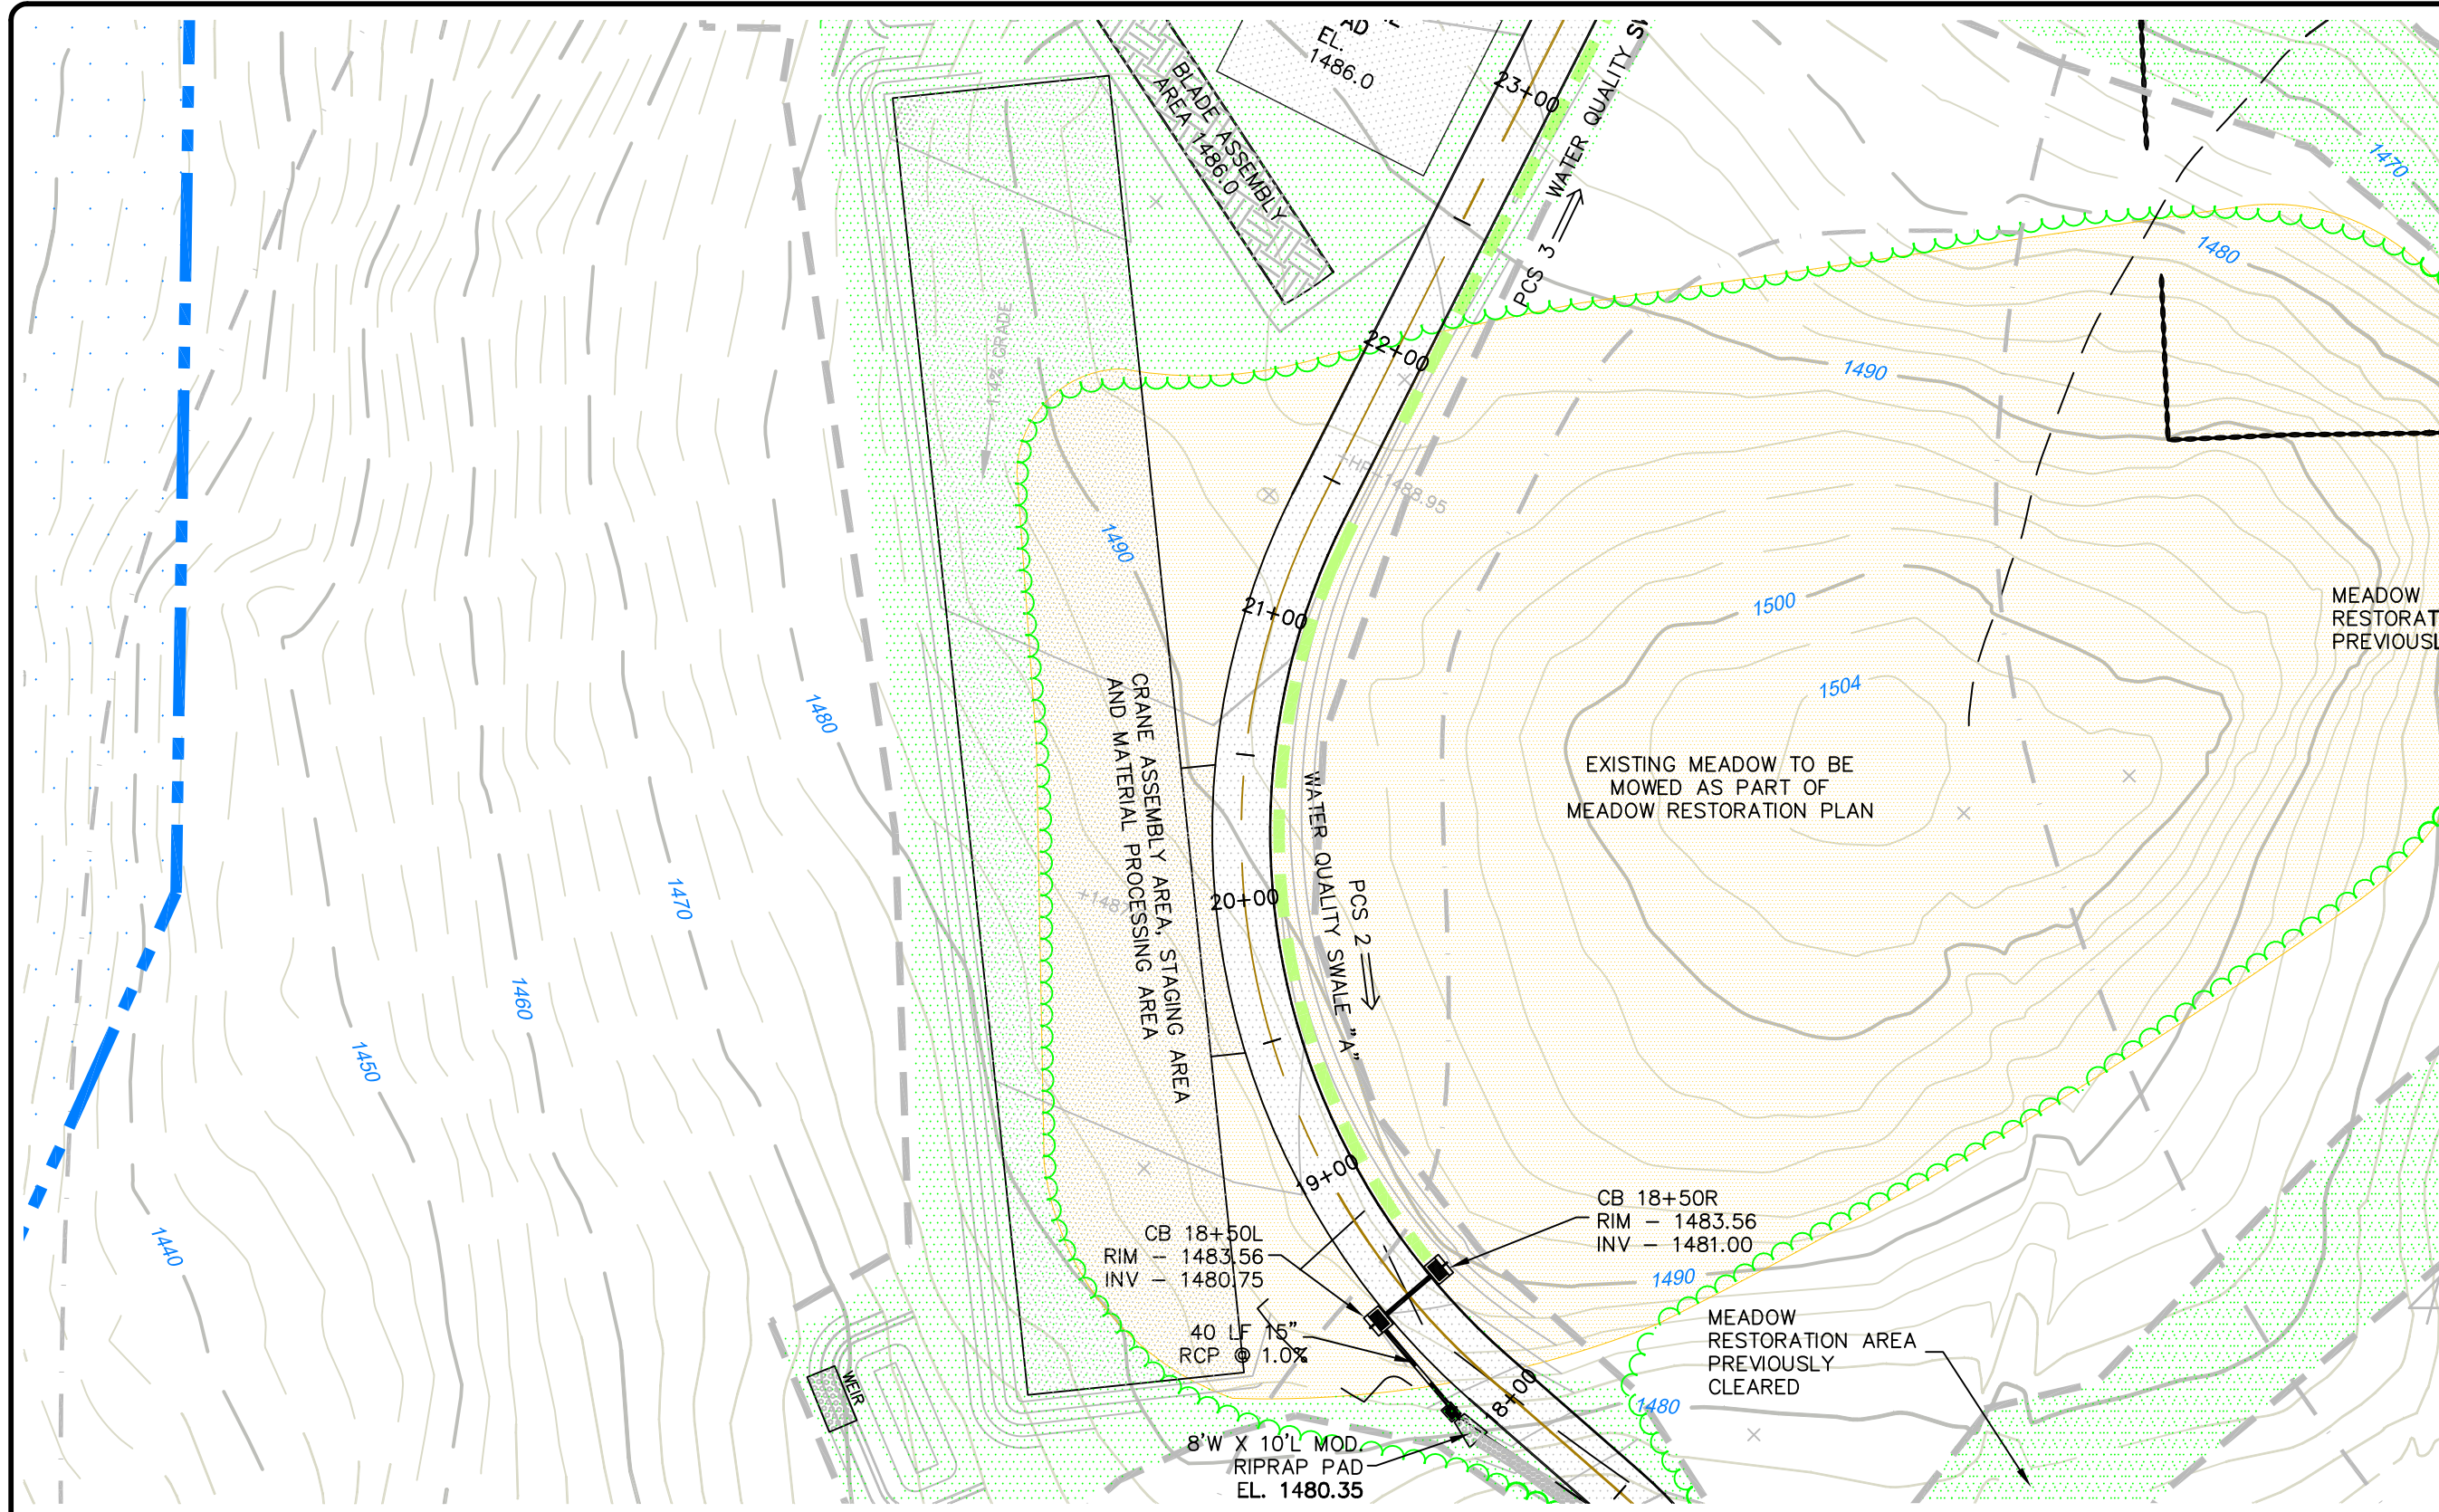


**LEGEND**

- |  |                           |  |  |  |   |
|--|---------------------------|--|--|--|---|
|  | DRY WATER QUALITY SWALE   |  | PROPERTY LINE                                    |  | EXISTING ROADWAY                        |
|  | EXISTING MEADOW           |  | EXISTING CONTOUR                                 |  | PROPOSED ACCESS DRIVE                   |
|  | VERNAL POOL AREA          |  | CONTOUR FROM CONSTRUCTION GRADING TO REMAIN      |  | PERM. RIPRAP DIVERSION/CONVEYANCE SWALE |
|  | 100' VERNAL POOL SETBACK  |  | CONTOUR FROM CONSTRUCTION GRADING TO BE MODIFIED |  | LIMITS OF CLEARING                      |
|  | 750' VERNAL POOL ENVELOPE |  | PROPOSED CONTOUR                                 |  | PROPOSED UPLAND MEADOW RESTORATION AREA |
|  |                           |  | PROPOSED STORM DRAINAGE                          |  |   |
|  |                           |  | EDGE OF WATER                                    |  |   |
|  |                           |  | WETLANDS/WATERCOURSE BOUNDARY                    |  |   |
|  |                           |  | 100' WETLANDS REVIEW AREA                        |  |   |

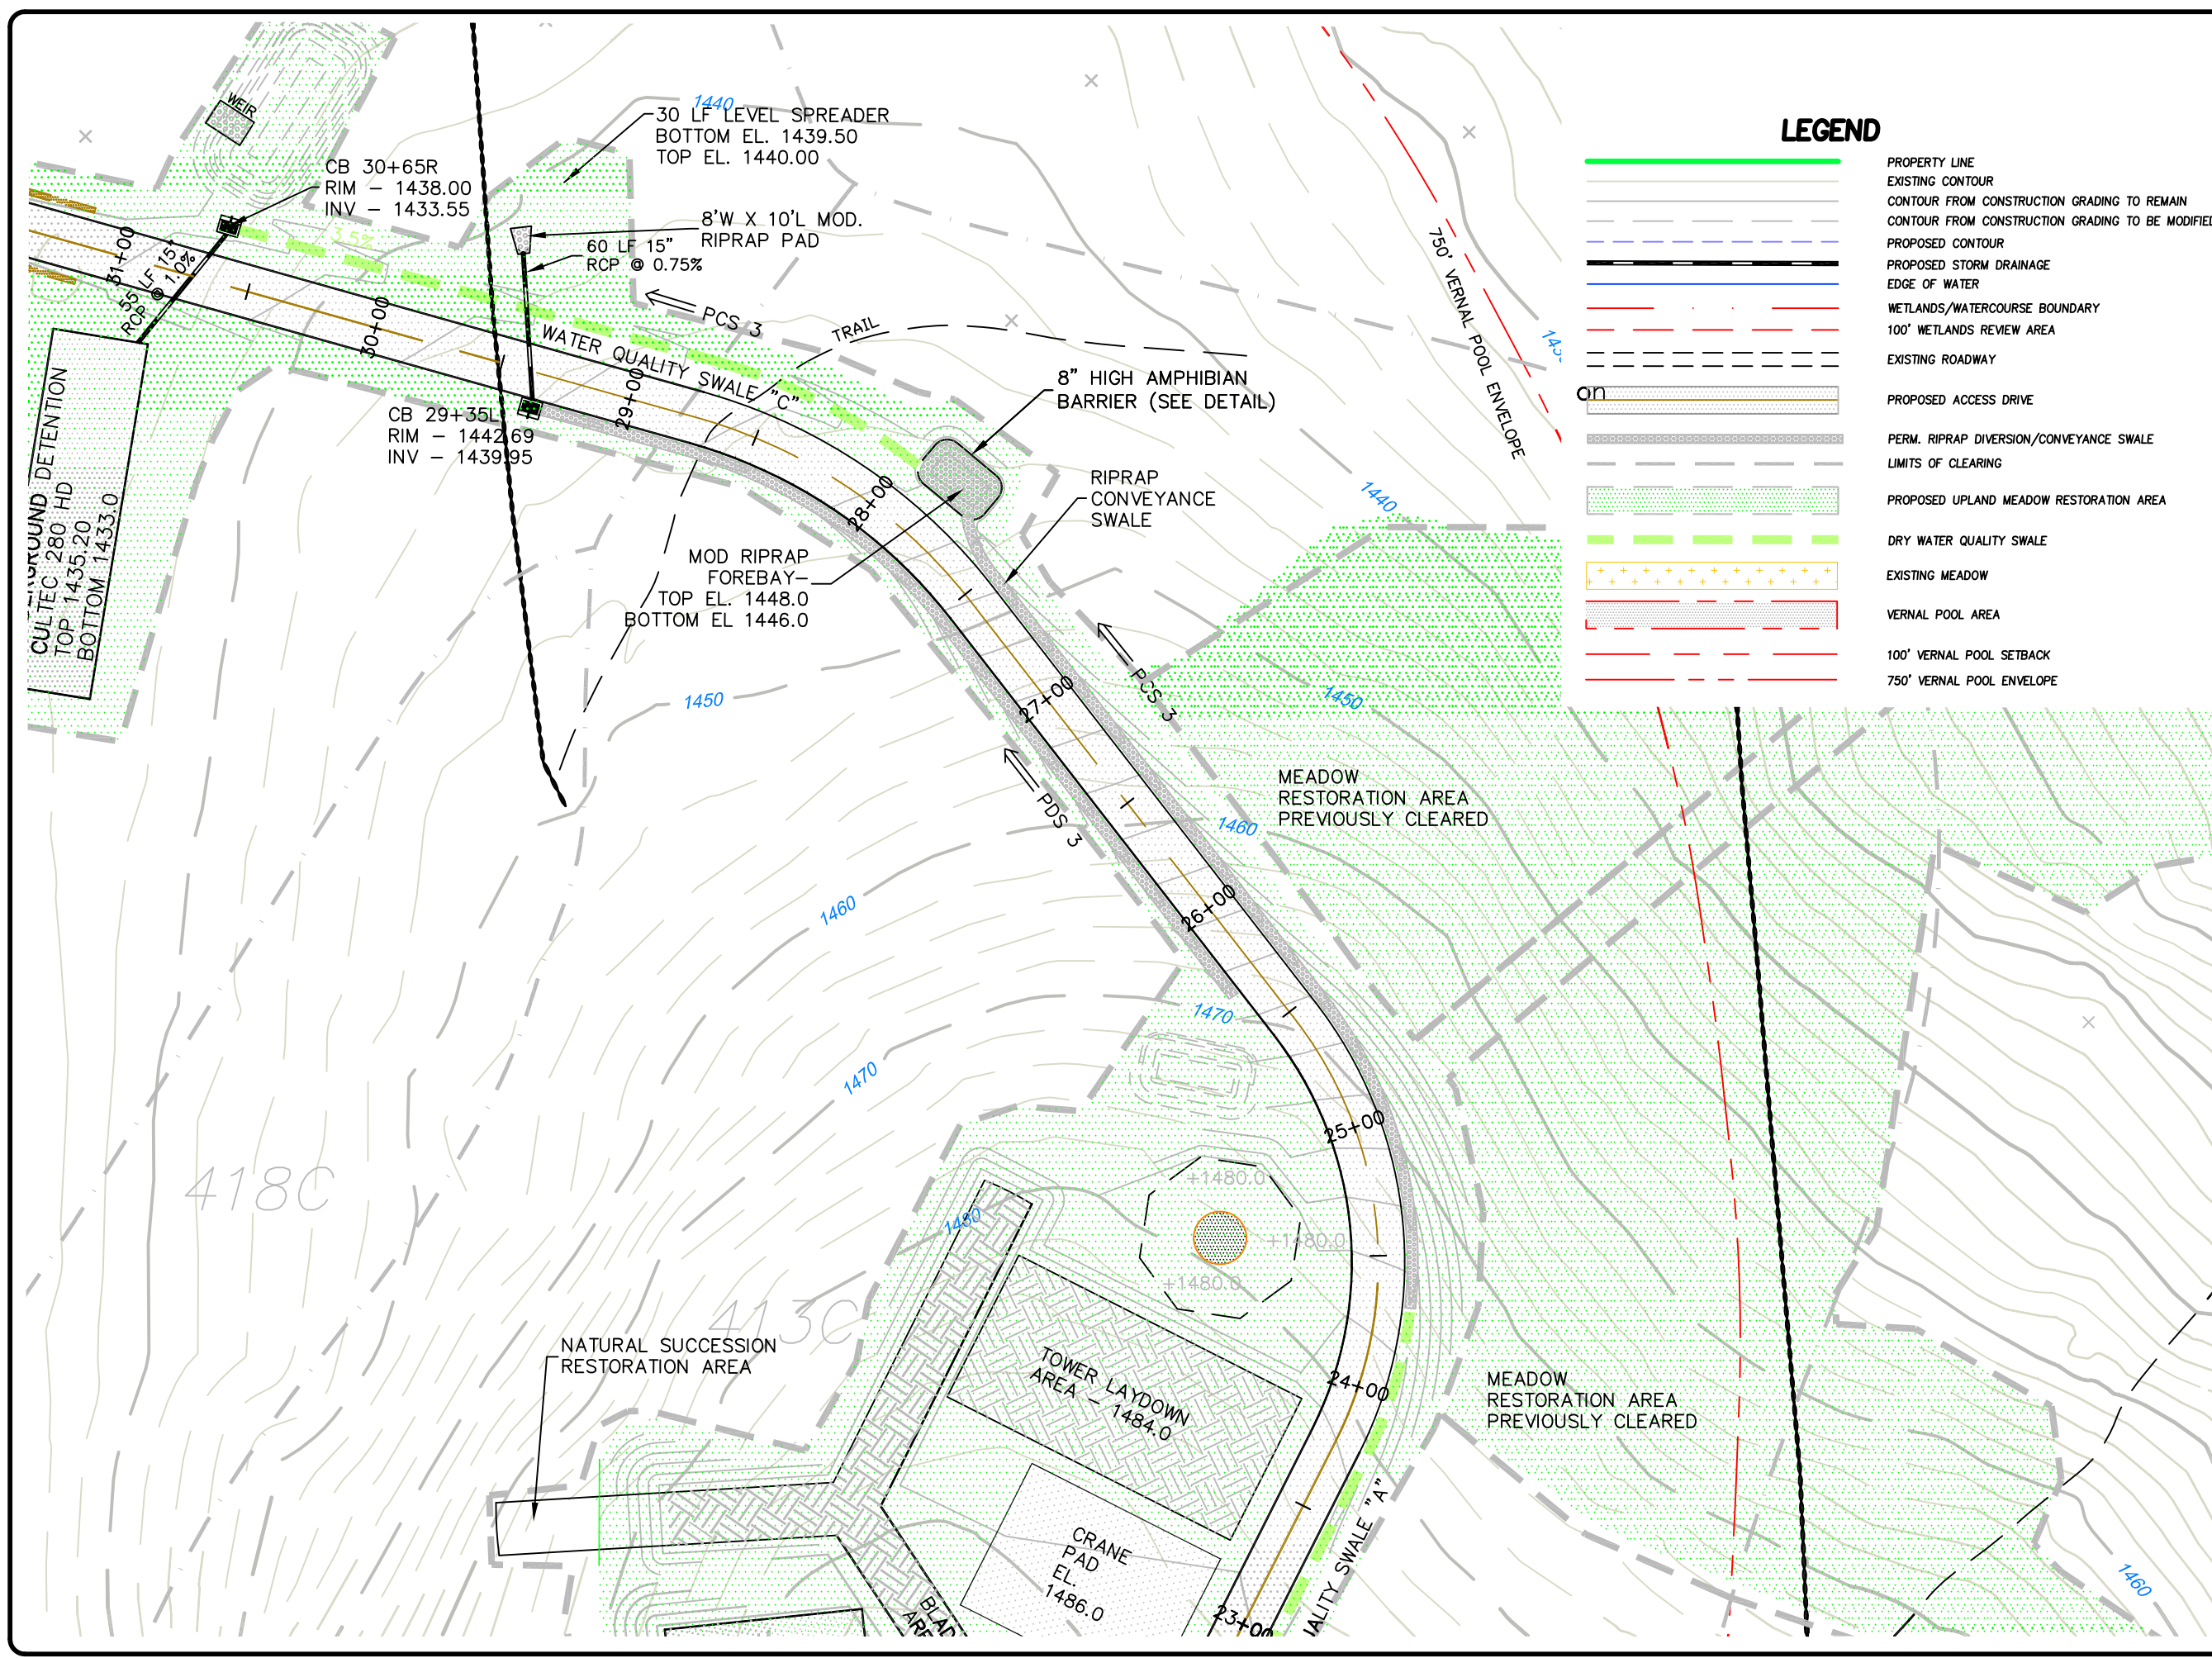

**LEGEND**

- PROPERTY LINE
- EXISTING CONTOUR
- CONTOUR FROM CONSTRUCTION GRADING TO REMAIN
- CONTOUR FROM CONSTRUCTION GRADING TO BE MODIFIED
- PROPOSED CONTOUR
- PROPOSED STORM DRAINAGE
- EDGE OF WATER
- WETLANDS/WATERCOURSE BOUNDARY
- 100' WETLANDS REVIEW AREA
- EXISTING ROADWAY
- PROPOSED ACCESS DRIVE
- PERM. RIPRAP DIVERSION/CONVEYANCE SWALE
- LIMITS OF CLEARING
- PROPOSED UPLAND MEADOW RESTORATION AREA
- DRY WATER QUALITY SWALE
- EXISTING MEADOW
- VERNAL POOL AREA
- 100' VERNAL POOL SETBACK
- 750' VERNAL POOL ENVELOPE

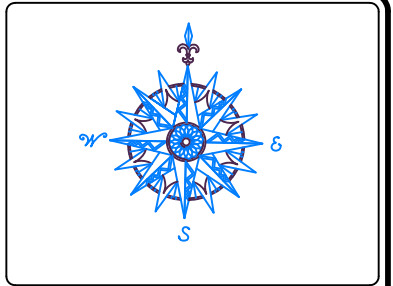

NO.	REVISION	DATE
1	REVISED PER SITING COUNCIL	24 OCT 11
2	REVISED ROAD ALIGNMENT	29 JUN 12
3	CLEARING AREA REVISED	23 JUL 12
<i>Previous Editions Obsolete</i>		



1 inch = 300 ft.

**BNE ENERGY, INC.**  
 29 SOUTH MAIN STREET  
 TOWN CENTER SUITE 200  
 WEST HARTFORD, CT 06107



**POST CONSTRUCTION GRADING PLAN**  
 TURBINE TWO AND MAIN ACCESS DRIVE  
 23+50 TO 31+30

**WIND COLEBROOK SOUTH**  
 FLAGG HILL ROAD  
 COLEBROOK CONNECTICUT



DESIGNER: BB	APPROVED: CJ
SCALE: 1" = 80'	
DATE: 26 AUG 11	
PROJ. NO.: 3092	
CADD FILE NAME: 3092	
DRAWING NO.: <b>C506</b>	



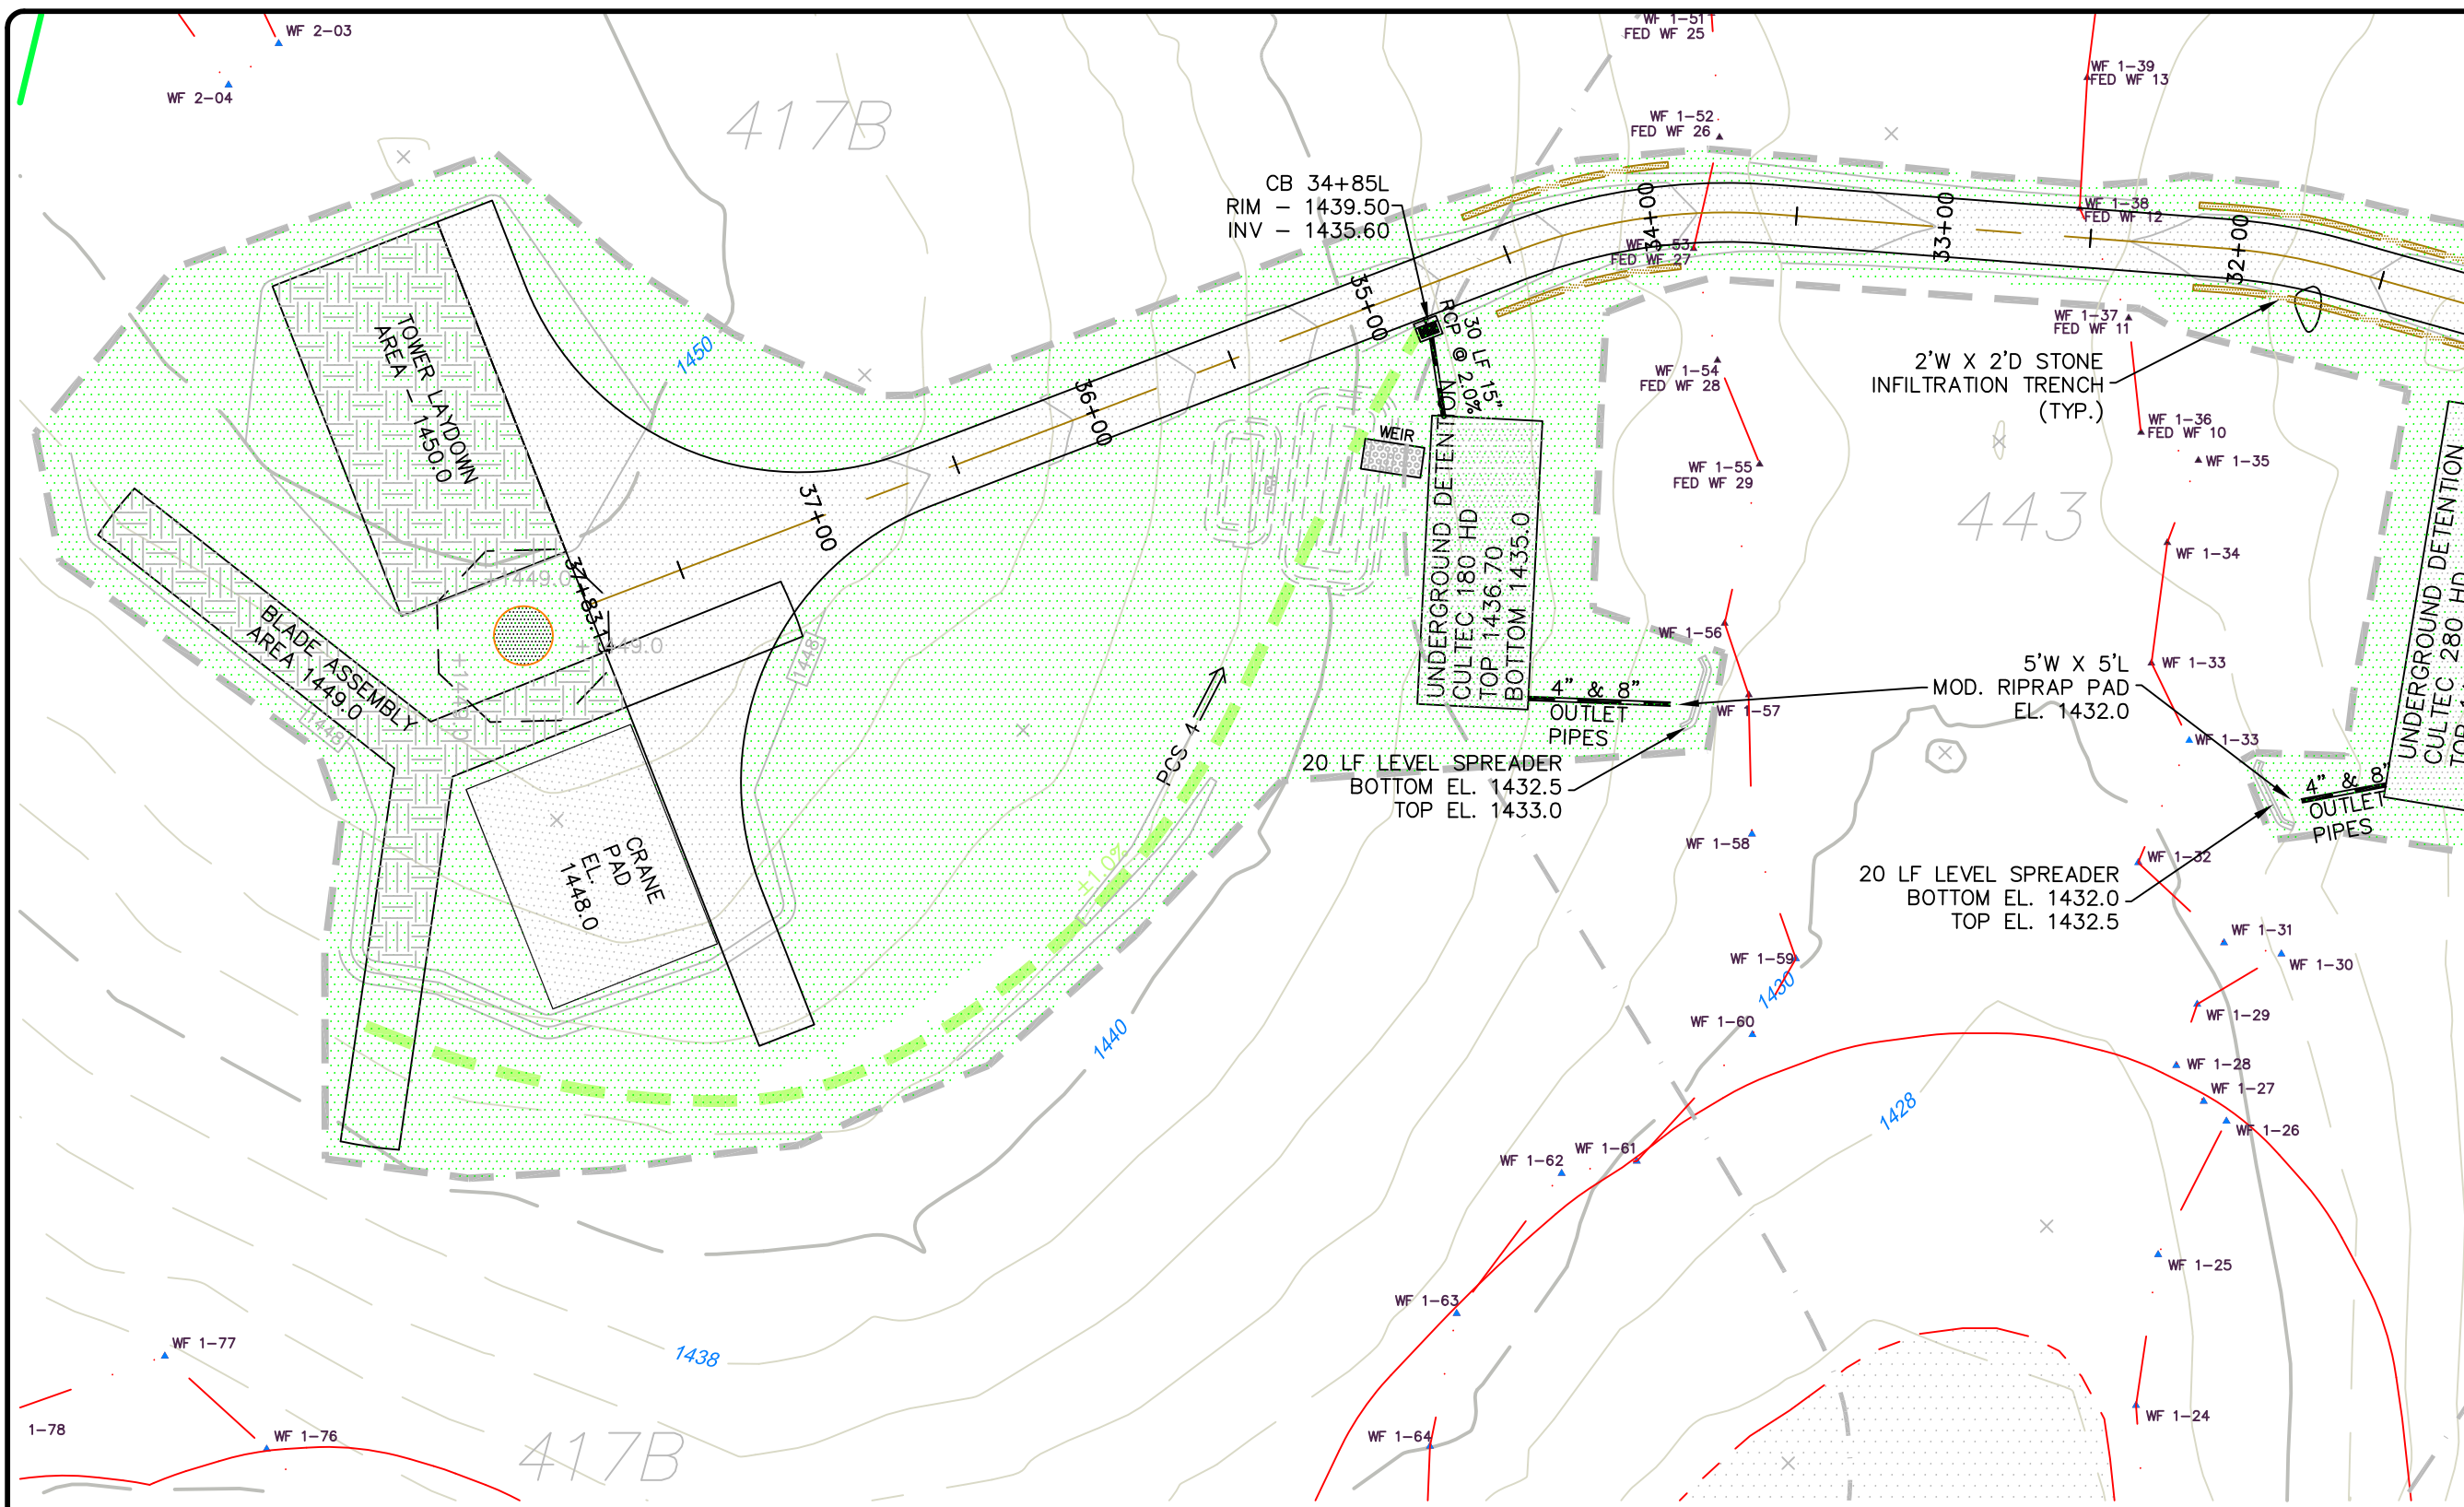

NO.	REVISION	DATE
1	REVISED PER SITING COUNCIL	24 OCT 11
2	FEDERAL WL DELINEATION ADDED	22 NOV 11
3	REVISED ROAD ALIGNMENT	29 JUN 12
<i>Previous Editions Obsolete</i>		



**BNE ENERGY, INC.**  
 29 SOUTH MAIN STREET  
 TOWN CENTER SUITE 200  
 WEST HARTFORD, CT 06107

**POST CONSTRUCTION GRADING PLAN**  
 TURBINE THREE AND MAIN ACCESS DRIVE  
 31+50 TO 37+83

**WIND COLEBROOK SOUTH**  
 FLAGG HILL ROAD  
 COLEBROOK CONNECTICUT



**CIVIL C1**  
 CORNERSTONE PROFESSIONAL PARK, SUITE D-101  
 43 SHERMAN HILL ROAD  
 WOODBURY CONNECTICUT (203) 266-0778

DESIGNER: BB	APPROVED: CJ
SCALE: 1" = 80'	
DATE: 26 AUG 11	
PROJ. NO.: 3092	
CHD. FILE NAME: 3092	
DRAWING NO.: <b>C507</b>	

**LEGEND**

- DRY WATER QUALITY SWALE
- EXISTING MEADOW
- VERNAL POOL AREA
- 100' VERNAL POOL SETBACK
- 750' VERNAL POOL ENVELOPE
- PROPERTY LINE
- EXISTING CONTOUR
- CONTOUR FROM CONSTRUCTION GRADING TO REMAIN
- CONTOUR FROM CONSTRUCTION GRADING TO BE MODIFIED
- PROPOSED CONTOUR
- PROPOSED STORM DRAINAGE
- EDGE OF WATER
- WETLANDS/WATERCOURSE BOUNDARY
- 100' WETLANDS REVIEW AREA
- EXISTING ROADWAY
- PROPOSED ACCESS DRIVE
- PERM. RIPRAP DIVERSION/CONVEYANCE SWALE
- LIMITS OF CLEARING
- PROPOSED UPLAND MEADOW RESTORATION AREA




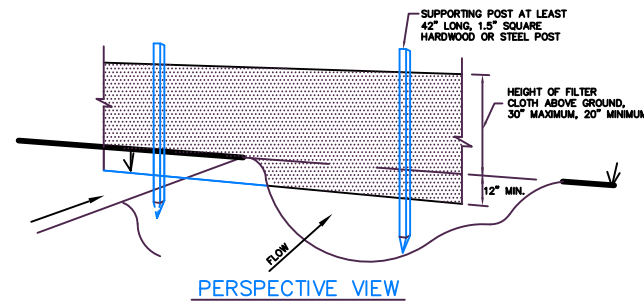

**CONSTRUCTION NOTES FOR SILT FENCE**

- EXCAVATE A TRENCH A MINIMUM OF 6 INCHES DEEP AND 6 INCHES WIDE ON THE UP SIDE OF THE FENCE LOCATION.
  - DRIVE SUPPORT POSTS ON THE DOWN SLOPE SIDE OF THE TRENCH TO A DEPTH OF AT LEAST 12 INCHES INTO ORIGINAL GROUND.
  - STAPLE OR SECURE THE GEOTEXTILE TO THE SUPPORT POSTS PER MANUFACTURER'S INSTRUCTIONS SUCH THAT AT LEAST 6 INCHES OF GEOTEXTILE LIES WITHIN THE TRENCH.
  - BACKFILL THE TRENCH WITH TAMPED SOIL OR AGGREGATE OVER THE GEOTEXTILE.
- POSTS: 1.5" SQUARE HARDWOOD OR STEEL  
 FILTER CLOTH: MIRAFI 100X, ENVROFENCE OR APPROVED EQUAL



**SILT FENCE DETAIL**



STOCKPILE MANAGEMENT PER 2002 CT GUIDELINES FOR E & S CONTROL:

- LOCATE STOCKPILE SO THAT NATURAL DRAINAGE IS NOT OBSTRUCTED.
- DIVERT RUNOFF WATER AWAY FROM OR AROUND THE STOCKPILE.
- INSTALL A GEOTEXTILE SILT FENCE OR HAY BALE BARRIER AROUND THE STOCKPILE AREA APPROXIMATELY 10 FEET FROM PROPOSED TOE OF THE SLOPE.
- THE SIDE SLOPES OF STOCKPILED MATERIAL SHOULD BE NO STEEPER THAN 2:1.
- STOCKPILES THAT ARE NOT TO BE USED WITHIN 30 DAYS NEED TO BE SEEDED AND MULCHED IMMEDIATELY AFTER FORMATION OF THE STOCKPILE.
- AFTER STOCKPILE HAS BEEN REMOVED, THE SITE SHOULD BE GRADED AND PERMANENTLY STABILIZED.

**TEMPORARY TOPSOIL STOCKPILE**

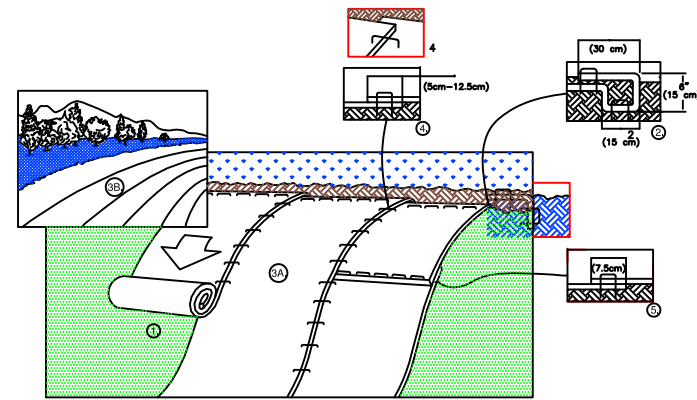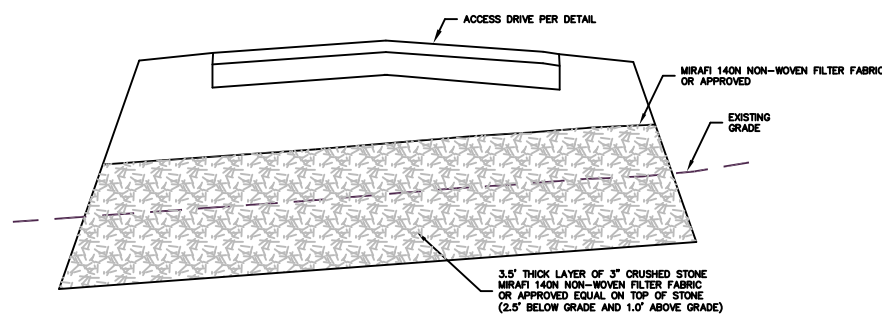

- PREPARE SOIL BEFORE INSTALLING BLANKETS, INCLUDING ANY NECESSARY APPLICATION OF LIME, FERTILIZER, AND SEED. NOTE: WHEN USING CELL-O-SEED DO NOT SEED PREPARED AREA. CELL-O-SEED MUST BE INSTALLED WITH PAPER SIDE DOWN.
- BEGIN AT THE TOP OF THE SLOPE BY ANCHORING THE BLANKET IN A 6" (15cm) DEEP X 6" (15cm) WIDE TRENCH WITH APPROXIMATELY 12" (30cm) OF BLANKET EXTENDED BEYOND THE UP-SLOPE PORTION OF THE TRENCH. ANCHOR THE BLANKET WITH A ROW OF STAPLES/STAKES APPROXIMATELY 12" (30cm) APART IN THE BOTTOM OF THE TRENCH. BACKFILL AND COMPACT THE TRENCH AFTER STAPLING. APPLY SEED TO COMPACTED SOIL AND FOLD REMAINING 12" (30cm) PORTION OF BLANKET BACK OVER SEED AND COMPACTED SOIL. SECURE BLANKET OVER COMPACTED SOIL WITH A ROW OF STAPLES/STAKES SPACED APPROXIMATELY 12" (30cm) APART ACROSS THE WIDTH OF THE BLANKET.
- ROLL THE BLANKETS (A) DOWN OR (B) HORIZONTALLY ACROSS THE SLOPE. BLANKETS WILL UNROLL WITH APPROPRIATE SIDE AGAINST THE SOIL SURFACE. ALL BLANKETS MUST BE SECURELY FASTENED TO SOIL SURFACE BY PLACING STAPLES/STAKES IN APPROPRIATE LOCATIONS AS SHOWN IN STAPLE PATTERN GUIDE. WHEN USING OPTIONAL DOT SYSTEM, STAPLES/STAKES SHOULD BE PLACED THROUGH EACH OF THE COLORED DOTS CORRESPONDING TO THE APPROPRIATE STAPLE PATTERN.
- THE EDGES OF PARALLEL BLANKETS MUST BE STAPLED WITH APPROXIMATELY 2"-5" (5cm-12.5cm) OVERLAP DEPENDING ON BLANKET TYPE. TO ENSURE PROPER SEAM ALIGNMENT, PLACE THE EDGE OF THE OVERLAPPING BLANKET (BLANKET BEING INSTALLED ON TOP) EVEN WITH THE COLORED SEAM STRIP ON THE PREVIOUSLY INSTALLED BLANKET.
- CONSECUTIVE BLANKETS SPUNCE DOWN THE SLOPE MUST BE PLACED END OVER END (SHINGLE STYLE) WITH AN APPROXIMATE 3" (7.5cm) OVERLAP. STAPLE THROUGH OVERLAPPED AREA, APPROXIMATELY 12" (30cm) APART ACROSS ENTIRE BLANKET WIDTH.


NOTE:  
 \*IN LOOSE SOIL CONDITIONS, THE USE OF STAPLE OR STAKE LENGTHS GREATER THAN 6" (15cm) MAY BE NECESSARY TO PROPERLY SECURE THE BLANKETS.

**EROSION CONTROL BLANKETS**

S150BN: Material:  
 100% Straw fiber matrix sewn between two bio-degradable nets.  
 Net: Temporary lightweight bio-degradable (Both sides)


- CRITICAL POINTS  
 A. OVERLAPS AND SEAMS  
 B. PROJECTED WATER LINE  
 C. CHANNEL BOTTOM/SIDE SLOPE VERTICES
- NOTE:  
 \* HORIZONTAL STAPLE SPACING SHOULD BE ALTERED IF NECESSARY TO ALLOW STAPLES TO SECURE THE CRITICAL POINTS ALONG THE CHANNEL SURFACE.  
 \* IN LOOSE SOIL CONDITIONS, THE USE OF STAPLE OR STAKE LENGTHS IN EXCESS OF 6" (15 cm) MAY BE NECESSARY TO PROPERLY ANCHOR THE BLANKETS.

**EROSION CONTROL BLANKET**

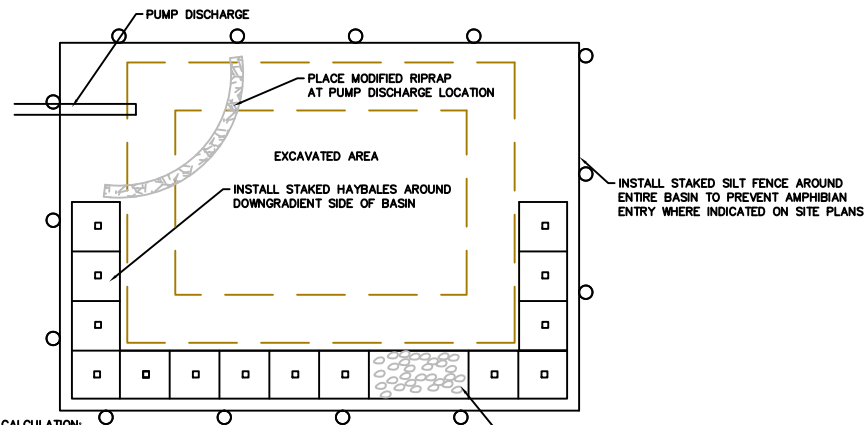


BASIN SIZING CALCULATION:  
 CUBIC FEET OF STORAGE = PUMP DISCHARGE RATE (GPM) X 16  
 CUBIC FEET OF STORAGE = 100 GPM X 16 = 1,600 CUBIC FEET  
 BASIN DIMENSIONS - 16'W X 35'L X 3'D = 1,680 CUBIC FEET OF STORAGE PROVIDED

**DEWATERING SETTLING BASIN**

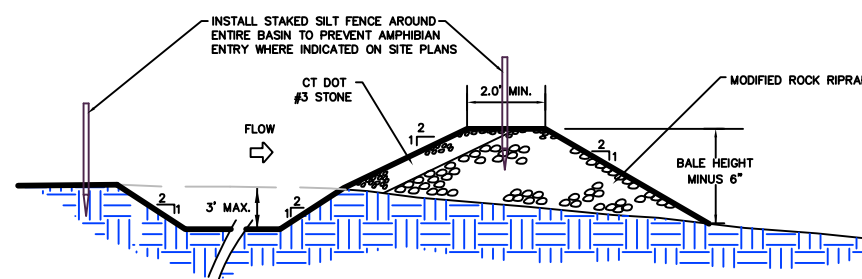


**DEWATERING SETTLING BASIN OUTLET**

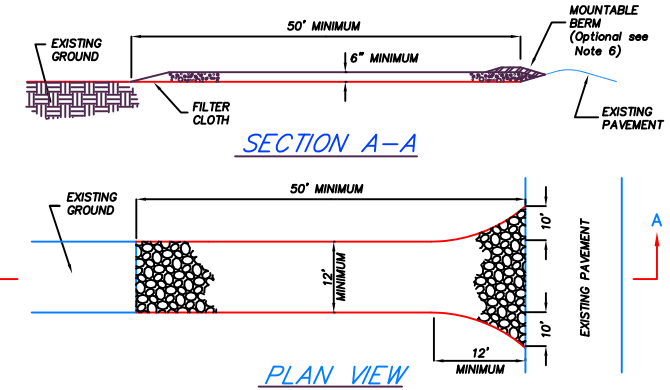

**NOTES:**

- STONE SIZE - USE 1" - 2" STONE, OR RECLAIMED OR RECYCLED CONCRETE EQUIVALENT.
- LENGTH - AS REQUIRED, BUT NOT LESS THAN 50 FEET.
- THICKNESS - NOT LESS THAN SIX (6) INCHES.
- WIDTH - 12 FOOT MINIMUM, BUT NOT LESS THAN THE FULL WIDTH AT POINTS WHERE INGRESS OR EGRESS OCCURS. 24 FOOT MINIMUM IF SINGLE ENTRANCE TO SITE.
- FILTER CLOTH - TO BE PLACED OVER THE ENTIRE AREA PRIOR TO PLACING OF STONE.
- SURFACE WATER - ALL SURFACE WATER FLOWING OR DIVERTED TOWARD CONSTRUCTION ENTRANCES SHALL BE PIPED ACROSS THE ENTRANCE. IF PIPING IS IMPRACTICAL, A MOUNTABLE BERM WITH 5:1 SLOPES WILL BE PERMITTED.
- MAINTENANCE - THE ENTRANCE SHALL BE MAINTAINED IN A CONDITION WHICH WILL PREVENT TRACKING OF FLOWING OF SEDIMENT ONTO PUBLIC RIGHTS-OF-WAY. THIS MAY REQUIRE PERIODIC TOP DRESSING WITH ADDITIONAL STONE AS CONDITIONS DEMAND AND REPAIR AND/OR CLEANOUT OF ANY MEASURE USED TO TRAP SEDIMENT. ALL SEDIMENT SPILLED, DRIPPED, WASHED OR TRACKED ONTO PUBLIC RIGHTS-OF-WAY MUST BE REMOVED IMMEDIATELY.
- WASHING - WHEELS SHALL BE CLEANED TO REMOVE SEDIMENT PRIOR TO ENTRANCE ONTO PUBLIC RIGHTS-OF-WAY. WHEN WASHING IS REQUIRED, IT SHALL BE DONE ON AN AREA STABILIZED WITH STONE AND WHICH DRAINS INTO AN APPROVED SEDIMENT TRAPPING DEVICE.
- PERIODIC INSPECTION AND NEEDED MAINTENANCE SHALL BE PROVIDED AFTER EACH RAIN.

**STABILIZED CONSTRUCTION ENTRANCE**

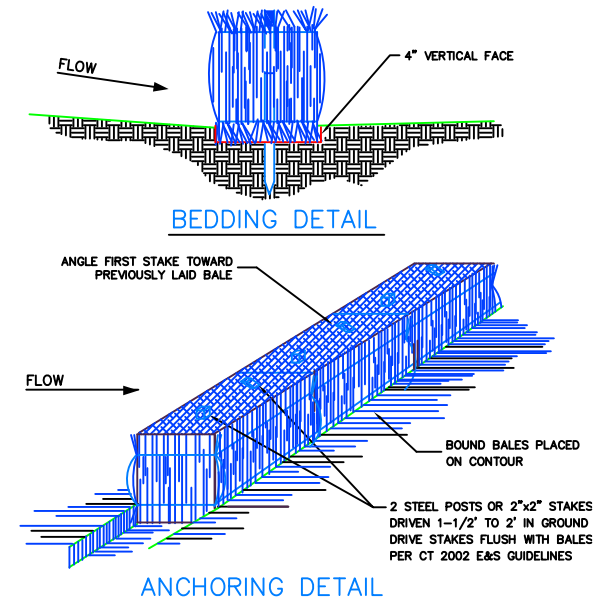

**NOTES:**

- BALES SHALL BE EITHER STRAW OR HAY.
- BALES SHALL BE PLACED AT THE TOE OF SLOPE OR ON THE CONTOUR AND IN A ROW WITH ENDS TIGHTLY ABUTTING THE ADJACENT BALES.
- EACH BALE SHALL BE EMBEDDED IN THE SOIL A MINIMUM OF 4 INCHES, AND PLACED SO THE BINDINGS ARE HORIZONTAL.
- BALES SHALL BE SECURELY ANCHORED IN PLACE BY EITHER TWO STAKES OR RE-BARS DRIVEN THROUGH THE BALE. THE FIRST STAKE IN EACH BALE SHALL BE DRIVEN TOWARD THE PREVIOUSLY LAID BALE AT AN ANGLE TO FORCE THE BALES TOGETHER. STAKES SHALL BE DRIVEN FLUSH WITH THE BALE.
- INSPECTION SHALL BE FREQUENT, AND REPAIR AND/OR REPLACEMENT SHALL BE MADE PROMPTLY AS NEEDED TO MAINTAIN EFFECTIVENESS OF INSTALLATION.
- BALES SHALL BE REMOVED WHEN THEY HAVE SERVED THEIR USEFULNESS SO AS NOT TO BLOCK OR IMPEDE STORM FLOW OR DRAINAGE.

**STAKED HAY BALE BARRIER**

NO.	REVISION	DATE
1	REVISED PER SITING COUNCIL	24 OCT 11

Previous Editions Obsolete

**BNE ENERGY, INC.**  
 29 SOUTH MAIN STREET  
 TOWN CENTER SUITE 200  
 WEST HARTFORD, CT 06107

**DETAILS**

**WIND COLEBROOK SOUTH**  
 FLAGG HILL ROAD


COLEBROOK CONNECTICUT




CORNERSTONE PROFESSIONAL PARK, SUITE D-101  
 43 SHERMAN HILL ROAD  
 WOODBURY CONNECTICUT (203) 266-0778

DRAWN: BB	APPROVED: CJ
SCALE: N.T.S.	
DATE: 26 AUG 11	
PROJ. NO.: 3092	
CADD FILE NAME: 3092	
DRAWING NO.:	


**C601**




**TEMPORARY DIVERSION SWALE**

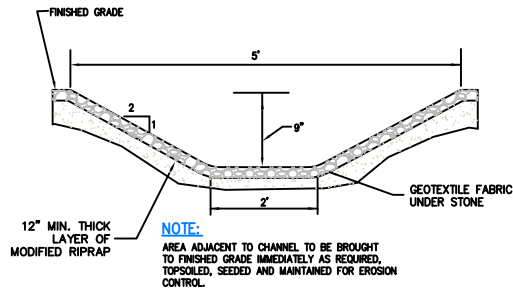


**RIPRAP DIVERSION/CONVEYANCE SWALE**

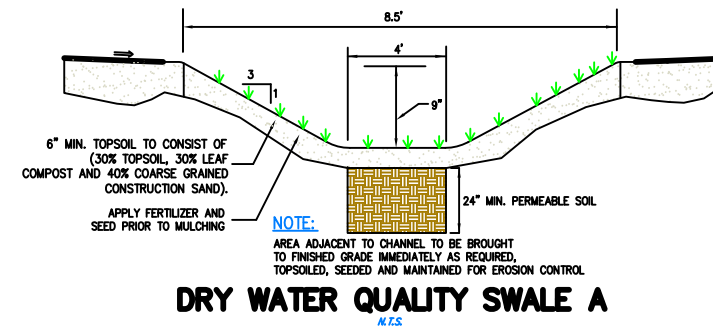


**DRY WATER QUALITY SWALE A**

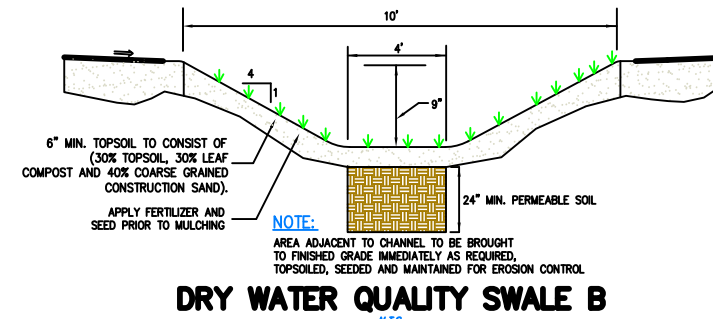


**DRY WATER QUALITY SWALE B**

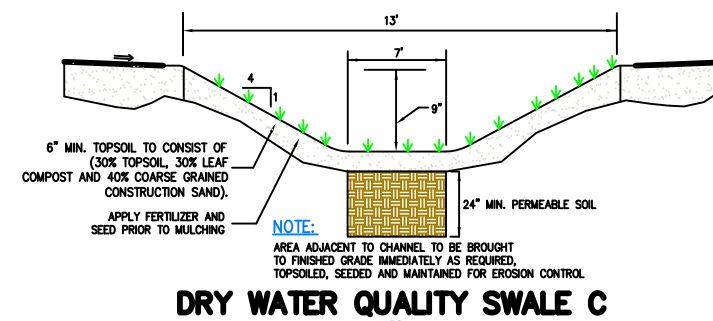


**DRY WATER QUALITY SWALE C**




**LEVEL SPREADER DETAIL**

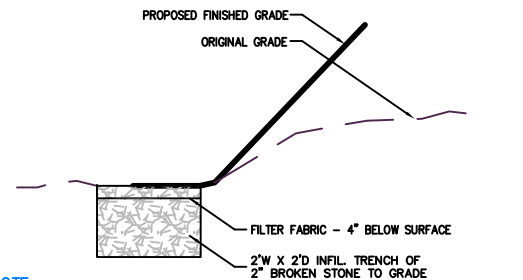


**STONE INFILTRATION TRENCH**

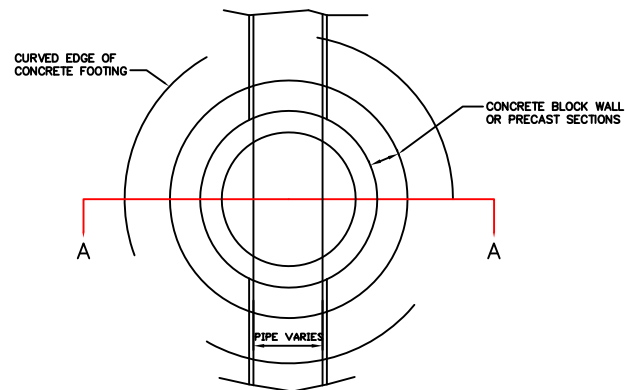




**DRAINAGE MANHOLE**



**STANDARD TYPE "CL" CATCH BASIN**

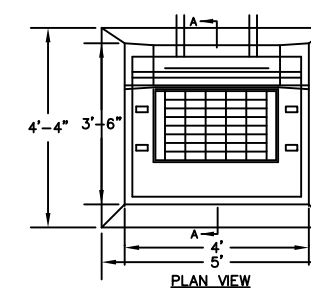

**STANDARD TYPE "C" CATCH BASIN**

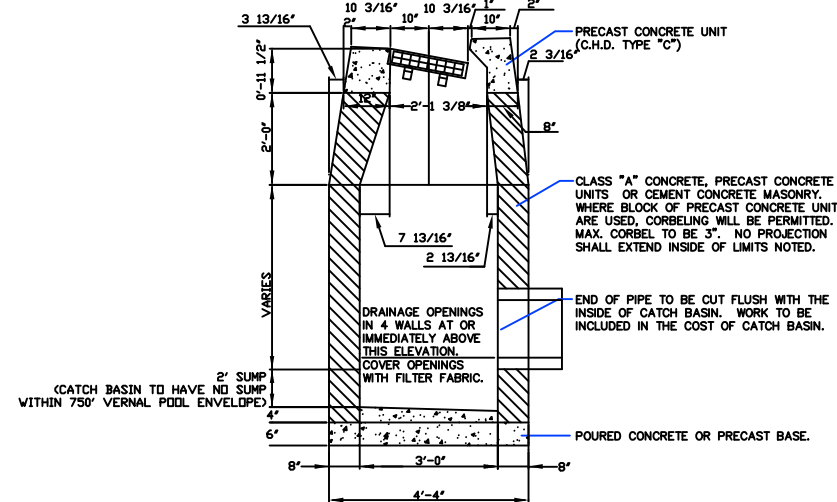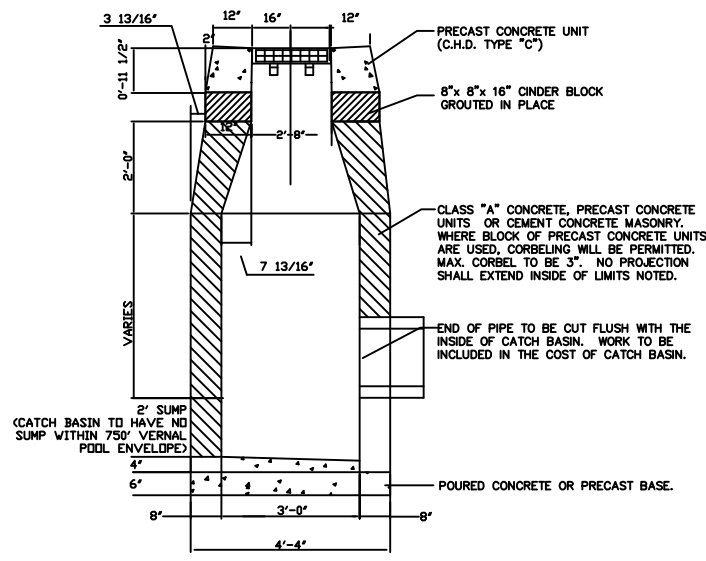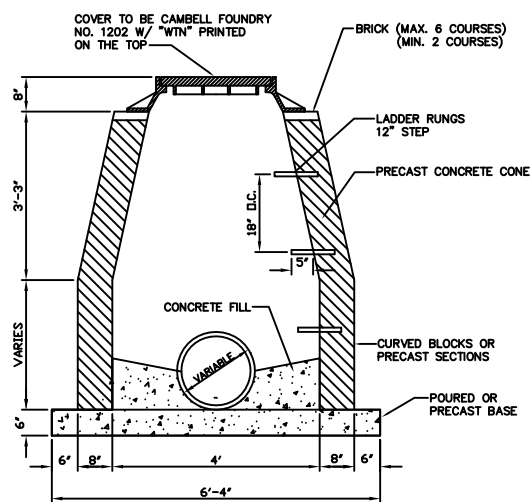

NO.	REVISION	DATE

BNE ENERGY, INC.  
29 SOUTH MAIN STREET  
TOWN CENTER SUITE 200  
WEST HARTFORD, CT 06107


DETAILS

WIND COLEBROOK SOUTH  
FLAGG HILL ROAD

**CIVIL**

CORNERSTONE PROFESSIONAL PARK, SUITE D-101  
43 SHERMAN HILL ROAD  
WOODBURY CONNECTICUT (203) 266-0778


DESIGNER: BB	APPROVED: CJ
SCALE: N.T.S.	
DATE: 26 AUG 11	
PROJECT NO.: 3092	
CADD FILE NAME: 3092	
DRAWING NO.: C602	

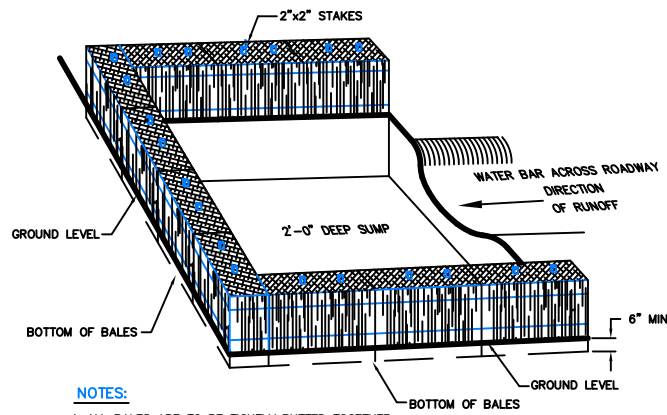

NOTES:

- 1. ALL BALES ARE TO BE TIGHTLY BUTTED TOGETHER.
2. BALES SHALL BE EITHER STRAW OR HAY.
3. PROVIDE FREQUENT INSPECTION AND MAINTENANCE. REMOVE ACCUMULATED SEDIMENT AND REPLACE CLOGGED BALES TO RESTORE EFFECTIVENESS OF INSTALLATION.


WATER BAR WITH HAY BALE TRAP

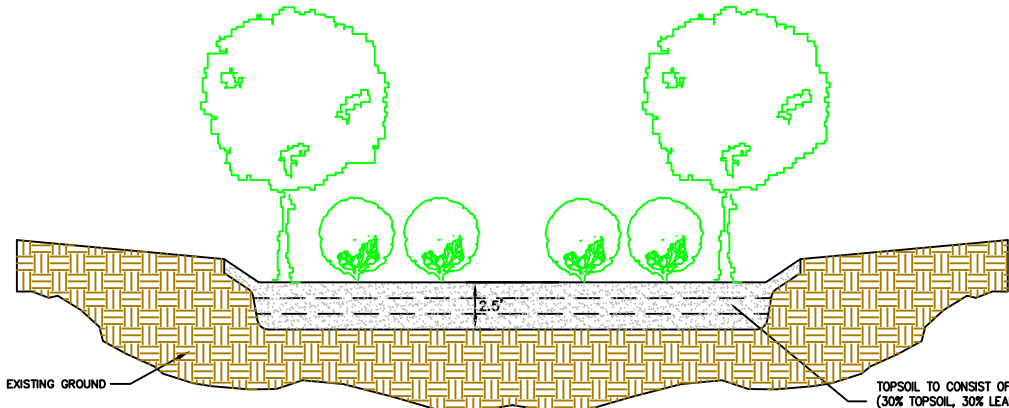


BIORETENTION AREA SOIL LAYERING DETAIL

NOTES:


- EXCAVATE RAIN GARDEN AREAS TO PROPOSED INVERT DEPTHS AND SCARIFY EXISTING SOIL SURFACES, TAKING CARE NOT TO COMPACT THE IN-SITU MATERIALS
-PLACE TOPSOIL IN 8"-12" LIFTS, DO NOT COMPACT
-LIFTS MAY BE LIGHTLY WATERED TO ENCOURAGE NATURAL COMPACTION
-OVERFILL OF TOPSOIL IS REQUIRED TO ACCOMMODATE NATURAL SETTLEMENT TO PROPER GRADE

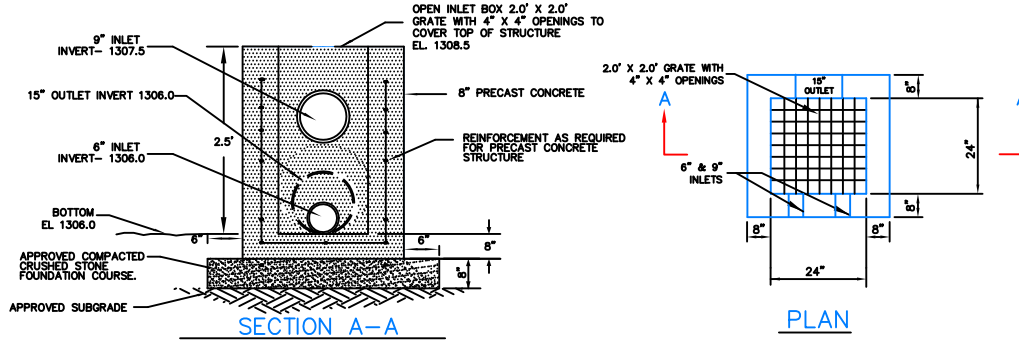

STORMWATER POND #1 OUTLET CONTROL STRUCTURE

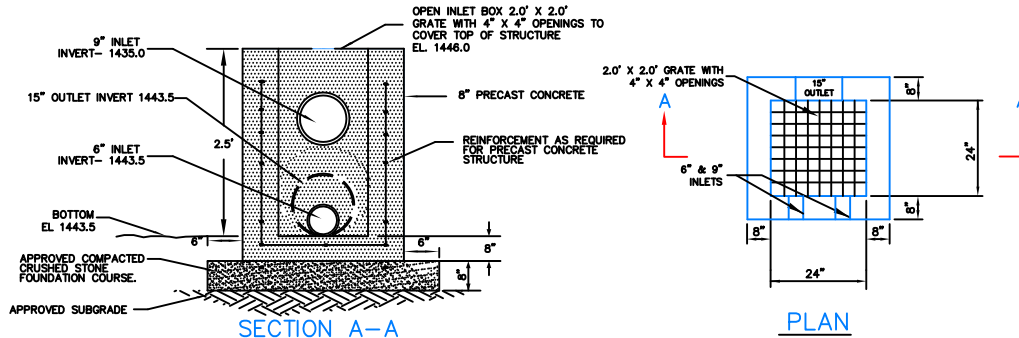


DETENTION/INFILTRATION BASIN #2 OUTLET CONTROL STRUCTURE



AMPHIBIAN BARRIER DETAIL


USE WITHIN 750' OF VERNAL POOL AREAS

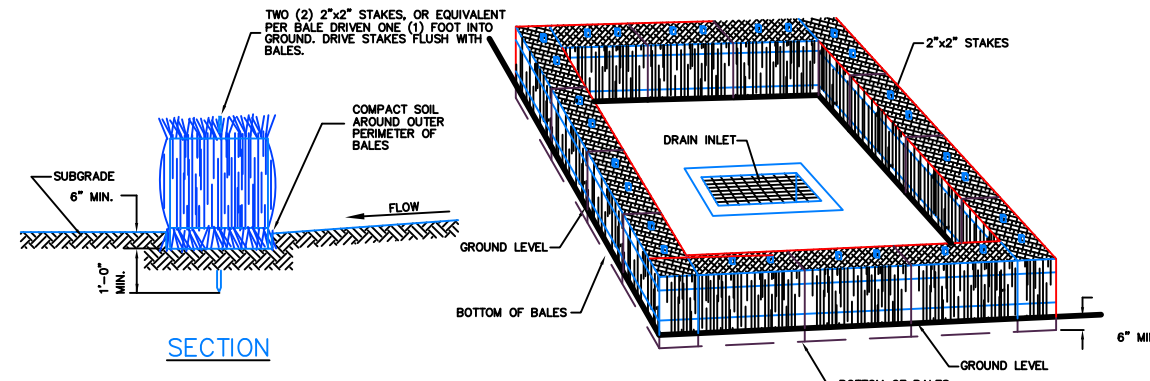

NOTES:


- 1. ALL BALES ARE TO BE TIGHTLY BUTTED TOGETHER.
2. BALES SHALL BE EITHER STRAW OR HAY.
3. PROVIDE FREQUENT INSPECTION AND MAINTENANCE. REMOVE ACCUMULATED SEDIMENT AND REPLACE CLOGGED BALES TO RESTORE EFFECTIVENESS OF INSTALLATION.

BALED FILTER

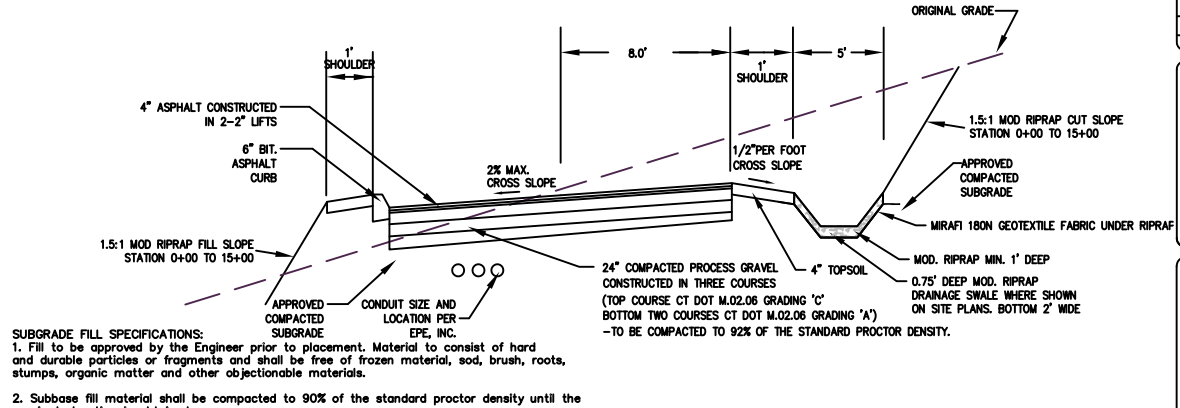


ACCESS DRIVE CROSS SECTION

- 1. Fill to be approved by the Engineer prior to placement. Material to consist of hard and durable particles or fragments and shall be free of frozen material, sod, brush, roots, stumps, organic matter and other objectionable materials.
2. Subbase fill material shall be compacted to 90% of the standard proctor density until the required elevation is obtained.
3. Subbase and fill specifications to be confirmed and modified as necessary after site analysis by geotechnical engineer. Access drive design must be able to accommodate all proposed construction vehicles including crawler crane.

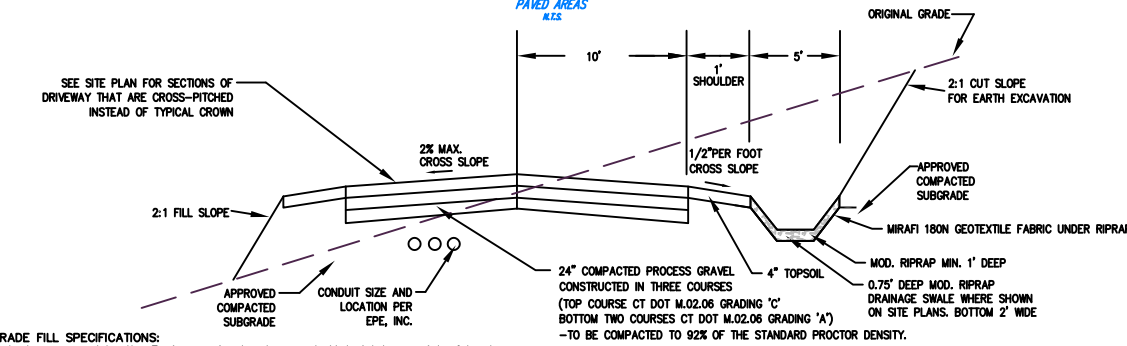

ACCESS DRIVE CROSS SECTION

- 1. Fill to be approved by the Engineer prior to placement. Material to consist of hard and durable particles or fragments and shall be free of frozen material, sod, brush, roots, stumps, organic matter and other objectionable materials.
2. Subbase fill material shall be compacted to 90% of the standard proctor density until the required elevation is obtained.
3. Subbase and fill specifications to be confirmed and modified as necessary after site analysis by geotechnical engineer. Access drive design must be able to accommodate all proposed construction vehicles including crawler crane.

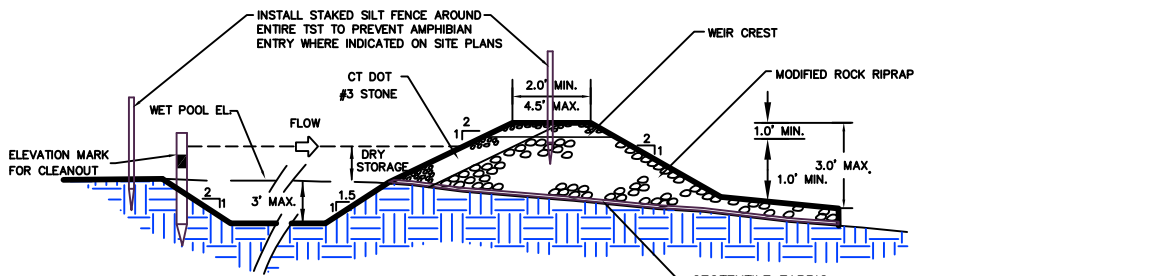

TEMPORARY SEDIMENT TRAP OUTLET

Revision table with columns for NO., REVISION, and DATE. Revision 1: REVISED PER ENV. CONSULTANT, 28 AUG 12.

BNE ENERGY, INC.
29 SOUTH MAIN STREET
TOWN CENTER SUITE 200
WEST HARTFORD, CT 06107

DETAILS

WIND COLEBROOK SOUTH
FLAGG HILL ROAD


COLEBROOK CONNECTICUT



CORNERSTONE PROFESSIONAL PARK, SUITE D-101
43 SHERMAN HILL ROAD
WOODBURY (203) 266-0778 CONNECTICUT

DRW: BB, APPR: CJ
SCALE: N.T.S.
DATE: 26 AUG 11
PROJ. NO.: 3092
CADD FILE NAME: 3092
DRAWING NO.:

C603

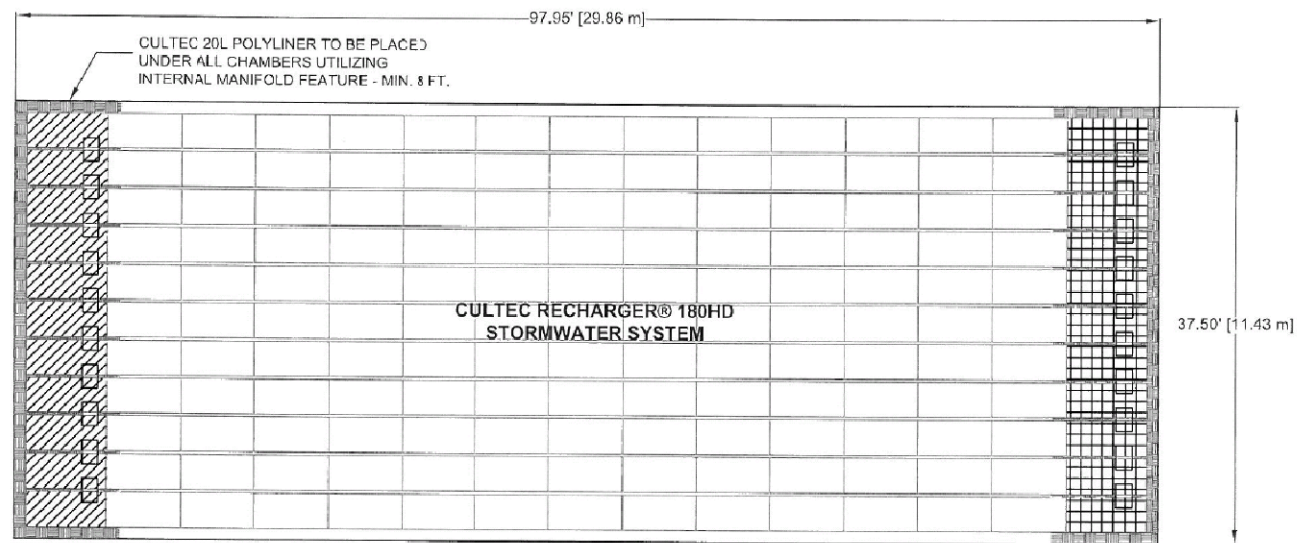


**MATERIALS LIST**

DESCRIPTION	QUANTITY	UNIT
RECHARGER 180SHD STARTER	11	PIECES
RECHARGER 180SHD INTERMEDIATE	143	PIECES
RECHARGER 180SHD END	11	PIECES
H.V.LV FC-24 FEED CONNECTORS	20	PIECES
CULTEC NO. 410 FILTER FABRIC 7.5' x 30'	4	ROLLS
CULTEC NO. 20L POLYETHYLENE LINER	150	SQUARE FEET
1 1/2 - 2 INCH DIAMETER BROKEN STONE	234	CUBIC YARDS
VOLUME OF EXCAVATION	460	CUBIC YARDS

**CULTEC RECHARGER® 180HD LEGEND**

- RECHARGER 180SHD STARTER
- RECHARGER 180SHD INTERMEDIATE
- RECHARGER 180SHD END
- H.V.LV FC-24 FEED CONNECTORS
- CULTEC NO. 20L POLYETHYLENE LINER

**CULTEC STORMWATER MANAGEMENT SYSTEM**  
**STORAGE REQUIRED: 6,000 c.f.**  
**STORAGE PROVIDED: 6,164 c.f.**  
*\*INSTALLED USING TYPICAL STONE REQUIREMENTS OF 6 INCHES ABOVE AND BELOW CHAMBERS AND A 1 FT. BORDER SURROUNDING*

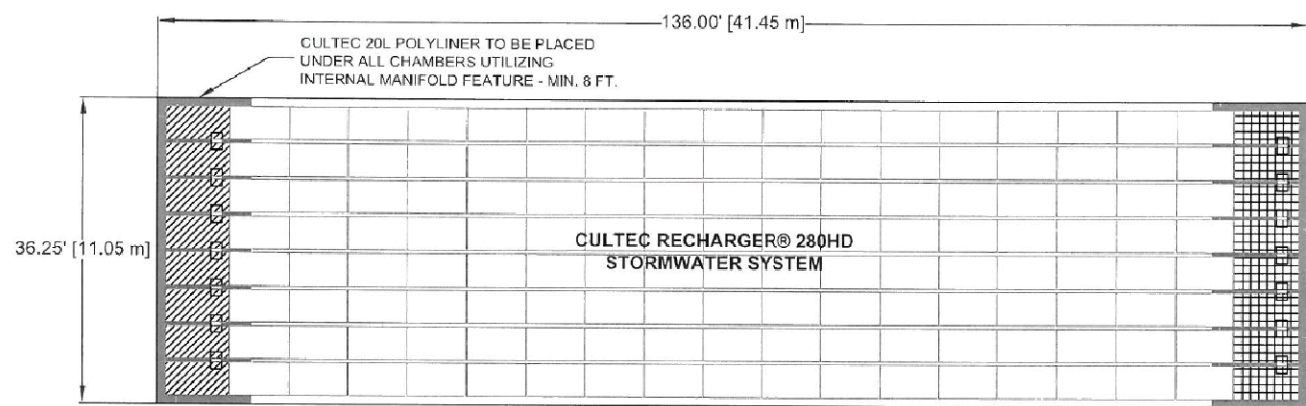

**MATERIALS LIST**

DESCRIPTION	QUANTITY	UNIT
RECHARGER 280SHD STARTER	8	PIECES
RECHARGER 280SHD INTERMEDIATE	126	PIECES
RECHARGER 280SHD END	8	PIECES
H.V.LV FC-24 FEED CONNECTORS	14	PIECES
CULTEC NO. 410 FILTER FABRIC 7.5' x 30'	5	ROLLS
CULTEC NO. 20L POLYETHYLENE LINER	145	SQUARE FEET
1 1/2 - 2 INCH DIAMETER BROKEN STONE	214	CUBIC YARDS
VOLUME OF EXCAVATION	108	CUBIC YARDS

**CULTEC RECHARGER® 280HD LEGEND**

- RECHARGER 280SHD STARTER
- RECHARGER 280SHD INTERMEDIATE
- RECHARGER 280SHD END
- H.V.LV FC-24 FEED CONNECTORS
- CULTEC NO. 20L POLYETHYLENE LINER

**CULTEC STORMWATER MANAGEMENT SYSTEM**  
**STORAGE REQUIRED: 10,000 c.f.**  
**STORAGE PROVIDED: 10,240 c.f.**  
*\*INSTALLED USING TYPICAL STONE REQUIREMENTS OF 6 INCHES ABOVE AND BELOW CHAMBERS AND A 1 FT. BORDER SURROUNDING*

NO.	REVISION	DATE



**BNE ENERGY, INC.**  
**29 SOUTH MAIN STREET**  
**TOWN CENTER SUITE 200**  
**WEST HARTFORD, CT 06107**

**DETAILS**  
**CULTEC DETENTION BEDS**

**WIND COLEBROOK SOUTH**  
**FLAGG HILL ROAD**

**CIVIL C1**

CORNERSTONE PROFESSIONAL PARK, SUITE D-101  
 43 SHERMAN HILL ROAD  
 WOODBURY, CONNECTICUT (203) 266-0778

DRWING NO.	C604
SCALE	N.T.S.
DATE	26 AUG 11
PROJ. NO.	3092
CHD FILE NAME	3092
DRWING NO.	C604

## **APPENDIX E CONSTRUCTION RECORDS**

During the construction of the project, a log should be kept that documents the specific activities, relative to this plan, that happen on the site. This should include when BMPs (controls) are installed and when construction of facilities is initiated.

**INSPECTOR CERTIFICATION**

Project:	Wind Colebrook South
Project Location:	29 Flagg Hill Road Colebrook, Connecticut
Contractor:	
Address:	
Phone:	
Fax:	

**CONSTRUCTION ACTIVITIES / EROSION & SEDIMENT CONTROLS INSTALLATION LOG**

Start Date	Completion Date	Construction Activity or E&SC Controls Installed	Operator



**APPENDIX F  
INSPECTION AND MAINTENANCE RECORDS**

**INSPECTOR CERTIFICATION**

Project:	Wind Colebrook South
Project Location:	29 Flagg Hill Road Colebrook, Connecticut
Contractor:	
Address:	
Phone:	
Fax:	

**CONSTRUCTION INSPECTION & MAINTENANCE LOG**

Date	Activity	Description	(1) Report No.
	% Inspection % Maintenance	By: _____	
	% Inspection % Maintenance	By: _____	
	% Inspection % Maintenance	By: _____	
	% Inspection % Maintenance	By: _____	
	% Inspection % Maintenance	By: _____	
	% Inspection % Maintenance	By: _____	
	% Inspection % Maintenance	By: _____	
	% Inspection % Maintenance	By: _____	
	% Inspection % Maintenance	By: _____	
	% Inspection % Maintenance	By: _____	

**CONSTRUCTION SITE INSPECTION REPORT**

General Information			
Project Name:	Wind Colebrook South		
Location:	29 Flagg Hill Road Colebrook, Connecticut		
CT DEP Tracking No.		(1) Report No.	
Date of Inspection:		Start / End Time:	
Inspector's Name(s):			
Inspector's Title(s):			
Inspector's Contact Information:			
Describe present phase of construction:			
Type of Inspection: <input type="checkbox"/> Regular <input type="checkbox"/> Pre-storm event <input type="checkbox"/> During storm event <input type="checkbox"/> Post-storm event			
Weather Information			
Has it rained since the last inspection? <input type="checkbox"/> Yes <input type="checkbox"/> No			
If yes, provide: Storm Start Date & Time:                      Storm Duration (hrs):                      Approximate Rainfall (in):			
Weather at time of this inspection?			
Discharge Information (A)			
Do you suspect that discharges may have occurred since the last inspection? <input type="checkbox"/> Yes <input type="checkbox"/> No			
Are there any discharges at the time of inspection? <input type="checkbox"/> Yes <input type="checkbox"/> No			
Describe location of any discharges from the site:			

**SITE-SPECIFIC BMPs**

(B)	BMP Description	BMP Installed and Operating Properly?	Corrective Action Needed	Date for corrective action / responsible party
1		%oYes %oNo		
2		%oYes %oNo		
3		%oYes %oNo		
4		%oYes %oNo		
5		%oYes %oNo		
6		%oYes %oNo		
7		%oYes %oNo		
8		%oYes %oNo		
9		%oYes %oNo		
10		%oYes %oNo		
11		%oYes %oNo		
12		%oYes %oNo		
13		%oYes %oNo		
14		%oYes %oNo		
15		%oYes %oNo		
16		%oYes %oNo		
17		%oYes %oNo		
18		%oYes %oNo		
19		%oYes %oNo		

**OVERALL SITE ISSUES**

(C)	BMP/activity	Implemented?	Maintained?	Corrective Action	Date for corrective action/responsible person
1	Are all slopes and disturbed areas not actively being worked properly stabilized?	% Yes % No	% Yes % No		
2	Are natural resource areas (e.g., streams, wetlands, mature trees, etc.) protected with barriers or similar BMPs?	% Yes % No	% Yes % No		
3	Are perimeter controls and sediment barriers adequately installed (keyed into substrate) and maintained?	% Yes % No	% Yes % No		
4	Are discharge points and receiving waters free of sediment deposits?	% Yes % No	% Yes % No		
5	Are storm drain inlets properly protected?	% Yes % No	% Yes % No		
6	Is there evidence of sediment being tracked into the street?	% Yes % No	% Yes % No		
7	Is trash/litter from work areas collected and placed in covered	% Yes % No	% Yes % No		

(C)	BMP/activity	Implemented?	Maintained?	Corrective Action	Date for corrective action/responsible person
	dumpsters?				
8	Are washout facilities (e.g., paint, stucco, concrete) available, clearly marked, and maintained?	% Yes % No	% Yes % No		
9	Are vehicle and equipment fueling, cleaning, and maintenance areas free of spills, leaks, or any other deleterious material?	% Yes % No	% Yes % No		
10	Are materials that are potential stormwater contaminants stored inside or under cover?	% Yes % No	% Yes % No		
11	Are non-stormwater discharges (e.g., wash water, dewatering) properly controlled?	% Yes % No	% Yes % No		
12	(Other)	% Yes % No	% Yes % No		

(C)	BMP/activity	Implemented?	Maintained?	Corrective Action	Date for corrective action/responsible person
13	(Other)	%Yes %No	%Yes %No		

**GENERAL INSPECTION COMMENTS AND EXPLANATION**

General Inspection Comments (D)
Is other descriptive information attached to this inspection report? %Yes %No

Plan Information (E)
Were all current plan BMP's in place at the time of inspection? %Yes %No
Are additional BMP's required? %Yes %No
Does the plan need to be updated? %Yes %No
Explanation of additional BMP and Plan update requirements:

Certification statement:

I certify that I have thoroughly and completely reviewed the Stormwater Pollution Control Plan for the site. I further certify, based on such review and in my professional judgment, that the Stormwater Pollution Control Plan has been prepared in accordance with the Connecticut Guidelines for Soil Erosion and Sediment Control, as amended, and the conditions for the General Permit for the Discharge of Stormwater and Dewatering Wastewaters from Construction Activities issued on October 1, 2002 (or as reissued or modified), and the controls required for such Plan are appropriate for the site. I am aware that there are significant penalties for false statements in this certification, including the possibility of fine and imprisonment for knowingly making false statements.

Name: \_\_\_\_\_

(Please print)

Signature: \_\_\_\_\_

Title: \_\_\_\_\_ Date: \_\_\_\_\_



**CONSTRUCTION SITE MAINTENANCE REPORT**

General Information			
Project Name:	Wind Colebrook South		
Location:	29 Flagg Hill Road Colebrook, Connecticut		
CT DEP Tracking No.:		(1) Report No.	
Date of Maintenance:		Start / End Time:	
Describe present phase of construction:			
Type of Maintenance:			
% Regular    % Pre-storm event    % Post-storm event    % Plan Update			
Maintenance Information			
Inspection Report Reference (No., Item)	Maintenance performed:		
Performed by:			
Inspection Report Reference (No., Item)	Maintenance performed:		
Performed by:			
Inspection Report Reference (No., Item)	Maintenance performed:		
Performed by:			
Inspection Report Reference (No., Item)	Maintenance performed:		
Performed by:			
Inspection Report Reference (No., Item)	Maintenance performed:		
Performed by:			

Inspection Report Reference (No., Item)	Maintenance performed:
Performed by:	
Inspection Report Reference (No., Item)	Maintenance performed:
Performed by:	
Inspection Report Reference (No., Item)	Maintenance performed:
Performed by:	
Inspection Report Reference (No., Item)	Maintenance performed:
Performed by:	
Inspection Report Reference (No., Item)	Maintenance performed:
Performed by:	
Inspection Report Reference (No., Item)	Maintenance performed:
Performed by:	
Inspection Report Reference (No., Item)	Maintenance performed:
Performed by:	
Inspection Report Reference (No., Item)	Maintenance performed:
Performed by:	

Certification statement:

I certify that I have thoroughly and completely reviewed the Stormwater Pollution Control Plan for the site. I further certify, based on such review and in my professional judgment, that the Stormwater Pollution Control Plan has been prepared in accordance with the Connecticut Guidelines for Soil Erosion and Sediment Control, as amended, and the conditions for the General Permit for the Discharge of Stormwater and Dewatering Wastewaters from Construction Activities issued on October 1, 2002 (or as reissued or modified), and the controls required for such Plan are appropriate for the site. I am aware that there are significant penalties for false statements in this certification, including the possibility of fine and imprisonment for knowingly making false statements.

Name: \_\_\_\_\_

Signature: \_\_\_\_\_

Title: \_\_\_\_\_ Date: \_\_\_\_\_

**APPENDIX G  
HAZARDOUS MATERIAL OR OIL SPILL RECORDS**

**HAZARDOUS SUBSTANCE/OIL SPILL DISCHARGE EVENT**

General Information			
Project Name:	Wind Colebrook South		
Location:	29 Flagg Hill Road Colebrook, Connecticut		
CT DEP Tracking No.:		(2) Discharge Report No.	
Date of Event:		Time of Event:	
Responsible Party:			
Substance Discharged:			
Description of Event			
Is other descriptive information attached to this inspection report?			
%oYes %oNo			
Control and Containment Measures Implemented			

Counter Measures Proposed
Does the SWPPP need to be updated? <input type="checkbox"/> Yes <input type="checkbox"/> No
Explanation of additional BMP and SWPPP update requirements:

**Certification statement:**

I certify that I have thoroughly and completely reviewed the Stormwater Pollution Control Plan for the site. I further certify, based on such review and in my professional judgment, that the Stormwater Pollution Control Plan has been prepared in accordance with the Connecticut Guidelines for Soil Erosion and Sediment Control, as amended, and the conditions for the General Permit for the Discharge of Stormwater and Dewatering Wastewaters from Construction Activities issued on October 1, 2002 (or as reissued or modified), and the controls required for such Plan are appropriate for the site. I am aware that there are significant penalties for false statements in this certification, including the possibility of fine and imprisonment for knowingly making false statements.

Name: \_\_\_\_\_

Signature: \_\_\_\_\_

Company: \_\_\_\_\_

Title: \_\_\_\_\_      Date: \_\_\_\_\_

**APPENDIX H  
UPDATE RECORDS**

**PLAN UPDATE DESCRIPTION**

General Information			
Project Name:	Wind Colebrook South		
Location:	29 Flagg Hill Road Colebrook, Connecticut		
CT DEP Tracking No.		Revision No.	
Section:		Date:	
Description of Revision			
Reason for Revision			
Revision Requested By:	‰ Inspection	‰ Maintenance	‰ Agency Inspection
‰ Other:			

**PLAN UPDATE LOG**

<b>Revision No.</b>	<b>Description -</b>		
<b>Section:</b>	<b>Date of Revision :</b>		
<b>By:</b>			
<b>Revision No.</b>	<b>Description -</b>		
<b>Section:</b>	<b>Date of Revision :</b>		
<b>By:</b>			



Revision No.	Description -
Section:	Date of Revision : <input style="width: 150px;" type="text"/>
By:	
Revision No.	Description -
Section:	Date of Revision : <input style="width: 150px;" type="text"/>
By:	
Revision No.	Description -
Section:	Date of Revision : <input style="width: 150px;" type="text"/>
By:	

**Certification statement:**

I certify that I have thoroughly and completely reviewed the Stormwater Pollution Control Plan for the site. I further certify, based on such review and in my professional judgment, that the Stormwater Pollution Control Plan has been prepared in accordance with the Connecticut Guidelines for Soil Erosion and Sediment Control, as amended, and the conditions for the General Permit for the Discharge of Stormwater and Dewatering Wastewaters from Construction Activities issued on October 1, 2002 (or as reissued or modified), and the controls required for such Plan are appropriate for the site. I am aware that there are significant penalties for false statements in this certification, including the possibility of fine and imprisonment for knowingly making false statements.

Name: \_\_\_\_\_

Signature: \_\_\_\_\_

Company: \_\_\_\_\_

Title: \_\_\_\_\_ Date: \_\_\_\_\_

**APPENDIX I  
CT DEP NOTICE OF TERMINATION (NOT)**



## General Permit for the Discharge of Stormwater and Dewatering Wastewaters from Construction Activities

### Notice of Termination Form

Please complete and submit this form in accordance with the general permit (DEP-PED-GP-015) in order to ensure the proper handling of your termination. Print or type unless otherwise noted.

Note: Ensure that for commercial and industrial facilities, registrations under the *General Permit for the Discharge of stormwater Associated with Industrial Activity* (DEP-PED-GP-014) or the *General Permit for the Discharge of stormwater from Commercial Activities* (DEP-PED-GP-004) have been filed where applicable. For questions about the applicability of these general permits, please call the Department at 860-424-3018.

#### Part 1: Registrant Information

1. Permit number: **GSN**
2. Fill in the name of the registrant(s) as indicated on the registration certificate:  
Registrant: \_\_\_\_\_
3. Site Address:  
City/Town: \_\_\_\_\_ State: \_\_\_\_\_ Zip Code: \_\_\_\_\_
4. Date all storm drainage structures were cleaned of construction sediment:  
Date of Completion of Construction: \_\_\_\_\_  
Date of Last Inspection (must be at least three months after final stabilization pursuant to Section 6(b)(6)(D) of the general permit) \_\_\_\_\_
5. Check the post-construction activities at the site (check all that apply):  
 Industrial  Residential  Commercial  Capped Landfill   
 Other(describe): \_\_\_\_\_

#### Part II: Certification

"I have personally examined and am familiar with the information submitted in this document and all attachments thereto, and I certify that, based on reasonable investigation, including my inquiry of those individuals responsible for obtaining the information, the submitted information is true, accurate and complete to the best of my knowledge and belief. I understand that a false statement made in this document or its attachments may be punishable as a criminal offense, in accordance with Section 22a-6 of the Connecticut General Statutes, pursuant to Section 53a-157b of the Connecticut General Statutes, and in accordance with any other applicable statute."

Signature of Permittee	Date
Name of Permittee (print or type)	Title (if applicable)

Note: Please submit this Notice of Termination Form to:  
 STORMWATER PERMIT COORDINATOR  
 BUREAU OF WATER MANAGEMENT  
 DEPARTMENT OF ENVIRONMENTAL PROTECTION  
 79 ELM STREET  
 HARTFORD, CT 06106-5127

**APPENDIX J**  
**CONNECTICUT GENERAL PERMIT FOR THE DISCHARGE OF STORMWATER AND**  
**DEWATERING WASTEWATERS ASSOCIATED WITH CONSTRUCTION ACTIVITIES**  
**(DEP-PED-GP-015)**
