




CTDOT Maintenance Resurfacing Program Bi-Monthly Update Tuesday, November 16th, 2021

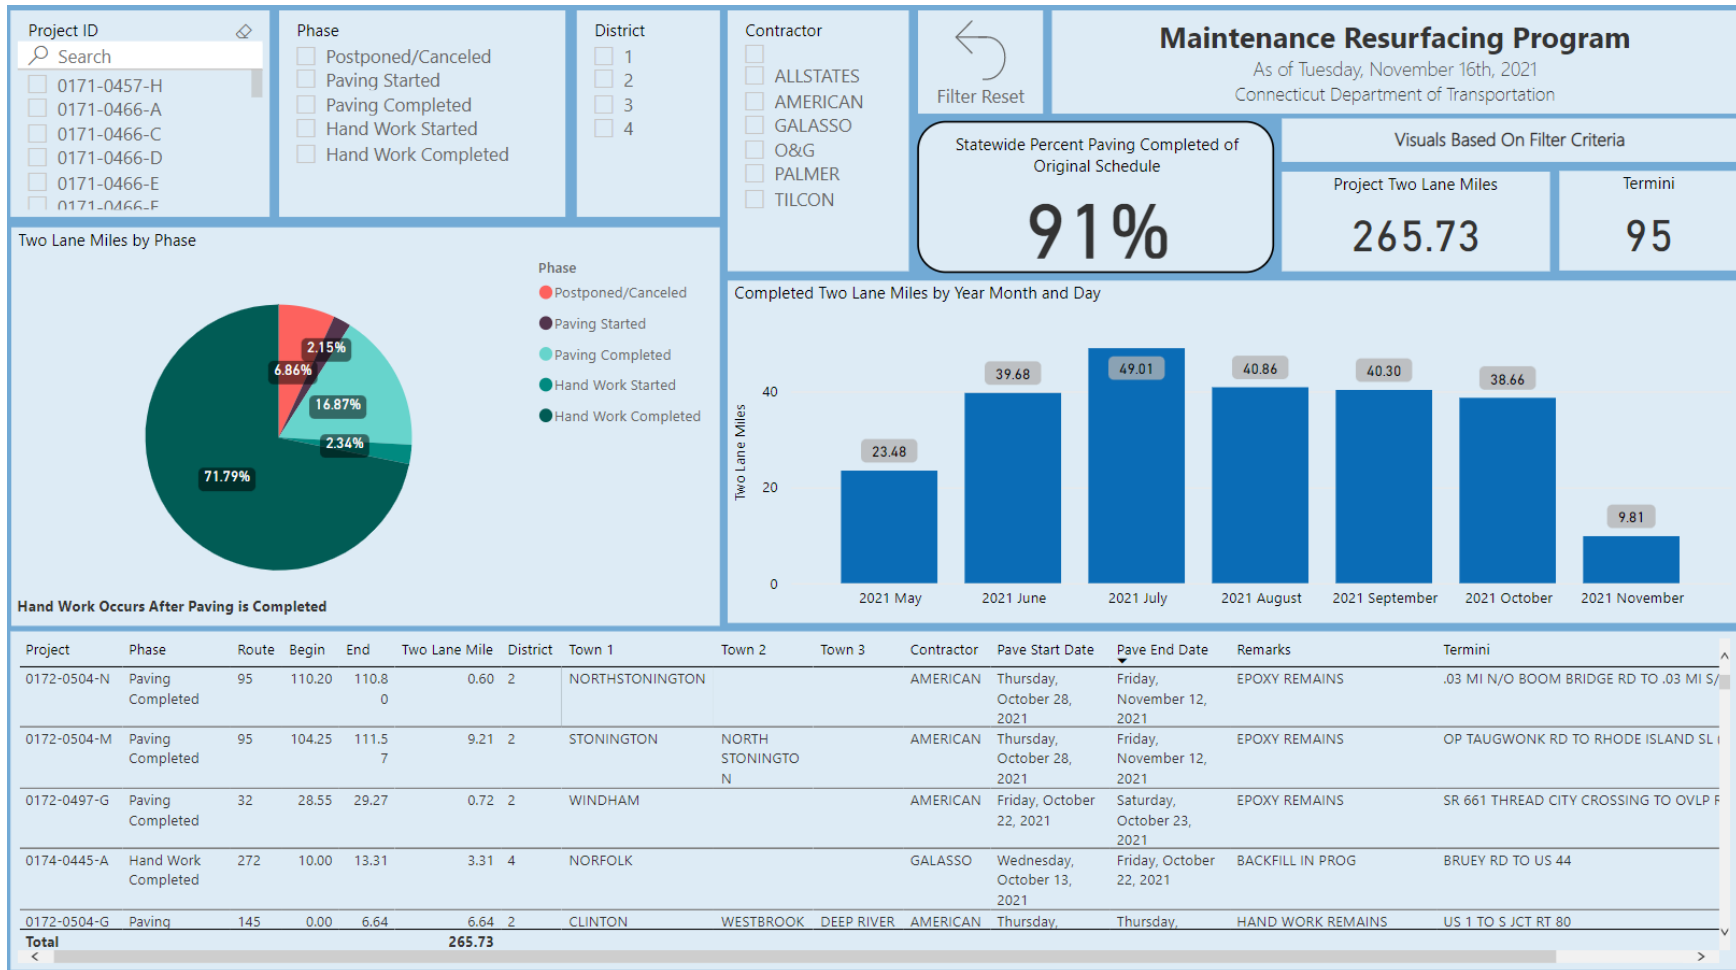

Please feel free to visit the CTDOT Maintenance Resurfacing Program PowerBI dashboard at the link below. Any feedback or enhancement requests are welcome and appreciated.

[Maintenance Resurfacing Program Dashboard](#)

Tuesday, November 16, 2021

2021 RESURFACING PROGRAM

DISTRICT 1

L/L	RTE	TOWN(S)	TERMINI DESCRIPTION	SCHD	COMP	CONTRACTOR	RESURFACING P.O.	PREP WORK	PRE CONST	MACHINE LAID	HAND WORK	INCID	REMARKS
SECTION 11			PROJECT 0171-0466										
A	19	N+S STAFFORD	RT 190 (EAST MAIN ST) TO HYDEVILLE RD	3.02	3.02	PALMER	232800	2/24/2021 4/22/2021	5/18/2021	6/14/2021 7/15/2021	7/20/2021 7/23/2021	7/26/2021 8/10/2021	FIELD REVIEW REMAINS
C	30	N+S ELLINGTON	TOLLAND TL TO RT 140 (CRYSTAL LAKE RD)	0.76	0.76	GALASSO	233289	3/19/2021 3/19/2021	4/20/2021	5/3/2021 5/6/2021	5/7/2021 5/7/2021	5/14/2021 8/9/2021	FIELD REVIEW REMAINS
D	44	E+W MANSFIELD	COVENTRY TL TO RT 195 (STORRS RD)	3.38	3.38	ALL STATES	233135	1/21/2021 6/23/2021	5/3/2021	6/16/2021 7/20/2021	7/23/2021 7/23/2021	7/27/2021 8/25/2021	FIELD REVIEW REMAINS
E	75	N+S WINDSOR WINDSOR LOCKS	.17 MI S/O BGN OP RT 20 TO RT 140 (ELM ST)	2.72	2.72	GALASSO	233291	3/30/2021 5/7/2021	5/21/2021	6/27/2021 7/15/2021		7/28/2021 8/11/2021	FIELD REVIEW REMAINS
F	140	E+W EAST WINDSOR ELLINGTON	SB RT 191 (MAIN ST) TO CON FR RT 286 (ONE WAY)	5.51	5.51	GALASSO	233292	1/11/2021 5/20/2021	4/30/2021	6/1/2021 6/16/2021	6/22/2021 6/23/2021	8/2/2021 8/18/2021	FIELD REVIEW REMAINS
G	140	E+W WINDSOR LOCKS	RT 75 (ELLA GRASSO TPKE) TO RT 159 (SOUTH MAIN ST)	2.35	2.35	GALASSO	233293	4/1/2021 8/31/2021	9/1/2021	9/27/2021 10/5/2021	10/18/2021 10/21/2021	10/31/2021 11/4/2021	FIELD REVIEW REMAINS
H	187	N+S BLOOMFIELD	HARTFORD TL TO RT 218 (COTTAGE GROVE RD)	1.23	1.23	AMERICAN	234181	3/31/2021 6/22/2021	7/7/2021	7/26/2021 7/28/2021	8/3/2021 8/3/2021	8/12/2021 8/29/2021	FIELD REVIEW REMAINS
I	500	N+S EAST HARTFORD	.01 MI NO UP WB I-84 ACC RMP(TR827)TO NB GOVERNOR ST	0.84									CANCELLED
J	502	E+W EAST HARTFORD	FORBES ST TO MANCHESTER TL	1.52	1.52	AMERICAN	234183	3/25/2021 6/10/2021	6/3/2021	7/7/2021 7/16/2021	7/23/2021 7/23/2021	7/26/2021 8/29/2021	FIELD REVIEW REMAINS
K	510	N+S EAST WINDSOR ENFIELD	US 5 (SOUTH MAIN ST) TO US 5 (KING ST)	2.61	2.61	GALASSO	233294	1/13/2021 7/29/2021	8/19/2021	9/14/2021 9/23/2021	9/28/2021 9/30/2021	10/6/2021 11/10/2021	FIELD REVIEW REMAINS
L	44	E+W EAST HARTFORD	SR 907 TO BGN OVLP US 5	1.68	1.68	AMERICAN	234184	3/24/2021 5/10/2021	7/28/2021	9/12/2021 9/16/2021	10/29/2021 10/29/2021	10/7/2021 10/17/2021	FIELD REVIEW REMAINS
SECTION 13			PROJECT 0171-0457										
H	84	WB EAST HARTFORD	WB ACC FR SR 518 (ROBERTS ST) TO X56 NB SR 500 INC RAMP	2.24	2.24	AMERICAN	233306	6/17/2020 5/19/2021	4/28/2021	5/23/2021 6/18/2021			EPOXY REMAINS
SECTION 13			PROJECT 0171-0467										
A	3	N+S MIDDLETOWN CROMWELL	RT 66 (WASHINGTON ST) TO RT 372 (WEST ST)	3.98	3.98	TILCON	232653	4/19/2021 8/1/2021	6/30/2021	8/8/2021 8/24/2021	9/11/2021 9/13/2021	9/12/2021 10/11/2021	FIELD REVIEW REMAINS
C	10	N+S SOUTHTON PLAINVILLE	.01 MI SO QUINN RV TO .04 MI NO RT 372 (EAST MAIN ST)	2.55	2.55	TILCON	232759	4/5/2021 8/9/2021	7/26/2021	8/10/2021 8/17/2021	9/7/2021 9/10/2021	9/17/2021 9/21/2021	FIELD REVIEW REMAINS
D	15	N+S BERLIN	MERIDEN TL TO .13 MI SO MIDDLETOWN RD	6.19	6.19	TILCON	232760	4/12/2021 7/21/2021	6/28/2021	7/18/2021 8/9/2021	8/18/2021 8/27/2021	9/14/2021 10/1/2021	FIELD REVIEW REMAINS
E	42	E+W CHESHIRE	SOUTH BROOKSVALE RD TO RT 10	1.84	1.84	O&G	232743	2/24/2021 3/30/2021	4/15/2021	4/30/2021 5/7/2021	5/12/2021 5/18/2021	6/2/2021 7/22/2021	FIELD REVIEW REMAINS
F	69	N+S WOLCOTT	OP MAD RIVER TO .02 MI SO NORTH ST	3.03	3.03	AMERICAN	233307	3/22/2021 4/29/2021	4/20/2021	5/3/2021 5/14/2021	5/17/2021 5/19/2021	6/21/2021 7/22/2021	FIELD REVIEW REMAINS
G	70	E+W MERIDEN	MAIN ST TO NEW HANOVER ST	0.52	0.52	TILCON	232762	3/9/2021 5/27/2021	5/19/2021	6/4/2021 6/6/2021		7/16/2021 7/22/2021	FIELD REVIEW REMAINS
H	71A	N+S NEW BRITAIN	SR571 (WB) TO BUELL ST	0.52	0.52	TILCON	262761	3/22/2021 4/30/2021	4/21/2021	5/3/2021 5/6/2021	5/7/2021 5/7/2021	5/10/2021 6/27/2021	FIELD REVIEW REMAINS
I	84	E/B NEW BRITAIN	.01 MI EO WB RMP TR 815 TO .03 MI WO ACC FR NB RT 72	1.25	1.25	TILCON	232759	3/22/2021 4/6/2021	5/5/2021	5/24/2021 5/27/2021			EPOXY REMAINS

Tuesday, November 16, 2021

2021 RESURFACING PROGRAM

DISTRICT 1

L/L	RTE	TOWN(S)	TERMINI DESCRIPTION	SCHD	COMP	CONTRACTOR	RESURFACING P.O.	PREP WORK	PRE CONST	MACHINE LAID	HAND WORK	INCID	REMARKS	
J	84	W/B	PLAINVILLE NEW BRITAIN		1.19	1.19	TILCON	232758	3/22/2021 4/6/2021	5/5/2021	6/2/2021 6/4/2021		EPOXY REMAINS	
K	91	N/B	HARTFORD		1.37								PPD TO 2022	
L	173	N+S	NEWINGTON		1.78	1.78	GALASSO	233290	3/29/2021 7/1/2021	6/22/2021	7/6/2021 7/15/2021	7/19/2021 7/19/2021	7/20/2021 8/26/2021	FIELD REVIEW REMAINS
M	217	N+S	MIDDLEFIELD MIDDLETOWN		4.08	4.08	AMERICAN	234180	3/1/2021 4/30/2021	4/29/2021	5/24/2021 6/8/2021	6/14/2021 6/16/2021	6/26/2021 7/26/2021	FIELD REVIEW REMAINS
N	322	E+W	CROMWELL WOLCOTT		2.72	2.72	AMERICAN TILCON	234182	3/9/2021 9/3/2021	8/23/2021	9/14/2021 9/23/2021	10/8/2021 10/12/2021	10/11/2021 11/2/2021	FIELD REVIEW REMAINS
DISTRICT 1 TOTAL =====>					58.88	56.67								

Tuesday, November 16, 2021

2021 RESURFACING PROGRAM

DISTRICT 2

L/L	RTE	TOWN(S)	TERMINI DESCRIPTION	SCHD	COMP	CONTRACTOR	RESURFACING P.O.	PREP WORK	PRE CONST	MACHINE LAID	HAND WORK	INCID	REMARKS
SECTION 21				PROJECT 0172-0497									
G	32	N+S WINDHAM	SR 661 THREAD CITY CROSSING TO OVLP RT66	0.72	0.72	AMERICAN	239092		9/21/2021	10/22/2021 10/23/2021			EPOXY REMAINS
SECTION 21				PROJECT 0172-0503									
A	14	E+W PLAINFIELD	W JCT RT 14A TO RT 12	3.53	3.53	AMERICAN	238919	4/6/2021 9/21/2021	8/16/2021	9/22/2021 10/2/2021	10/15/2021		HANDWORK IN PROG
C	169	N+S POMFRET	RT 101 TO RT 171	5.46	5.46	ALL STATES	236747	3/11/2021 8/24/2021	7/22/2021	9/9/2021 9/23/2021	9/29/2021 10/15/2021	10/18/2021	EPOXY REMAINS
D	195	N+S MANSFIELD	RT 275 TO US 44	2.28	2.28	AMERICAN	235060	3/26/2021 6/3/2021	4/23/2021	6/6/2021 6/11/2021	6/15/2021 6/17/2021	6/6/2021	EPOXY REMAINS
E	607	N+S KILLINGLY	RT 12 TO SOUTH FRONTAGE RD	2.54	2.54	ALL STATES	235019	3/16/2021 5/28/2021	4/28/2021	6/2/2021 6/10/2021	6/28/2021 7/6/2021	6/7/2021	EPOXY REMAINS
F	196	E+W HADDAM	RT 151 TO RT 66	5.38	5.38	ALL STATES	235249	3/29/2021 6/18/2021	5/5/2021	6/18/2021 7/6/2021	7/13/2021 7/28/2021	6/14/2021	EPOXY REMAINS
G	12	E+W THOMPSON	EX FR NB I-395 TO .03 MI SO RT 131	3.07	3.07	AMERICAN	235247	5/26/2021 8/5/2021	4/23/2021	8/11/2021 8/14/2021	9/8/2021 9/11/2021	7/22/2021	EPOXY REMAINS
H	275	N+S MANSFIELD	RT 32 TO RT 195	2.14	2.14	ALL STATES	234693	3/9/2021 7/19/2021	4/28/2021	7/30/2021 8/3/2021	8/12/2021 8/24/2021	7/21/2021	EPOXY REMAINS
I	354	E+W COLCHESTER SALEM	STANAVAGE RD TO RT 82	4.34	4.34	AMERICAN	235248	4/5/2021 8/2/2021	4/23/2021	8/2/2001 8/10/2021	8/26/2021 9/10/2021	9/21/2021	EPOXY REMAINS
SECTION 23				PROJECT 0172-0504									
A	163	N+S BOZRAH	.04 MI NO CAROLINE RD TO BOZRAH ST EXT	1.70	1.70	AMERICAN	234187	3/22/2021 4/23/2021	4/16/2021	5/11/2021 5/13/2021	5/14/2021 5/14/2021	5/17/2021	EPOXY REMAINS
C	612	E+W BOZRAH	RT 163 TO SR 608	0.14	0.14	AMERICAN	234187	3/22/2021 4/23/2021	4/16/2021	5/11/2021 5/13/2021	5/14/2021 5/14/2021	5/17/2021	EPOXY REMAINS
D	602	E+W ESSEX	RT 154 TO RT 80	3.28									PPD DUE TO CONST CONFLICT
E	138	E+W DEEP RIVER SPRAGUE	RT 97 TO LISBON TL	2.59									PPD DUE TO UTILITY CONFLICT
F	2A	E+W MONTVILLE	BGN OP I-395 TO RT 12 (INC RMPS)	6.02	6.02	AMERICAN	236607	3/25/2021 8/12/2021	7/1/2021	8/16/2021 9/17/2021	9/27/2021 10/1/2021	7/27/2021	EPOXY REMAINS
G	145	N+S PRESTON	US 1 TO S JCT RT 80	6.64	6.64	AMERICAN	237433	3/30/2021 8/16/2021	8/19/2021	10/7/2021 10/21/2021		9/2/2021	HAND WORK REMAINS
H	625	N+S WESTBROOK	US 1 TO RT 145	0.99	0.99	AMERICAN	237433	3/30/2021 8/16/2021	8/19/2021	10/7/2021 10/21/2021		9/8/2021	HAND WORK REMAINS
I	201	N+S GRISWOLD	NO STONINGTON TL TO RT 165	2.78	2.78	AMERICAN	234186	3/10/2021 4/30/2021	4/16/2021	5/17/2021 5/20/2021	5/21/2021 5/21/2021	5/24/2021	EPOXY REMAINS
J	81	N+S HADDAM	KILLINGWORTH TL TO RT 154 (SAYBROOK RD)	5.70		AMERICAN	238386	5/27/2021 10/13/2021	9/9/2021	11/15/2021		10/20/2021	PAVE IN PROG
K	138	E+W GRISWOLD	RT 12 (MAIN ST) TO ACC TO NB I-395	1.11	1.11	AMERICAN	235250	3/17/2021 6/15/2021	5/19/2021	7/21/2021 7/22/2021	7/23/2021 7/23/2021	7/8/2021	EPOXY REMAINS
L	1A	N+S STONINGTON	US 1 TO TRUMBULL AVE	0.65	0.65	AMERICAN	234185	3/17/2021 4/28/2021	4/16/2021	5/3/2021 5/6/2021	5/21/2021 5/21/2021	5/21/2021	EPOXY REMAINS
M	95	N/B STONINGTON NORTH STONINGTON	OP TAUGWONK RD TO RHODE ISLAND SL (INC RMPS)	9.21	9.21	AMERICAN	239846	9/14/2021 10/11/2021	9/21/2021	10/28/2021 11/12/2021			EPOXY REMAINS

Tuesday, November 16, 2021

2021 RESURFACING PROGRAM

DISTRICT 3

L/L	RTE	TOWN(S)	TERMINI DESCRIPTION	SCHD	COMP	CONTRACTOR	RESURFACING P.O.	PREP WORK	PRE CONST	MACHINE LAID	HAND WORK	INCID	REMARKS	
SECTION 31			PROJECT 0173-0508											
J	15	N/B	HAMDEN NORTH HAVEN	.17 MI NO END OP CONNOLLY PKWY TO WLFD TL	5.91	5.91	TILCON	235580	7/12/2021 8/11/2021	6/22/2021	8/10/2021 9/13/2021	9/20/2021	EPOXY REMAINS	
SECTION 31			PROJECT 0173-0514											
A	10	N+S	CHESHIRE	.10 MI NO KINGS RD TO RT 42 (EB) (NO BROOKSVALE RD)	0.77	0.77	TILCON	233952	3/17/2021 4/22/2021	4/21/2021	5/7/2021 5/11/2021	5/14/2021 5/14/2021	6/14/2021 6/29/2021	FIELD REVIEW REMAINS
C	454	E+W	SHELTON	RT 110 (HOWE AVE) TO BIRCHBANK RD #1	1.89	1.89	O&G	234162	5/11/2021 5/18/2021	5/4/2021	5/23/2021 5/28/2021	5/28/2021 5/28/2021	6/17/2021 6/17/2021	FIELD REVIEW REMAINS
D	34	E+W	ORANGE WEST HAVEN	RT 121 (GRASSY HILL RD) (SB) TO .13 MI WO RT 122	9.69	9.69	TILCON	233954	3/29/2021 5/27/2021	4/27/2021	6/1/2021 7/16/2021	9/3/2021 9/27/2021	8/9/2021	BACKFILL REMAINS
E	720	E+W	NORTH HAVEN	HARTFORD TPKE #1 TO US 5 (STATE ST)	0.52	0.52	TILCON	234458	4/1/2021 6/1/2021	5/18/2021	6/9/2021 6/12/2021	6/23/2021 6/23/2021	7/12/2021	EPOXY IN PROG
F	1	N+S	MADISON	GUILFORD TL TO RT 79 (DURHAM RD)	2.88	2.88	TILCON	233956	4/9/2021 5/17/2021	5/20/2021	6/28/2021 7/20/2021	7/22/2021 7/26/2021	7/20/2021	BACKFILL REMAINS
G	77	N+S	GUILFORD	RT 80 (KILLINGWORTH RD) TO .20 MI NO ELM ST CON	0.70	0.70	AMERICAN	235330	4/8/2021 6/3/2021	6/1/2021	6/29/2021 7/8/2021	10/27/2021 10/27/2021	7/8/2021	EPOXY REMAINS
H	63	N+S	WOODBIDGE	NEW HAVEN TL TO .87 MI NO RT 114	3.11	3.11	TILCON	235326	6/1/2021 6/15/2021	6/3/2021	7/7/2021 7/22/2021	9/29/2021 9/30/2021	8/17/2021	EPOXY REMAINS
I	749	N+S	WOODBIDGE	RT 63 (AMITY RD) TO RT 69 (LITCHFIELD TPKE)	0.23	0.23	TILCON	235326	6/1/2021 6/15/2021	6/3/2021	7/9/2021 7/14/2021	9/30/2021 9/30/2021	8/17/2021	EPOXY REMAINS
J	705	N+S	WEST HAVEN	RT 162 (JONES HILL RD) TO RT 162 (PLATT AVE)	2.63	2.63	TILCON	235372	4/27/2021 7/15/2021	6/10/2021	7/25/2021 8/10/2021	8/30/2021 8/31/2021	10/13/2021	EPOXY REMAINS
K	80	N+S	EAST HAVEN	.73 MI EO NEW HAVEN TL TO NORTH BRANFORD TL	2.35									PPD UNTIL 2022
L	146	E+W	GUILFORD	SACHEMS HEAD RD TO US 1 (BOSTON POST RD)	2.65									PPD UNTIL 2022
SECTION 33			PROJECT 0173-0499											
J	25	N+S	TRUMBULL	.37 MI SO RT 111 TO RT 111	0.84	0.84	O&G	235328	3/17/2021 5/4/2021	6/8/2021	7/25/2021 7/29/2021		8/27/2021	EPOXY REMAINS
SECTION 33			PROJECT 0173-0515											
A	137	N+S	STAMFORD	US 1 (SB)(TRESSR BLVD) TO HIGH RIDGE RD #1	4.23	4.23	O&G	235327	3/5/2021 5/4/2021	5/25/2021	6/23/2021 7/24/2021		8/13/2021	EPOXY REMAINS
C	130	E+W	FAIRFIELD BRIDGEPORT	EB-US 1 NB TO UP I-95 (GOV JOHN D LODGE TPKE)	3.91	3.91	O&G	235492	3/16/2021 7/17/2021	6/15/2021	7/30/2021 8/21/2021		8/30/2021	WATERBORNE IN PROG
D	137	N+S	STAMFORD	HIGH RIDGE RD #1 TO ACC TO SB RT 15	6.51	6.51	O&G	235546	3/22/2021 4/30/2021	6/17/2021	8/24/2021 10/1/2021	10/18/2021 10/18/2021		WATERBORNE REMAINS
E	111	N+S	TRUMBULL MONROE	.01 MI NO RT 25 (MAIN ST) TO .12 MI NO PURDY HILL RD	2.81	2.81	O&G	234340	3/24/2021 5/11/2021	5/6/2021	6/13/2021 6/23/2021	7/12/2021 7/12/2021	7/13/2021 8/5/2021	FIELD REVIEW REMAINS
F	59	N+S	FAIRFIELD	CORNELL RD TO .05 MI SO BGN RT 15	2.41	2.41	O&G	235600	8/31/2021 9/12/2021	8/5/2021	10/1/2021 10/20/2021	10/27/2021		HANDWORK IN PROG

Tuesday, November 16, 2021

2021 RESURFACING PROGRAM

DISTRICT 3

L/L	RTE	TOWN(S)	TERMINI DESCRIPTION	SCHD	COMP	CONTRACTOR	RESURFACING P.O.	PREP WORK	PRE CONST	MACHINE LAID	HAND WORK	INCID	REMARKS	
G	713	N+S	FAIRFIELD		0.27	0.27	O&G	235600	4/13/2021 8/16/2021	8/5/2021	10/8/2021 10/20/2021	10/27/2021	HANDWORK IN PROG	
H	130	E+W	STRATFORD		1.52	1.52	TILCON	235491	3/25/2021 8/31/2021	8/3/2021	8/31/2021 9/13/2021	10/1/2021 10/1/2021	9/14/2021 WATERBORNE IN PROG	
I	127	N+S	BRIDGEPORT		2.43								PPD UNTIL 2022	
J	136	E+W	NORWALK		1.86								PPD UNTIL 2022	
K	809	N+S	NORWALK		0.86								PPD UNTIL 2022	
L	137	N+S	STAMFORD		3.82	3.82	O&G	234161	4/9/2021 4/30/2021	4/29/2021	5/25/2021 6/11/2021	7/6/2021 7/12/2021	7/18/2021 7/21/2021	FIELD REVIEW REMAINS
DISTRICT 3 TOTAL =====>					64.80	54.65								

Tuesday, November 16, 2021

2021 RESURFACING PROGRAM

DISTRICT 4

L/L	RTE	TOWN(S)	TERMINI DESCRIPTION	SCHD	COMP	CONTRACTOR	RESURFACING P.O.	PREP WORK	PRE CONST	MACHINE LAID	HAND WORK	INCID	REMARKS
SECTION 41			PROJECT	0174-0439									
I	4	E+W SHARON	E JCT OLD SHARON RD #1 TO W JCT US 7	3.86	3.86	O&G	238226	9/22/2021 9/27/2021	9/15/2021	9/27/2021 10/1/2021			LEVELING FOR 2022 OVERLAY
SECTION 41			PROJECT	0174-0445									
A	272	E+W NORFOLK	BRUEY RD TO US 44	3.31	3.31	GALASSO	234233	3/23/2021 10/14/2021	9/30/2021	10/13/2021 10/22/2021	10/23/2021 10/28/2021	11/4/2021	BACKFILL IN PROG
C	43	N+S CORNWALL	RT 4 TO RT 63	5.16	5.16	O&G	233719	3/18/2021 7/30/2021	7/21/2021	8/10/2021 8/20/2021	9/10/2021 9/11/2021	8/26/2021	BACKFILL IN PROG
D	20	E+W WINCHESTER BARKHAMSTED	RT 8 TO HARTLAND TL	2.64	2.64	GALASSO	234229	3/10/2021 6/17/2021	5/27/2021	6/17/2021 6/25/2021	6/29/2021 7/2/2021	7/6/2021	EPOXY REMAINS
E	202	E+W TORRINGTON	.06 MI WO WALNUT ST TO FERN DR	2.56	2.56	O&G	233721	7/6/2021 9/15/2021	8/18/2021	9/16/2021 9/22/2021	9/24/2021 10/8/2021	10/5/2021	WATERBORNE REMAINS
F	254	E+W LITCHFIELD	THOMASTON TL TO RT 118	5.26	5.26	O&G	233720	3/17/2021 8/13/2021	7/21/2021	8/24/2021 9/13/2021	9/16/2021 9/27/2021	10/5/2021	WATERBORNE REMAINS
G	45	N+S WASHINGTON WARREN	US 202 TO .26 MI NO N JCT RT 341	5.67	5.67	O&G	233722	3/10/2021 6/10/2021	4/29/2021	6/11/2021 6/30/2021	7/1/2021 8/4/2021	9/13/2021	WATERBORNE REMAINS
H	540	E+W EAST GRANBY	RT 189 TO RT 187	1.44	1.44	GALASSO	234231	3/24/2021 5/7/2021	4/29/2021	5/10/2021 5/12/2021	5/13/2021 5/14/2021	5/17/2021	EPOXY REMAINS
I	318	E+W BARKHAMSTED	US 44 TO RT 181	1.47	1.47	GALASSO	234230	3/9/2021 5/3/2021	4/29/2021	5/17/2021 5/20/2021	5/21/2021 5/21/2021	6/17/2021	EPOXY REMAINS
J	219	N+S NEW HARTFORD	US 44 TO OP E BRANCH FARMINGTON RV	1.14	1.14	GALASSO	234232	3/1/2021 5/7/2021	4/29/2021	5/24/2021 5/26/2021	6/1/2021 6/1/2021	6/16/2021	EPOXY REMAINS
SECTION 43			PROJECT	0174-0440									
Q	847	N+S NAUGATUCK	ACC TO SB RT 8 TO WATERBURY TL	0.54	0.54	TILCON	239277	9/23/2021 9/28/2021	9/23/2021	10/1/2021 10/1/2021	10/13/2021 10/13/2021	10/18/2021	EPOXY REMAINS
SECTION 43			PROJECT	0174-0446									
A	69	N+S WATERBURY	WASHINGTON ST TO FROST RD	2.37	2.37	TILCON	233715	2/24/2021 8/18/2021	6/29/2021	8/30/2021 9/12/2021	10/6/2021 10/7/2021	10/27/2021	EPOXY REMAINS
C	69	N+S WATERBURY	PROSPECT TL TO OP I-84 EB ON RMP	2.84	2.84	TILCON	233716	2/24/2021 8/6/2021	6/29/2021	8/24/2021 8/30/2021	10/5/2021 10/5/2021	10/20/2021	EPOXY REMAINS
D	172	E+W SOUTHBURY	EX FR I-84 EB TO SPRUCE BROOK RD	4.05	4.05	O&G	234155	3/16/2021 7/14/2021	7/7/2021	7/26/2021 8/9/2021	8/16/2021 8/31/2021	8/19/2021	EPOXY REMAINS
E	133	N+S BROOKFIELD	RT 25 TO BGN OP HOUSATONIC RV	2.31	2.31	O&G	234156	3/31/2021 5/12/2021	4/30/2021	6/1/2021 6/10/2021	6/11/2021 7/16/2021	10/13/2021	BACKFILL IN PROG
F	7	N+S NEW MILFORD	.70 MI NO OP BULLYMUCK BK TO .49 MI SO OP POND OUTLET	3.55	3.55	TILCON	233717	4/1/2021 5/25/2021	5/26/2021	6/20/2021 6/29/2021	6/13/2021 6/13/2021		BACKFILL REMAINS
G	69	N+S PROSPECT	BETHANY TL TO RT 68 (UNION CITY RD)	2.68	2.68	O&G	234157	3/17/2021 7/7/2021	6/10/2021	7/16/2021 7/23/2021	7/26/2021 7/29/2021	8/3/2021	EPOXY REMAINS
H	67	N+S SEYMOUR	OXFORD TL (MOUNTAIN RD) TO SR 721	2.75	2.75	O&G	234159	4/9/2021 5/8/2021	4/30/2021	5/16/2021 5/20/2021	5/21/2021 5/25/2021	5/28/2021	EPOXY REMAINS
I	313	N+S WOODBRIDGE	SEYMOUR TL TO RT 114 (RACEBROOK RD)	1.35	1.35	O&G	234158	2/17/2021 5/6/2021	4/30/2021	5/12/2021 5/14/2021	5/17/2021 5/24/2021	6/1/2021	EPOXY REMAINS

Tuesday, November 16, 2021

2021 RESURFACING PROGRAM

DISTRICT 4

L/L	RTE	TOWN(S)	TERMINI DESCRIPTION	SCHD	COMP	CONTRACTOR	RESURFACING P.O.	PREP WORK	PRE CONST	MACHINE LAID	HAND WORK	INCID	REMARKS	
J	102	E+W	RIDGEFIELD	RT 35 (MAIN ST) TO BLOOMER RD	1.87	1.87	O&G	234160	2/17/2021 7/1/2021	6/10/2021	7/6/2021 7/8/2021	8/10/2021 8/13/2021	9/7/2021	EPOXY REMAINS
K	6	E+W	BRISTOL	SHERMAN ST TO COLLINS RD	3.70	3.70	AMERICAN	234188	3/15/2021 9/7/2021	8/4/2021	9/13/2021 9/20/2021	9/28/2021 10/5/2021	10/15/2021	EPOXY REMAINS
L	58	E+W	REDDING	SOUTH LA TO RT 107 (PUTNAM PARK RD)	2.64	2.64	TILCON	233718	3/30/2021 7/22/2021	6/29/2021	7/22/2021 7/27/2021	8/5/2021 8/9/2021	9/20/2021	EPOXY REMAINS
M	6	E+W	PLYMOUTH	RTE. 72 (SOUTH RIVERSIDE AVE) TO BRISTOL TL	0.49	0.49	O&G	235724	8/27/2021 9/9/2021	8/18/2021	9/14/2021 9/14/2021	9/17/2021 9/17/2021		BACKFILL REMAINS
N	84	E+W	DANBURY BETHEL BROOKFIELD NEWTOWN	.01 MI W/O ACC FR WB US 6 TO .01 MI E/O EB EX TO RT 25	7.53	7.53	TILCON	236860	7/12/2021 8/23/2021	8/4/2021	9/13/2021 10/15/2021	9/27/2021 9/27/2021	11/2/2021	BACKFILL IN PROG

DISTRICT 4 TOTAL =====> 71.18 71.18

DISTRICT TOTALS

DISTRICT I =====> 58.88 56.67

DISTRICT II =====> 70.87 59.3

DISTRICT III =====> 64.8 54.65

DISTRICT IV =====> 71.18 71.18

STATEWIDE VIP TOTAL =====> 265.73 241.80
