

---

**From:** Aja Chase <aja.chase@ericsson.com>  
**Sent:** Tuesday, February 20, 2024 10:31 AM  
**To:** CSC-DL Siting Council  
**Subject:** EM-AT&T-158-220728  
**Attachments:** 310968\_FCCA\_20240219.pdf; CTL02107 Alpha Overall Sector from Ground.jpg

Good Morning CSC,

Please find the attached FCCA letter and overall photo or work completed on the below site. Please advise if you need anything else, thank you!

10034981	CTL02107	MRCTB056357	180A BAYBERRY LANE	WESTPORT	06880
----------	----------	-------------	--------------------	----------	-------

Kindly,

Aja

February 19, 2024

**VIA E-Mail**

Michael Jackson  
Ramapo Communication Corp  
20 Romanelli Ave  
South Hackensack, NJ 07606

Re: 310968 – WSPT-WESTPORT REBUILD CT  
180A Bayberry Lane  
Westport, CT 06880  
Fairfield County  
Permit #: ZN-22-00772  
Colliers Engineering & Design, Architecture, Landscape Architecture, Surveying, CT P.C.  
Project No. 22904228

Dear Mr. Jackson,

For the above referenced site, AT&T has proposed installation of twelve (12) new antennas, nine (9) new radios, and two (2) new squids at an AGL of 98'-0", 100'-0", and 102'-0". Additionally, four (4) DC trunks, two (2) fiber trunks, and (3) Y cables are proposed to be installed on the tower.

Colliers Engineering & Design, Inc. has based their review on the following documents in completing this report:

- As-Built photographs provided by Ramapo Communications Corp dated September 20, 2023
- Construction Drawings provided by Colliers Engineering & Design dated December 6, 2022

Colliers Engineering & Design has been provided with As-Built photographs by Ramapo Communications Corp dated September 20, 2023. The As-Built photographs, which are included, accurately depict the final installation of the proposed AT&T equipment. Based upon the inspection of the As-Built photographs, it is the professional opinion of Colliers Engineering & Design that all work has been completed and is in compliance with all applicable codes and standards and the approved Construction Drawings.



Engineering  
& Design

310968 - WSPT-WESTPORT REBUILD CT

CED Project #: 22904228

February 19, 2024


Page 2 of 8

This evaluation of the As-Built condition is based solely on the provided As-Built photographs. Any equipment that has been installed after the As-Built photographs were taken is not part of this evaluation. Further, any equipment that has been installed, but was not captured in the provided As-Built photographs, is not part of this evaluation. Colliers Engineering & Design reserves the right to amend this evaluation if more information is provided.

If you have any questions or comments, or require additional information, please do not hesitate to contact me.

Very truly yours,

COLLIERS ENGINEERING & DESIGN, ARCHITECTURE, LANDSCAPE ARCHITECTURE,  
SURVEYING, CT P.C.



Dejian Xu, PE  
Technical Manager



**Photo - 1: Installation of Antennas and Equipment on Alpha Sector**



Sep 20, 2023 at 7:17:22 PM  
180 Bayberry Ln  
Westport CT 06880  
CTL02107


**Photo - 2: Installation of Antennas and Equipment on Beta Sector**



**Photo - 3: Installation of Antennas and Equipment on Gamma Sector**



**Photo - 4: Installation of Antennas and Equipment on Alpha Sector (From Ground)**

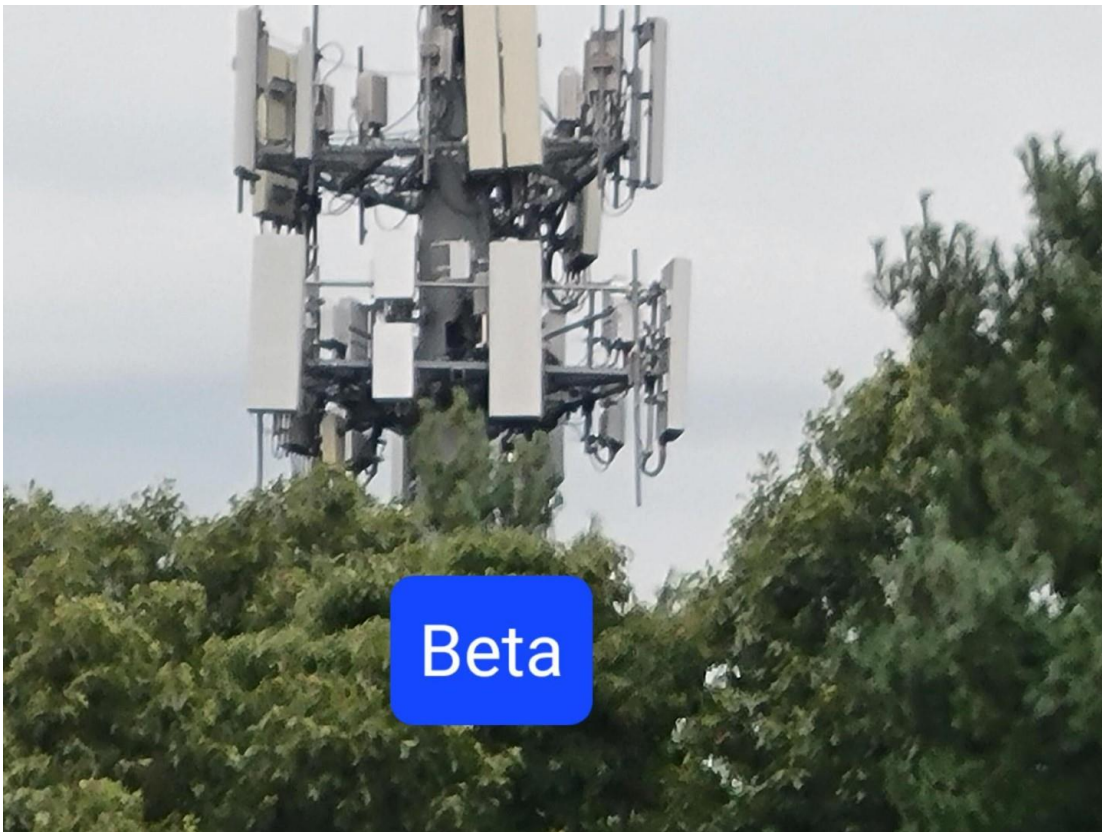

**Photo - 5: Installation of Antennas and Equipment on Beta Sector (From Ground)**





**Photo - 6: Installation of Antennas and Equipment on Gamma Sector (From Ground)**

Alpha



Sep 12, 2023 8:36:28 AM  
7 Sturges Hollow Road  
Westport  
Fairfield County  
Connecticut
