

CJIS-CT Governing Board

Quarterly Governing Board Meeting
July 24, 2025

*Held at the Division of Criminal Justice (DCJ),
Rocky Hill, CT.*





Update on Previous Action Items

Governing Board Meeting Action Item List			
Task	Owner	Status	Date Originated
Finalize Judicial Review of Security Policy	Diana Varese/ Sridhar Brahma	Complete	4/24/2025
Complete MOU for DEEP ENCON Onboarding	DEEP Commissioner's Office and CJIS	Complete	4/24/2025
Digital Evidence – Work out an approval process for the Digital Evidence study and next steps	James McGennis/Mark Tezaris	In Progress	4/24/2025



Wethersfield PD – CISS Search Use Case



Andrew Jacobson
Investigator/Detective/Officer



- 25+ years in law enforcement
 - 10 years with the Office of the Chief State's Attorney – Cold Case Unit
 - Helped secure arrests, convictions, and prison sentences for multiple violent felons in state & federal courts
- Retired from Hartford PD; now at Wethersfield PD supporting the Detective Bureau
- Leveraging experience, including CISS Search, to advance active and cold cases



Board Education: RMS Vendor 101

Introduction & Purpose:

- Define RMS and its role within the LEA (Law Enforcement Agency)
- RMS capabilities, benefits, and implementation



1. Strategic Importance of RMS



2. Core (Key) Capabilities of RMS



3. Benefits to LEA and Criminal Justice




4. Paper vs. Electronic Workflow Comparison



5. Implementation – CT RMS Vendor Landscape



6. Risks & Mitigation

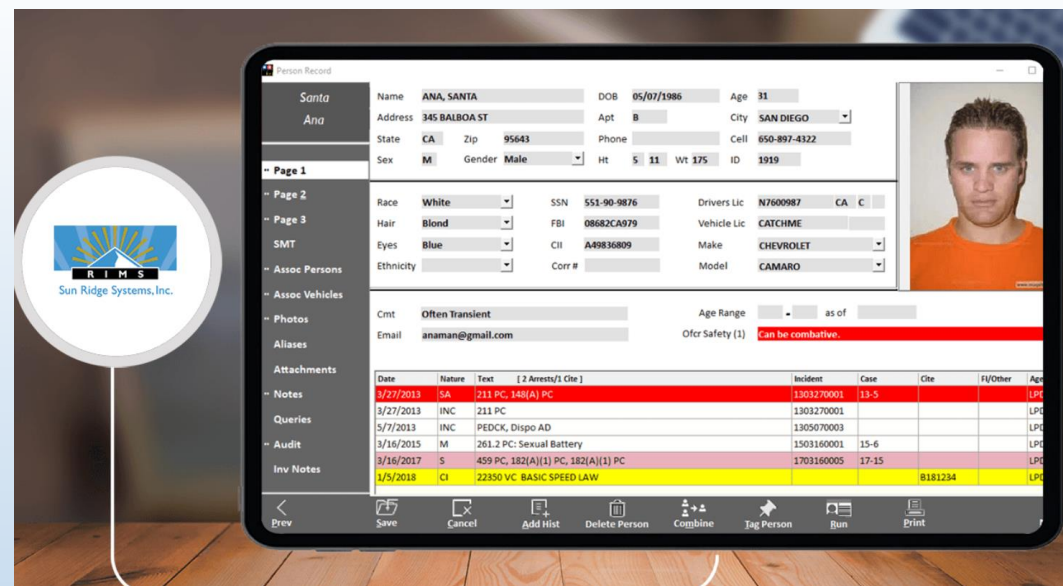

What is RMS?

Records Management System (RMS) is an agency-wide system that provides for the storage, retrieval, retention, updating, archiving, and viewing of information, records, documents, or files pertaining to law enforcement operations. RMS covers the entire life span of records development— from the initial generation to its completion.



Strategic Importance of an CAD/RMS

Most important responsibilities for a police LEA dispatcher CAD*:

- 🚨 **Respond to emergency calls** with speed, empathy, clarity, elicit information
- 📡 **Dispatch officers** to incidents and coordinate field operations
- 🗣️ **Communicate vital information** pulling information from systems
- 📄 **Document calls and actions** accurately for legal and operational use
- 🔒 **Maintain confidentiality** and manage sensitive law enforcement data



Important aspects for a police officer using a RMS in their vehicle:

- 🚗 **Real-time access** to incident data
- 📄 **Efficient report** writing and submission
- 🔍 **Quick search** capabilities
- 🔒 **Secure data** handling and compliance
- 🔗 **Seamless integration** with CAD* and other systems

(*CAD - Computer Aided Dispatch)



Law Enforcement Agency RMS– Key Capabilities

A Law Enforcement Agency (LEA) RMS plays a pivotal role in ensuring operational efficiency, legal compliance, and public safety. Top **responsibilities** of an LEA RMS:

1. Incident and Case Documentation

- Capture and manage reports for incidents, arrests, citations, and investigations

2. Secure Data Storage and Access Control

- Store sensitive law enforcement data securely with encryption and access restrictions

3. Search, Retrieval, and Sharing of Records

- Provide fast, reliable search tools for officers, detectives, and administrators

4. Reporting and Analytics

- Generate reports for crime trends, resource allocation, and performance metrics
- Support dashboards for command staff to make data-driven decisions

5. Lifecycle and Compliance Management

- Manage retention schedules, record sealing, and purging in accordance with law






The screenshot shows a detailed 'ARREST REPORT' form. Key sections include:

- AGENCY INFO:** Agency Name, Date, Time, Location, Arrestee Name, Address, City, State, Zip, County, and Date of Birth.
- ARRESTEE INFORMATION:** Arrestee's Name, Address, City, State, Zip, Date of Birth, and Date of Arrest.
- ARREST INFO:** Arrest Type, Arrestee's Name, Address, City, State, Zip, Date of Birth, and Date of Arrest.
- U.S. INFO:** U.S. Name, U.S. Address, U.S. City, U.S. State, U.S. Zip, U.S. Date of Birth, and U.S. Date of Arrest.
- COMPLAINT:** Complaint Number, Complaint Description, Complaint Date, and Complaint Status.
- ARRESTEE SIGNATURE:** Arrestee's Signature, Date, and Time.



Benefits to LEA and Criminal Justice Agencies

Major challenges police officers often face when completing arrest paperwork:

-  **Time-consuming documentation**
Officers can spend **three or more hours per shift** on paperwork, which takes time away from active policing and community engagement.
-  **Memory-dependent accuracy**
Reports are often written hours after incidents, relying on memory or handwritten notes, which can lead to inaccuracies or missing details.
-  **Risk to officer safety**
Completing paperwork in patrol vehicles can leave officers heads-down and distracted, making them vulnerable to ambushes or accidents.
-  **Manual data entry errors**
Typing reports manually—especially in non-ergonomic environments like squad cars—can result in factual mistakes, typos, or formatting issues that may affect court proceedings.
-  **Deadline pressure and legal consequences**
Missing documentation deadlines can delay or derail prosecutions, especially in jurisdictions with strict filing rules





Pre-CISS Paper Process vs. Electronic Workflow Process



Pre-CISS Paper Process



Electronic Workflow Process




RMS Vendors – Market Landscape

Who Are the RMS Vendors in the State of CT?

- **NexGen RMS**
- **CT State Police:** NexGen RMS
- **Accucom RMS**
- **IMC RMS:** Central Square Parent Company Group
- **Inform RMS:** Central Square Parent Company Group
- **Motorola RMS**
- **ProPhoenix RMS**
 - New Haven MPD



Percent (%) of CT Arrests by RMS Vendor

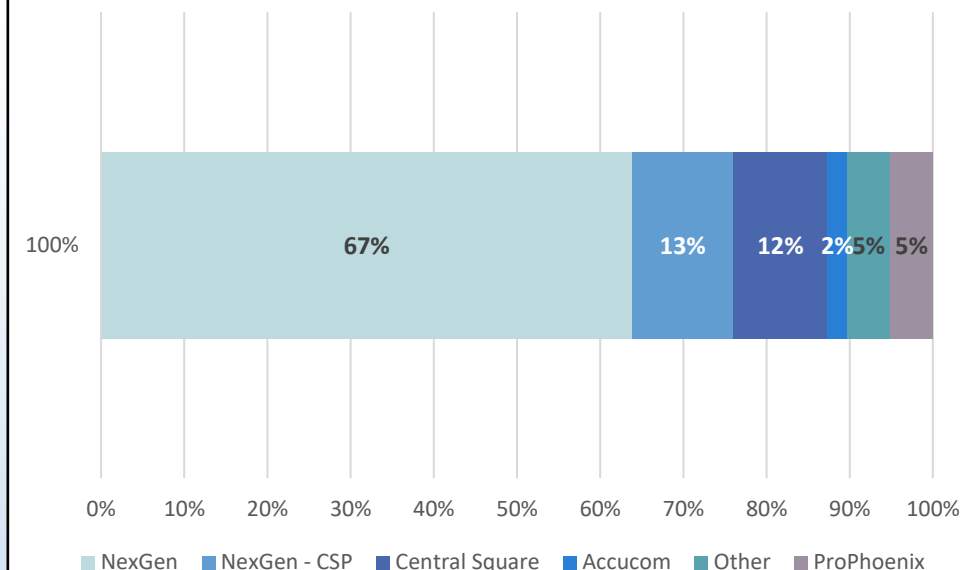

Interesting Facts

- Some other States have mandated a single RMS to simplify the effort and scope
- CT maintains an open and competitive market for RMS selection by each LEA
- When the project started there were over 20 different RMS systems in use in CT
- Now through a competitive CT marketplace we have consolidated down under 10.

CT RMS Market Analysis: September 2024 Analysis

Risks/Issues/Mitigations

- **Risk:** New RMS vendor selection by PDs | **Mitigation:** New legislation requires electronic integration, CJIS-CT developing new RMS policy ([Public Act No. 23-36](#))
- **Effective October 1, 2023**, per [P.A. 23-36](#) (C.G.S. Section 54-142s (g)), All RMS Vendors must meet approval and have intent to include connectivity in the implementation



CJIS-CT – CISS Source Systems Interface Status Report



Source System	Description	Branch or Agency Partner	Connection to CISS	Search	Workflow
OBIS-Offender Based Information System	Tracks individuals and offenders who are being supervised in the State's penal system.	DOC	●	✓	
Case Notes	Community supervision tracking system	DOC, BOPP	●	✓	
ePardon	Electronic portal for pardon application and management	BOPP	●		✓
CRMVS	Criminal Motor Vehicle System –court case management system for all criminal and motor vehicle cases in the GA and JD courts.	JUD	●	✓	
PRAWN	Paperless Re-Arrest Warrant Network	JUD	●	✓	
POR	Protection Order Registry –information system that tracks individual protective orders, standing criminal restraining orders, no contact orders and restraining orders	JUD	●	✓	
CIB	Centralized Infractions Bureau – information system that manages the cases initiated through the Complaint Ticket process: generally handles only the payment of monies for these cases.	JUD	●	✓	
CMIS	Case Management Information System - information system which tracks bail and probation data.	JUD	●	✓	✓
eProsecutor	Case Management System for use by prosecutors	DCJ	●		✓

Status Indicators

● Complete

▲ On Plan/
In Progress

■ Watch

⬡ Barriers

***CJIS-CT is starting to collect uptime for each source system and will provide periodic reports. The Goal is overall uptime to be 99.9%.**



CJIS-CT – CISS Source Systems Interface Status Report (cont'd)



Source System	Description	Branch or Agency Partner	Connection to CISS	Search	Workflow
Driver and Vehicle Registration	Integrated vehicle and licensing system	DMV	●	✓	
MNI/CCH	Master Name Index / Computerized Criminal History	DESPP	●	✓	
SOR	Sex Offender Registry	DESPP	●	✓	
Arrest Data	Arrest data from municipal PD Record Management Systems – ACCUCOM, IMC Vendors	Multiple MPD	▲	✓	✓
Arrest Data (CSP)	Data on arrests from CSP Record Management Systems	DESPP	▲	✓	✓
WANTED	COLLECT Data for state and federal Wanted persons.	DESPP	■	✓	
DMV Photos via COLLECT	SLEO Access to DMV Photos via COLLECT	DESPP/DMV	■	✓	
WEAPONS	Information Management System for tracking gun licenses (Removed from CISS)	DESPP	⬢	✓	

Status Indicators

- Complete
- ▲ On Plan/ In Progress
- Watch
- ⬢ Barriers

For Watch and Barrier Items – discussions are ongoing to improve the overall data availability.



CJIS-CT Security Review

Security Topic	Completed	In Progress	Not Started
CJIS-CT Security Policy 2.0	✓		
Audit – CJIS-CT Site Survey by DESPP	✓		
Audit – Evaluation of CJIS Security controls implemented in CISS Search	✓		
Audit – Background Investigation of CJIS-CT Employees and Consultants	✓		
Audit – Vendor APIs	✓		
Audit – DMV and JOCE		✓ (August 2025)	
Audit – CISS Electronic Workflows Arrest Data		✓ (August 2025)	
Audit – Whitelisting IPs from State and Local Agencies			✓
Audit – Complete Understanding of Source System			✓ (August 2025)
Audit – Account Management & Access			✓
Audit – Physical Location Inspection			✓



CISS Workflow Deployment

Target: June 2026 (NexGen)

Status: On Schedule

Budget: FY26 funding requested for 1.7M.

Tasks Underway/Accomplishments



- Release 11.4.7 (ECM Document Routing Changes for CSSD) completed on May 09, 2025.
- Completed CSSD training for Pretrial and Probation personnel in GA-15 to enable full paperless processing of arrest documentation
- Ansonia and Seymour PD’s achieved full electronic certification Status
- Initiated enhanced monitoring for 8 MPD’s that have met the initial qualification to go fully “Paperless”

Key Dates/Next

- Complete certification of 8 PD that are currently in the enhanced monitoring stage prior to full certification
- Arrest Package Workflow: Restart statewide deployment schedule
- Clean Slate Erasures: Enable PDs to process through RMS

Risks/Issues/Mitigations

- Risk: Deployment delays due to PD readiness and prioritization | Mitigation: Increased escalation to PD leadership as well as utilizing DCJ as an escalation point

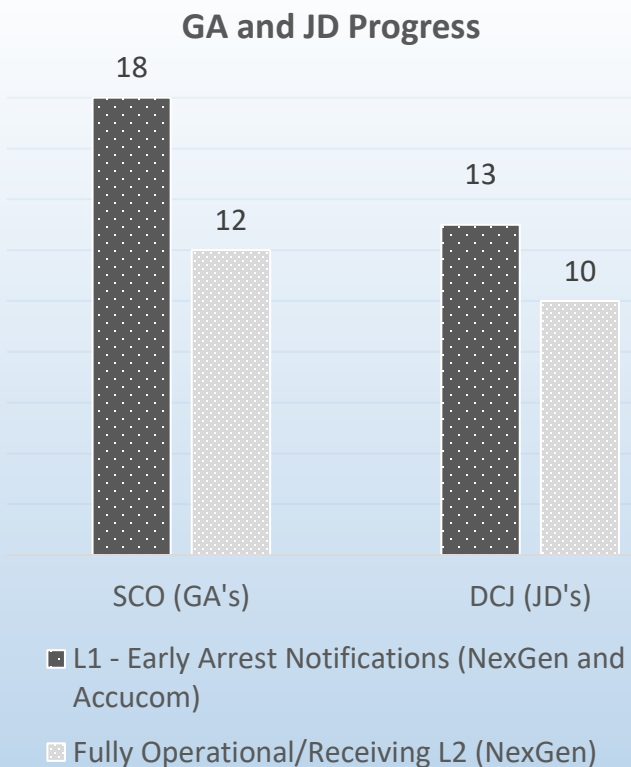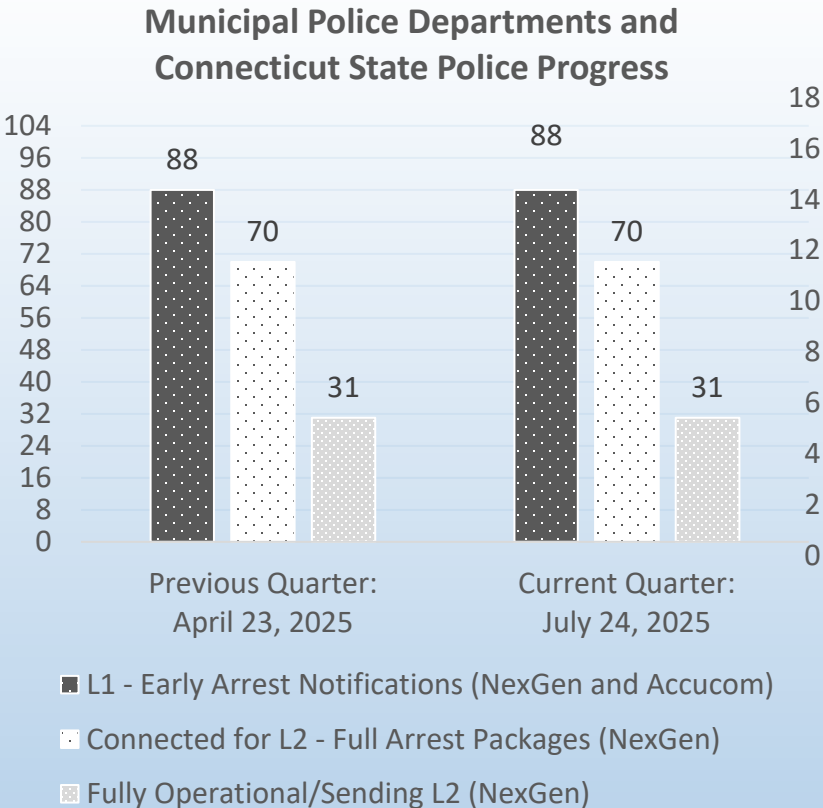


Phase 1 = L1 = Early Arrest Notifications
Phase 2 = L2 = Full Arrest Packages




April 2025 through June 2025 Arrest Package Performance and Defect Tracking

Arrest Package Performance

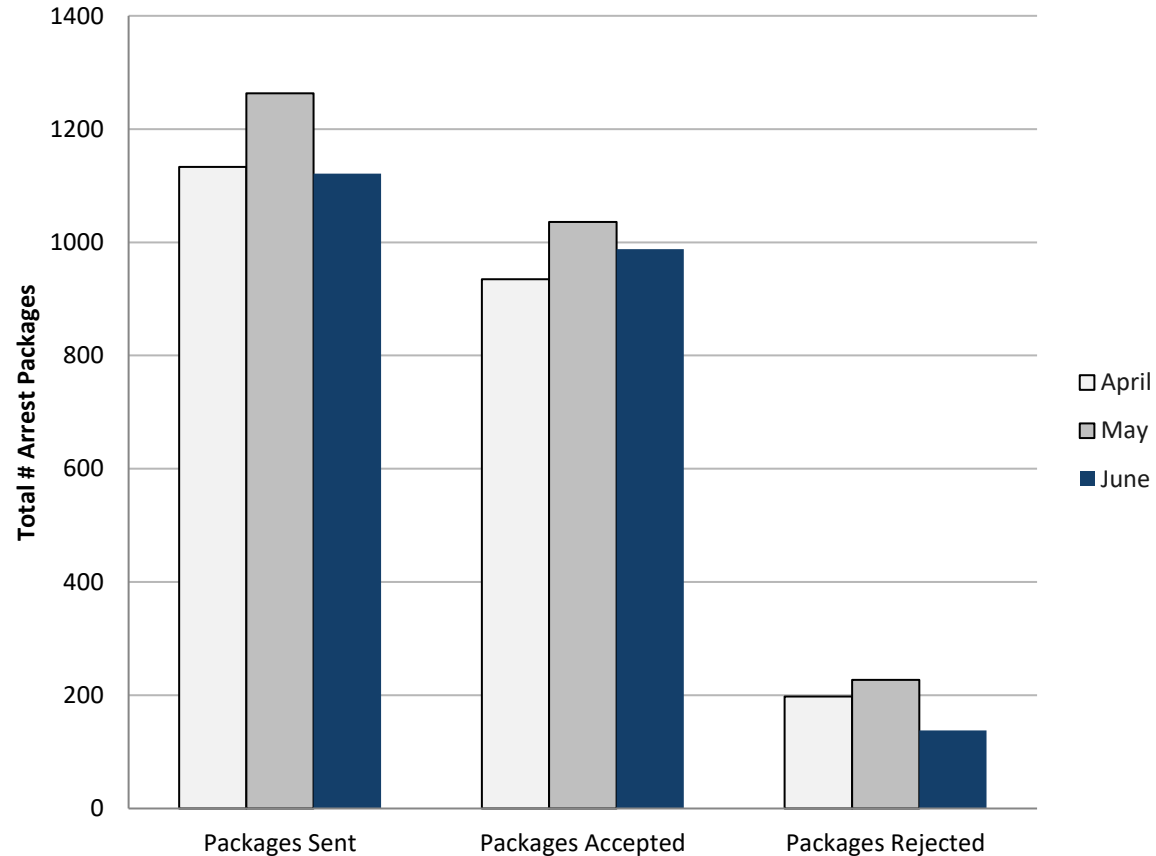

Defect Trends

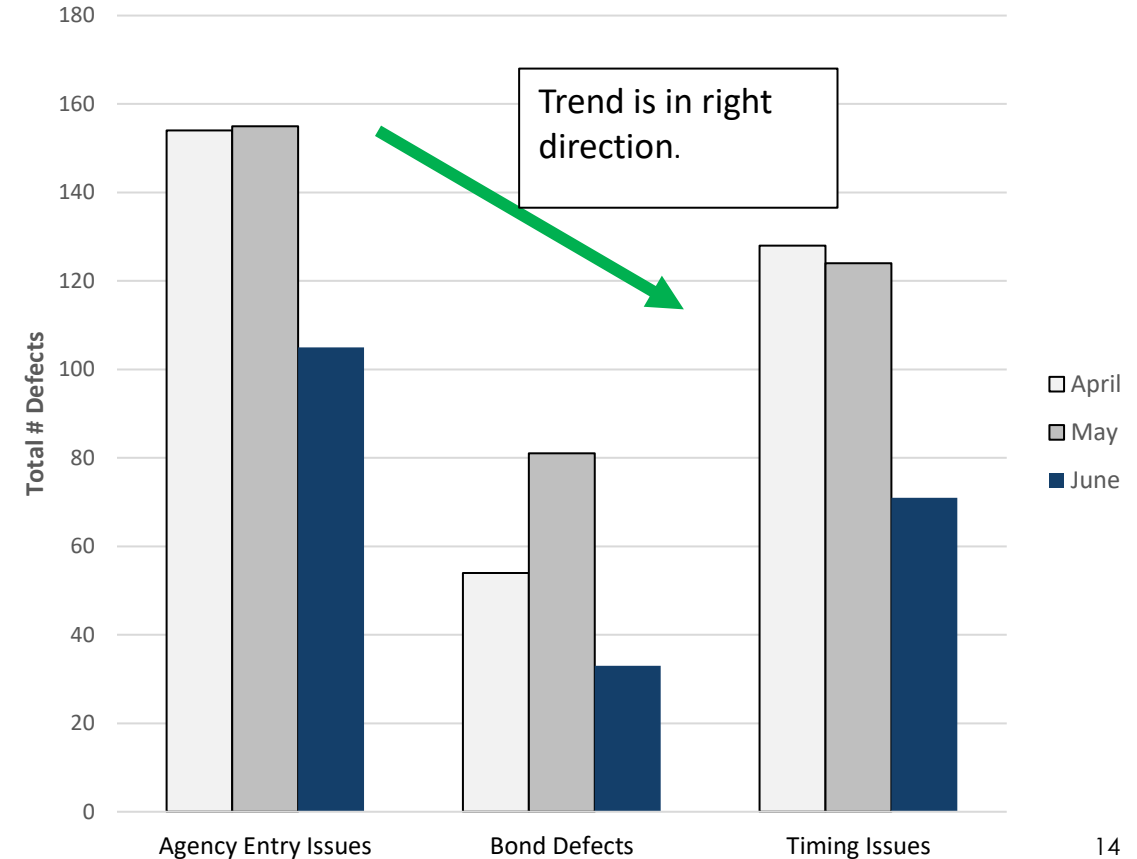



CSP Workflow - Electronic Arrest Deployment Dependencies

CSP Pilot Tasks Underway/Accomplishments

- **NexGen RMS - CT State Police:** Revised software evaluation and pilot training – COMPLETE
- **Regional Centers of Excellence:** Establishing centers in East, Central, and West regions – COMPLETE
- **Collaboration:** Partnering with municipal police departments for support and training – IN PROCESS


Prerequisites for Production Readiness for CISS Electronic Arrest Workflow

- **Court Liaison Staffing:** DESPP to work on a “Plan D” to staff the Electronic RMS Arrest Workflow – ON HOLD until next fiscal year
- Approval of CISS as a CJIS compliant “Vendor System” that is certified to have CSP CJIS and FBI Data – DESPP CSO – IN PROCESS
- Production Servers at DAS Groton Data Center have to be Certified for CJIS and built – COMPLETE
 - DESPP CSO Approval on GDC Server Stack – COMPLETE
 - Migration of Current RMS Production Servers to new Current Technology Stack in Groton - DESPP/DAS – IN PROCESS
 - Buildout of new RMS Production Servers to new Future Technology Stack in Groton - DESPP/DAS – IN PROCESS (NexGen)
- RMS Computer Workstations with All-in-One scanners for dedicated RMS electronic workflow processing (Evidence Officers) – DESPP/DAS – IN PROCESS
- All JD Court Systems must be online and receiving Electronic Arrest Workflow before CSP can onboard – CJIS-CT/Judicial/DCJ – IN PROCESS

1. Pilot Team on Track



2. Administrative Projects – High Risk Activities

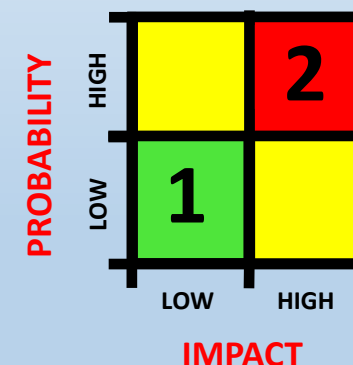



CISS Search Training and Onboarding

Target: Search Usage/Onboarding Efficiencies	Status: On Schedule	Budget: Aligned within budget limitations
--	---------------------	---

Tasks Underway/Accomplishments


- CJIS-CT Accomplishments:** Trained approx. 1,000 new CISS Search users (July 2024–July 2025); on pace to hit 7,000 trained users by December 2025. | Onboarding underway for MTA Police, Amtrak Police, and Litchfield County Dispatch (working directly with sponsoring PD Agency Admins) | Southbury PD on deck for onboarding | Continuously updating and adding training materials; shifting to fully electronic onboarding with eCUAR. | Partnering with the Law Enforcement Imaging Technology Task Force (LEITTF) to support IACP’s white paper on facial recognition—positioning CJIS-CT at the forefront of emerging tech guidance.
 - Underway:** Creating CISS Search accounts for personnel from DEEP (all are trained and have CUARs on file).
 - Underway:** Onboarding roughly 385 users from DPDS (CUARs in process) and working with CSSD on their 400+ users.
 - Underway:** New Agencies currently working toward onboarding - MTA, Amtrak, Litchfield County Dispatch and Southbury PD
 - Underway:** Gathering the next group of agencies/departments to onboard (example is Northwest Public Safety and State Colleges).

Key Dates/Next

- Q3:** Complete onboarding tasks for MTA, Amtrak, Southbury PD and LCD.
- Ongoing 2025:** CISS Search Training to achieve steady state
 - Training at CSP and MPD Academies (Last trainings - 7/8/25 CSP Academy and 7/16/25 at POSTC)
 - Train the Trainers (working on requirements with POSTC)
 - Rollcall Training (identify super users for Train the Trainer)

Risks/Issues/Mitigations

- Issue:** Manual onboarding inefficiencies | **Mitigation:** eCUAR (In Testing)
- Issue:** Certification success does not equate to increased usage. | **Mitigation:** Exploring usage opportunities and partnerships (JOCE/JASPA).

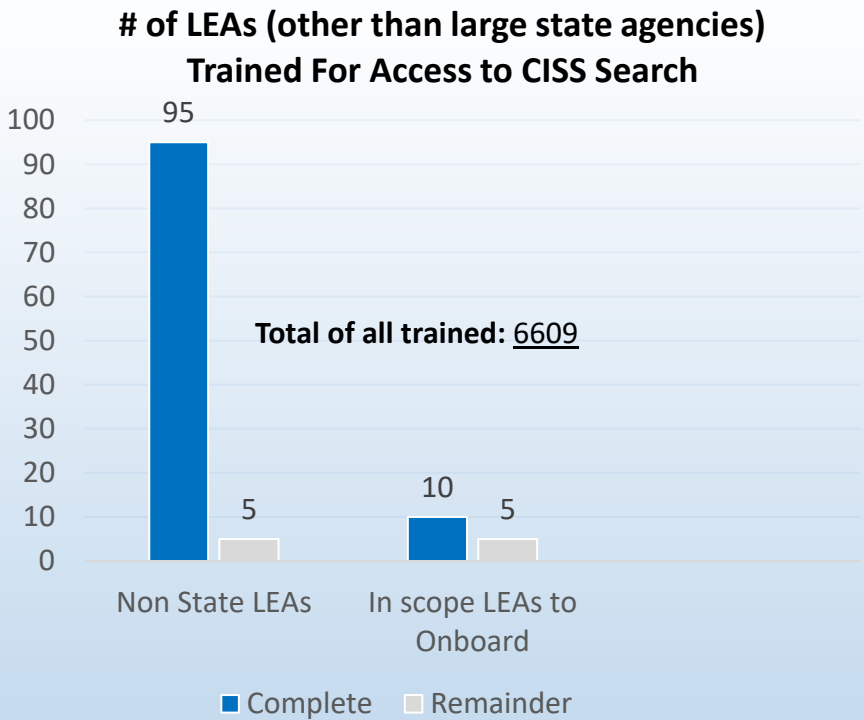

Total MPDs : 95 which includes Southbury PD

New Agencies Awaiting Onboarding: 4 is in process (MTA, AMTRAK, LCD, Southbury PD) with DEEP being onboarded.



Digital Evidence Study

Target: 08/2025

Status: Phase – Closeout

Budget: \$500K/(\$197K Remaining)

Accomplishments

- ✓ Current State Assessment Document – **Complete**
- ✓ ROI/TCO Analysis – Planning and Costing for each Solution Approach (1-5) – **Complete**
- ✓ Study Team and Stakeholder Solution Selection Workshops (Steps 12 & 13) –
 - ✓ 1st Workshop (Virtual) – **Complete (12/12/24)**, 2nd Workshop (In-Person) - **Complete (01/16/25)**
- ✓ Future State Document – **Complete**
 - ✓ Revision to include Solution Approach Ranking Matrix and ROI – **In Process**

Tasks Underway

- ✓ Executive Summary Document - **DRAFT Complete – Distributed for Executive Stakeholder Review**
- ✓ Stakeholder Agency Executive Reviews – **In Process**

Results

- ✓ All Five (5) Solution Approaches analyzed in the Study – Comparison in Graph in Appendix - **Complete**

Key Dates/Next

- NASPO - State Level DEMS Contract Option – **In-Process** – AG's Office Legal Review
- Pilot – Solution Approach #4B – Demonstration of Digital Media Files as part of the CISS Electronic Workflow – Q3/Q4
- **Draft reports are with key stakeholder for review. We expect it to take 1-2 months to finalize all documents.**


Risks/Issues/Mitigations

Financing – Risk: without funding this project will be on hold | **Issue:** Capital Funding is limited | **Mitigation:** Pursue funding through grants and state agencies for a low-cost enhancement to electronic arrest paperwork workflow which provides significant value to Stakeholders.





CISS Search Analytics and Research

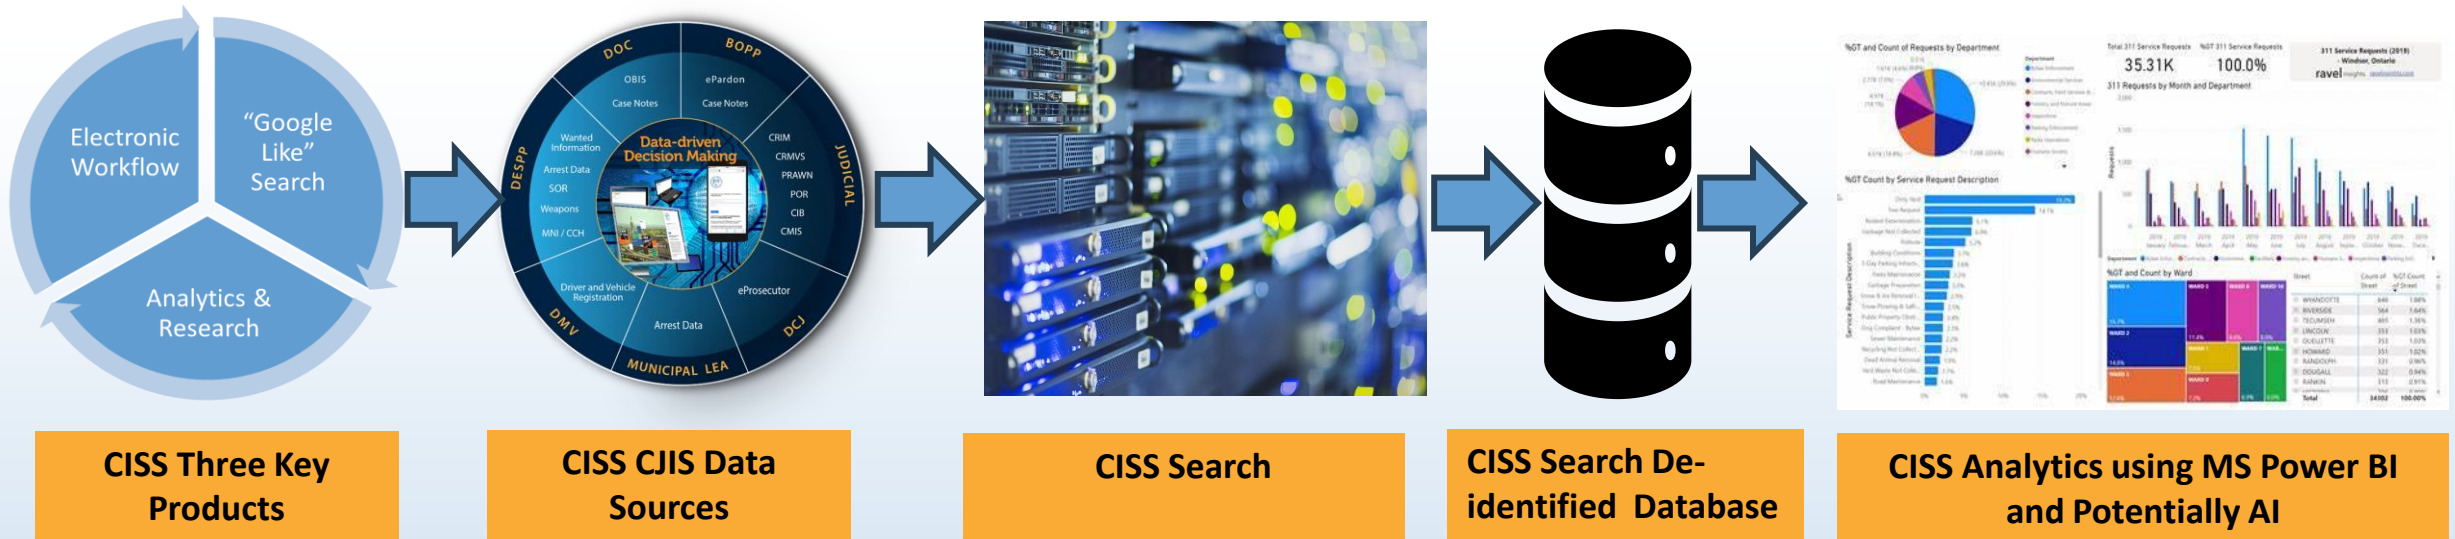

CJIS-CT Deidentified Master Database	
Included Data Sources	System
CSSD	CMIS
DESPP	MNI/CCH
DESPP	SOR
DMV	DRIVERS
DMV	VEHICLES
DOC	OBIS
DOC/BOPP	CASENOTES
SCO	CIB
SCO	CRMVS
SCO	POR
SCO	PRAWN

Key Points:


- Prototype started – Work part time. Internal demo targeted for September 2025
- On-going reusable solution for research instead of “one-time” throw away solutions
- Governance to share de-identified data - TBD
- Security will be included – TBD

Recent Requests Include:

- Sentencing Commission
- Police Use of Force Transparency (PA 19-90)
- OPM/Urban Institute
- Connecticut Racial Profiling Prohibition Project



CJIS-CT Governing Board 2025 Meeting Schedule

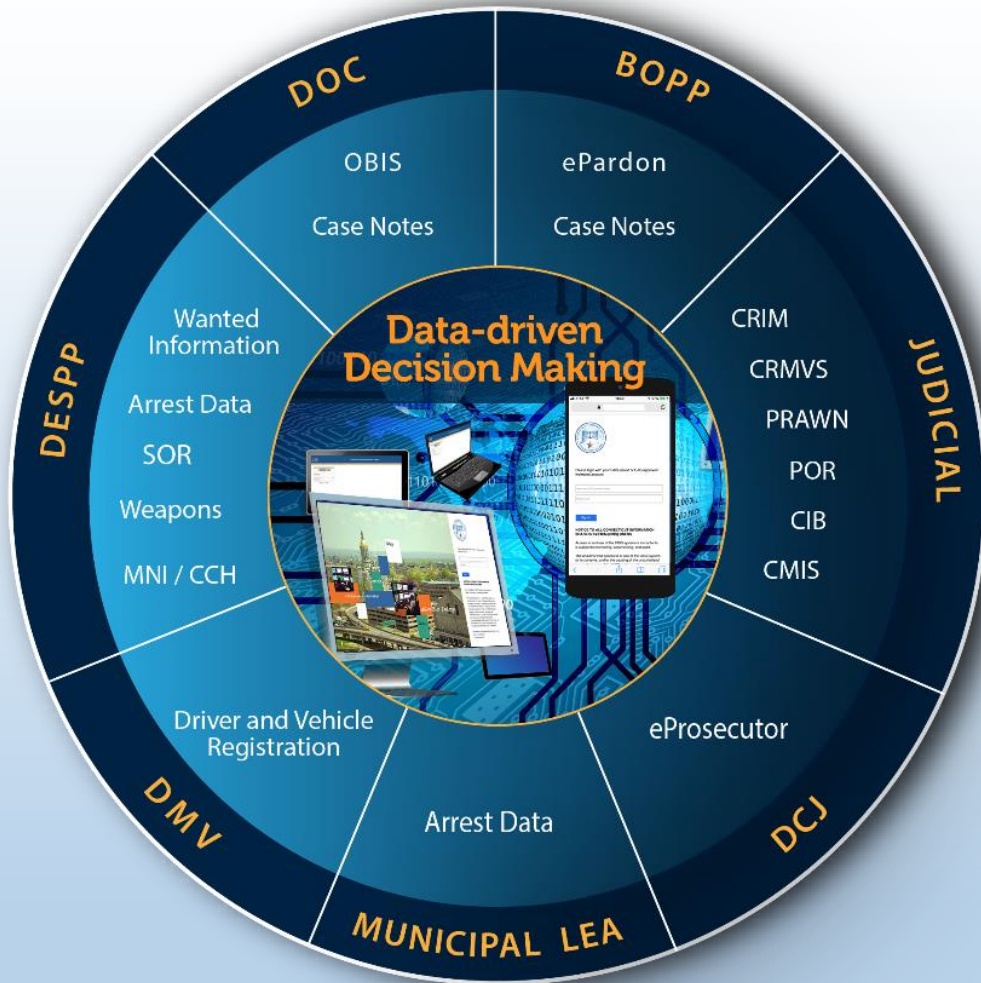

Next Meeting

October 23, 2025

For questions and comments email
CJIS.HelpDesk@ct.gov

CISS Dashboard
<https://dashboard.cjis-ciiss.ct.gov>

CJIS-CT Website
<https://portal.ct.gov/cjis>



Appendix-Reference Material



CISS Operations Scorecard

Metric	Target	Owner	Frequency for Review	Status	Trend	Comments
Help Desk-Tickets	5 days MTTR Mean Time to Resolve	Pat D.	Monthly			Currently 10 days. CJIS has reduced the Help Desk staff by 1 analyst due to budget..
Capacity Management	System capacity	Anatolie	Monthly			Hardware, applications, and licenses
Availability Management (OM reading)	System uptime 99.9% excluding scheduled downtime.	Anatolie, Archana	Monthly			Current uptime at 98.6%. Project to monitor in progress.
Endpoint Management	SCCM up to date	Anatolie, Archana	Monthly			Current and up to date
End of Life (EOL) Management	EOL systems identified and managed	Anatolie, Archana	Monthly			All identified, updated SharePoint to 2019. Ongoing updates..
Security-Unpatched Vulnerabilities	None	Anatolie, Archana	Monthly			Monthly patch 1 week behind plan as planned.
RMS Connectivity for CISS Workflows	Router connectivity to CISS	Archana	Monthly			Router connectivity tracking for CISS Workflow.
Time to onboard-PD (days)	Metric is number of days between the first police officer trained and the last, inclusive, as Service Excellence Initiatives	Derek	Monthly			Metric added to onboarding MPD. Goal is 3 months to onboard. Some taking longer due to MPD personnel availability conflicting with job.
Time to onboard-single user (days)	First use date-training date	Derek	Monthly			Reports shared periodically meetings to Governance and Governing Board.

Status Indicators

- Complete
- On Plan/ In Progress
- Watch
- Barriers

Trend Indicators

- No change since last review
- Improving status since last review
- Declining/worse status since last review



CISS Project Timeline



CISS Phase 1

Product Development software and hardware infrastructure (Complete 2020)

2009

- Initiate CISS Planning Phase.

2012

- Business/Technical Process Reviews.

2012–2015

- Agency Negotiation and Agreement to Share CJIS Data. Created Governance structure and signed major vendors.

2016–2020

- CISS Software Development. Initial training of State agencies and Municipal Police Departments.

2018–2020

- Releases CISS Software



CISS Phase 2

Additional RMS integrations/CISS version upgrades & Workflow Deployment/Training for PDs and Agencies (ongoing thru December 2028)

2020–2028

- Continued Training of State Agencies and Municipal Police Departments

2022: Case Success

- New Milford PD uses CISS to solve bank robbery case.

2023

- CISS reaches user milestone with 4,000 searches and 5,000 information exchanges monthly.

2024

- Cannabis Erasures
- Clean Slate
- Established CISS Users Group
- Internet Access for CISS Search



2025–Future

Sustainment phase of the product life cycle including on-going training and support, new initiatives and Use Cases, and data analytics/reports that is available for its customers.

2025–Future

- New CISS releases with new features
 - Additional Digital Workflows for information sharing between Connecticut criminal justice community.
 - CISS Search 2.0 upgrade to include Police Community Alerts, new source systems and AI search capabilities
 - Other (input from CISS users)
- Complete CISS Workflow Deployment for about 80 PDs and State Police using NexGen RMS
- Add additional RMS vendors to get 90%+ of all arrest using CISS Digital Workflows
- Digital Evidence Management (potential)
- CISS Analytics Product Development to Share De-Identified CJIS Data for Policy Analysis.
- Steady state for maintenance, support and budget.



CJIS-CT Project Descriptions

- **CISS Phase 2: Workflow Deployment**

The Workflow will replace current paper-based workflows with electronic messages and documents. L1 (Early Arrest Notifications) and L2 (Full Arrest Packages) represent different arrest package types.

- **CISS Phase 2: CISS Search | Connectivity**

CISS will take data input from criminal justice databases and make it searchable to law enforcement and criminal justice officials with the proper security clearance and credentials. This project is for deploying Search tool to municipal PDs and other agencies.

- **CJIS-CT Transition from Deployment to Steady State Phase**

As CJIS-CT and our partner agencies complete the deployment of CISS Workflows for NexGen, Accucom and IMC by the end of 2024, CJIS-CT will have transitioned to a “steady state” operational and maintenance phase.

- We will maintain a build, test, deploy capability and change control for new releases of CISS, and other production systems.
- Current effort to transition consultant positions to state positions to retain critical domain knowledge in progress.
- New significant projects will need funding for each project.



CJIS-CT Project Descriptions

- **Clean Slate Automation System**

Under legislation, Section [54-142a](#) of [PA 23-169](#), persons with criminal convictions will have certain records erased automatically after a set period of time. Operation of law is construed as Automated Erasure in the context of systems specifications used to develop and support technology components that implement the Clean Slate statute. CJIS-CT supports the Sentence Discharge Database (SDDDB) component of the Clean Slate Solution.

- **Clean Slate Message Viewer Portal Training**

CT Legislation has launched a Clean Slate Automatic Erasure Initiative. The Clean Slate Messages will be loaded into a CJIS-CT web application called Message Viewer Portal (MVP). Each LEA will need to have designated users with CJIS-CT accounts to log into the MVP where they will be able to select and download the Clean Slate Messages directed to their Agency for Erasure Action.



CJIS-CT Project Descriptions

- **Digital Evidence Study**

Deliver a study which aims to characterize the design and implementation of a digital centralized storage system, with sharing capabilities, effectively addressing the challenges faced by State agencies and municipal police departments in managing and storing digital evidence securely and efficiently. This includes storage of Body Worn Camera (BWC) and dash cameras bulk media. A key objective is to evaluate utilization of CISS for sharing of digital evidence. A report and briefing will be provided to interested stakeholders including executive, legislative and judicial branch stakeholders for direction on the implementation phase.

- **RMS Vendors – Integration Updates**

Police Records Management Systems (RMS) enable law enforcement agencies to store, retrieve, retain, archive, and view information, records, or files pertaining to law enforcement operations.



Clean Slate Automation System – Sentence Discharge Database (SDDB)

Deferred Scope Target: 2025

Status: Schedule – Live 1/1/2024

Budget: \$1,640,754*

Tasks Underway/Accomplishments

- **SDDB:** In production, supporting Clean Slate automation with 23+ year case history
- **SDDB v1.3.1:** Updated matching criteria in SDDB code to properly identify related transferred cases
- **DUI 14-227a:** Completed Custom eligibility development for SDDB and CCH


Key Dates/Next

- **DOC Discharges:** Reapplying ADMs to SDDB data after non-custodial record processing
- **Project Scope & Data Remediation:** Continue to scope and address new requirements identified and prioritized during initial launch
- **Erase Reversal:** Discovery and scoping of process

Risks/Issues/Mitigations

- **Risk:** Additional scope added to requirements | **Mitigation:** Any changes to CJIS requirements will need to follow the SDLC process which could impact schedule and budget

*CJIS-CT Budget
- Deferred Scope (new legislation [PA 23-169](#))
- Additional budget request made to OPM for FY 2025/2026 Project Work

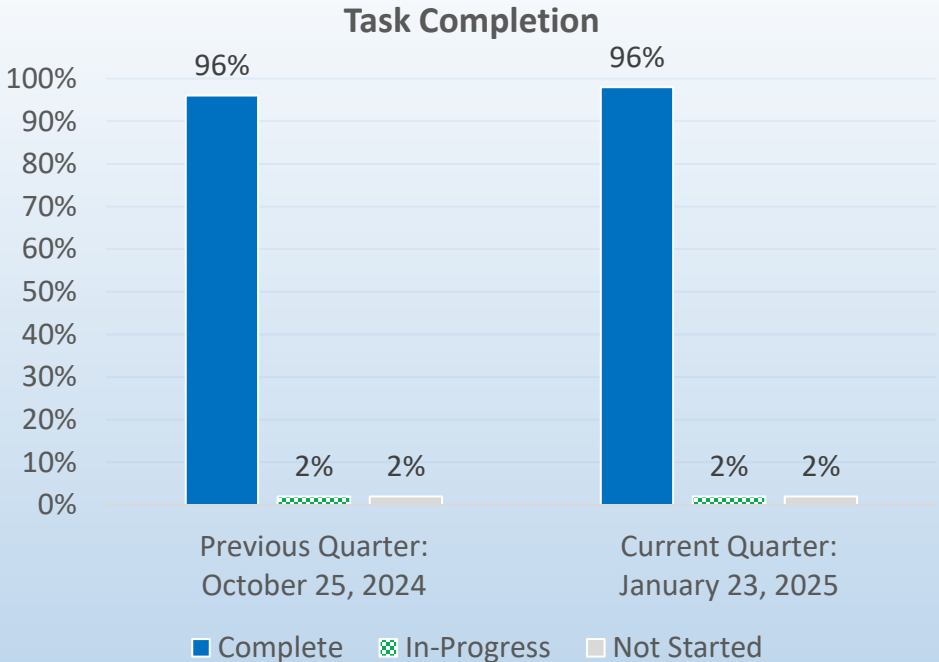

Note: Task completion status in July represents impact of project delays,



CJIS-CT Project Portfolio – July 2025 (1/2)

Project No.	Priority No.	Project Name	Project Status	Start	Finish	Status (%)
1	1.000	Clean Slate Automation Project	On schedule	3/1/2022	1/19/2026	88%
2	1.015	CISS Search - RMS Records Clean Slate Erasure	On schedule	11/17/2023	9/16/2025	87%
3	1.015	Develop analytics capability to support OPM	On schedule	4/1/2025	11/19/2025	53%
4	1.017	CISS WebServices Failure Recovery Options	On schedule	3/11/2024	8/1/2025	87%
5	1.017	CJIS-CT System Center CISS Endpoint Monitoring	On schedule	7/5/2024	8/27/2025	96%
6	1.030	Digital Media and Evidence Study	On schedule	4/10/2023	4/21/2026	85%
7	1.060	SharePoint Subscription Server Edition Upgrade	On schedule	6/23/2025	3/5/2026	6%
8	1.5	CISS SharePoint 2019 Post Prod Defect Fixes	On schedule	6/30/2025	11/5/2025	20%
9	1.500	INFORM-RMS-Vendor_Certification_Level-1_and_Level-2	On-Hold - Stakeholders Dependency	3/31/2025	7/1/2027	0%
10	1.999	Clean Slate Reversal	On-Hold - Stakeholders Dependency	9/1/2025	12/24/2025	0%
11	2.000	Third-Party External Audit – Security Architecture	On schedule	5/29/2025	12/3/2025	22%
12	2.000	DESPP Audits	On schedule	5/29/2025	12/31/2025	24%
13	2.000	CISS Workflow Deployment	On schedule	1/30/2017	1/8/2026	82%
14	2.002	CJIS Resources Vacation Information	On schedule	2/8/2024	1/1/2026	12%
15	2.005	Infrastructure Miscellaneous Project	On schedule	1/5/2024	7/17/2026	1%
16	2.010	NexGen_RMS-Vendor_Certification_Level-1_and_Level-2	On schedule	12/4/2017	11/13/2025	92%
17	2.020	CT State Police CISS UAT L2 Pilot - Troop C and Troop F	On schedule	10/18/2021	12/12/2025	90%
18	2.024	LiveScan Business Requirements for CISS Electronic Workflow	On schedule	10/3/2024	8/18/2025	97%
19	2.030	Accucom-RMS-Vendor_Certification_Level-1_and_Level-2	On schedule	6/11/2018	3/25/2026	90%
20	2.040	RMS Level 2 Workflow GA Integrated Multi Agency Testing	On schedule	12/20/2019	3/31/2028	64%
21	2.050	CISS 11-5 - CSSD Release	Early	7/1/2025	9/24/2026	0%
22	2.051	ProPhoenix-RMS-Vendor_Certification Level-1 and Level-2	On schedule	2/15/2024	1/12/2027	33%
23	2.060	IMC-RMS-Vendor_Certification_Level-1_and_Level-2	On schedule	12/8/2020	4/21/2027	24%
24	2.061	Urban Institute - OPM - De Identified Criminal History Data Set	On schedule	7/26/2024	9/24/2026	6%
25	2.080	CJIS SP Farm Consolidation	On schedule	3/3/2022	8/13/2025	85%
26	2.090	Workflow Submissions Portal_Phase1	On-Hold - Resource Constraints	2/3/2021	11/14/2025	71%
27	2.091	Help Desk Misc Tasks Plan	On schedule	1/2/2024	3/2/2026	48%
28	2.100	L1 Reports SOP	On schedule	3/1/2024	10/14/2025	82%



CJIS-CT Project Portfolio – July 2025(2/2)

Project No.	Priority No.	Project Name	Project Status	Start	Finish	Status (%)
29	3.000	CISS Search Training v1	On schedule	1/11/2016	9/30/2025	98%
30	3.000	CISS 2_0 Search	On schedule	8/27/2024	1/15/2029	52%
31	3.001	CISS-JOCE Collaboration	On-Hold - Change in Scope/Goals	8/16/2023	11/4/2025	59%
32	3.009	Project-X - Expected Legislative Changes - Management Reserve	On-Hold - Stakeholders Dependency	12/2/2024	9/18/2025	0%
33	3.010	eCUAR	On schedule	9/7/2021	12/22/2025	75%
34	3.020	Weapons Interface through CCH with CISS	On-Hold - Stakeholders Dependency	4/3/2023	2/5/2026	78%
35	3.050	CISS - MultiVue Upgrade	On schedule	9/8/2023	1/12/2026	75%
36	3.090	Automating CISS-JUD Code Tables	On schedule	1/10/2023	9/2/2025	94%
37	3.091	MTA	On-Hold - Stakeholders Dependency	10/2/2023	9/26/2025	94%
38	3.092	Technical Writer Projects- New	On schedule	3/4/2024	1/26/2026	4%
39	3.093	Agile Transformation	On-Hold - Resource Constraints	1/3/2025	1/3/2025	0%
40	4.000	Information security policy gap assessment and update	On schedule	1/2/2024	8/4/2025	94%
41	4.000	Cybersecurity and Enterprise Risk Management - Goals 2025	On schedule	5/1/2025	2/3/2026	18%
42	4.002	Sustainability Initiatives – Business Continuity Management - Goals	On schedule	5/1/2025	10/21/2025	23%
43	4.010	Internal CJIS Audit Assessments - Data Collection	On schedule	9/1/2023	11/4/2025	84%
44	4.015	Judicial Federation with CISS AD	On schedule	1/1/2024	5/25/2026	58%
45	4.020	DEEP - Onboarding including GFIPM Claims	On schedule	9/1/2024	9/3/2025	89%
46	4.040	CISS Public-Facing Dashboard_Rev3	On schedule	3/26/2024	12/11/2025	48%
47	5.010	DAS Marshal Self-Service Portal	On schedule	4/30/2019	4/9/2026	61%
48	5.030	Police Use of Force Form - Phase 3	On schedule	10/16/2019	5/26/2026	59%
49	5.040	Racial Profile Application Phase 2 Changes	On schedule	5/22/2023	11/17/2025	41%
50	6.000	CJIS-CT Compliance & Audit Project (CCAP)	On schedule	11/15/2024	12/24/2025	30%
51	6.010	Data Center HA & Business Continuity	On-Hold - Stakeholders Dependency	11/12/2019	8/6/2025	71%
52	6.040	Purchase Request Application Phase 1 A	On schedule	7/5/2023	4/16/2026	71%
53	6.050	CISS - Notification and Reporting Testing	On-Hold - Resource Constraints	8/4/2025	1/19/2026	0%
54	6.050	Miscellaneous - Operations Project Plan	On schedule	11/1/2020	3/16/2032	55%
55	6.060	Router Cutovers and CISS Search (Re)Connectivity	On schedule	2/11/2020	10/31/2025	93%
56	6.070	TAC Course Design v1	On-Hold - Change in Scope/Goals	12/11/2023	9/30/2025	77%



Project Intake Queue

PIR Creation Date	Title	PIR Status
12/29/2022 9:44	DOL validations for WOTC	On-Hold
12/29/2022 9:47	Electronic transmittal of continuance - mittimus - integrated into 11.5	On-Hold
1/29/2024 13:07	NIEM standard across all agencies	On-Hold
3/18/2024 13:21	OCME-Office of the Chief Medical Examiner report and pictures requested by DCJ for new CISS workflow message and possible CISS Search	On-Hold
3/18/2024 13:35	Motorola RMS API Connectivity - CISS integration	On-Hold
4/3/2024 8:19	Vacation Plan Project- Automation to capture events created in M365 group calendar and add to project	On-Hold
4/15/2024 13:54	Deadly Weapons Connectivity to CISS Search - DWOR	On-Hold
6/10/2024 13:29	CISS Search - Reports requested by Eric Jackson -UConn Transportation Institute	On-Hold
7/29/2024 13:17	Create a Mobile Device Application for CISS Search through the internet	On-Hold
11/4/2024 13:22	Standard CJIS Arrest Forms Repository for electronic workflow	On-Hold
11/18/2024 13:33	Sentencing Commission - Request for CJIS-CT to evaluate the possibility of hosting a Sentencing DataBase	On-Hold
4/14/2025 13:22	CISS Workflow - PD regionalization (Pending Legislation)	On-Hold
4/14/2025 13:30	CISS - Replace SharePoint Enterprise Search with Azure AI Search	On-Hold
4/21/2025 13:14	CISS - Replace FileNet with a new ECM software with cost of ownership is significantly lower	On-Hold
4/28/2025 13:04	CISS Workflow - Add Case update message for DSS (Depart. of Scientific Services)	On-Hold
10/28/2024 13:12	Body & Vehicle Cam Vendor/State negotiations pulling buying power for lower prices	Active
12/23/2024 13:32	Artificial Intelligence R&D	Active
4/14/2025 13:12	CISS Workflow - Add Waterbury community court to Judicial GA routing table	Active
5/12/2025 13:07	CISS Federated Users existing old defects in Jazz	Active



CISS FY24-FY25 General Fund Operational Budget Summary

CISS General Fund Operational Budget Summary		
	FY 25 Actual	FY 26 Budget
CJIS-CT General Fund Budget	\$ 5,007,254	\$ 5,013,320
Rescission	\$ (250,000)	\$ (250,000)
Rescission for FY25 reversed	\$ 250,000	
IT Capitalization Clean Slate Reimbursement to General Fund	\$ 297,702	
Carry Forward from FY25 to FY26		
Expected Funding from OPM for Deficiency Funding	\$ 171,089	
Total Operational Funding for CJIS-CT	\$ 5,476,045	\$ 4,763,320



CISS FY 25 Bond Commission Approved Allocations

CISS FY 26 Bond Commission Approved Allocations		
Approved Allocations		Amounts
Bond Funds from June 2011 to June 2020 Inclusive for Phase 1	\$	60,920,000
CJIS-CT Appropriated Bond Funds for CISS Phase 2 of \$8.9M	\$	8,900,000
Bond Funds Received in 2023 to Add One Additional RMS Vendor		450,000
New Bond Funds Received in 2025 from the IT Capitalization Fund		297,158
Total Bond Funds for Phase 1 and Appropriations for Phase 2	\$	70,567,158
Expenses		Amounts
CISS Phase 1 Expenses	\$	57,762,963
Bond Funds Expended from July 2020 - June 2025 Inclusive for Phase 2	\$	12,239,340
Total Costs for CISS Phase 1 and Phase 2	\$	70,002,303
Remaining Bond Funds for CISS Phase 2 Deployment	\$	564,855



Clean Slate Project Financials

Clean Slate Project Financials as of 06/30/2025		
Agency	FY25	FY26 Expected
CJIS-CT IT Capitalization Received FY22 - FY24	\$ 1,992,001	
IT Capitalization Bond Fund Carry forward from FY25		\$ 53,545
IT Capitalization Bond Fund Request but not received yet		\$ 932,000
Funds expended from FY22 to FY25 inclusive	\$ 1,938,456	
Funds expected for FY26		\$ 985,545



Digital Evidence Study Budget/Resources


Digital Evidence Study - Spend to 06-30-25

Budget Amount	Total Expended August 1, 2023 – June 30, 2025	Remaining Funding
\$500,000	\$302,403	\$197,597



Digital Evidence Solution Ranking Analysis

State of CT - Digital Evidence Solution Approaches Ranking (Study Team Result)

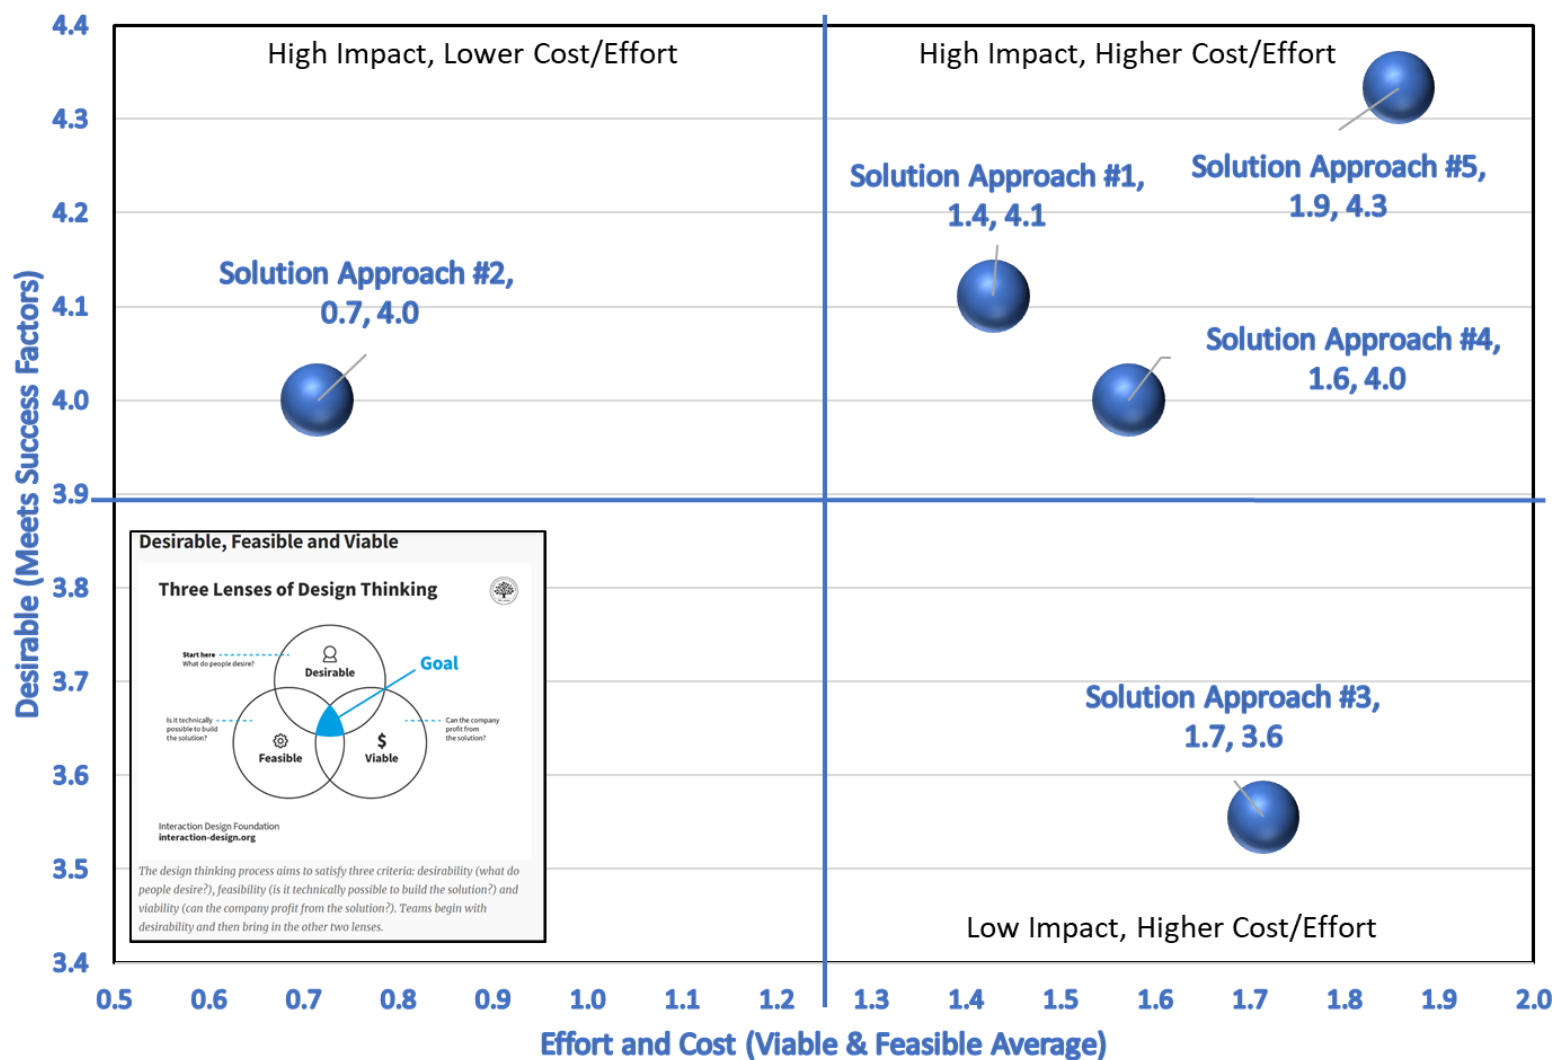

Solution Approach #1 – Mixed Model – 3rd party DEMS vendor, State of CT hardware, CISS identity management

* Phase 1, Phase 2 - (\$16.3 MM)*

Solution Approach #2 – SaaS model – Vendor provides software and storage

* Phase 2 - (\$8.4 MM)*

Solution Approach #3 - CT State-built sharing workflow and portal for PDs with storage included. Link-based sharing.

* Phase 1, Phase 2, Phase 4 - (\$19.4 MM)*

Solution Approach #4 - CT State-built CISS arrest integration, allows direct pipeline from LEA to prosecutor

* Phase 1, Phase 2, Phase 3 - (\$17.7 MM)*


Solution Approach #5 - CJIS-CT builds and maintains the entire Chain-of-Custody Architecture with storage infrastructure

* Phase 1, Phase 2, Phase 3, Phase 4, Phase 5, Phase 6 - (\$21.9 MM)*

- Initial Buildout Costs Only for Value Ranking Exercise – Decision Matrix Group Exercise – Not the Full TCO Values)
- See Digital Evidence Study for the Full TCO/ROI Analysis.



Digital Evidence Study – Development & Implementation Phases

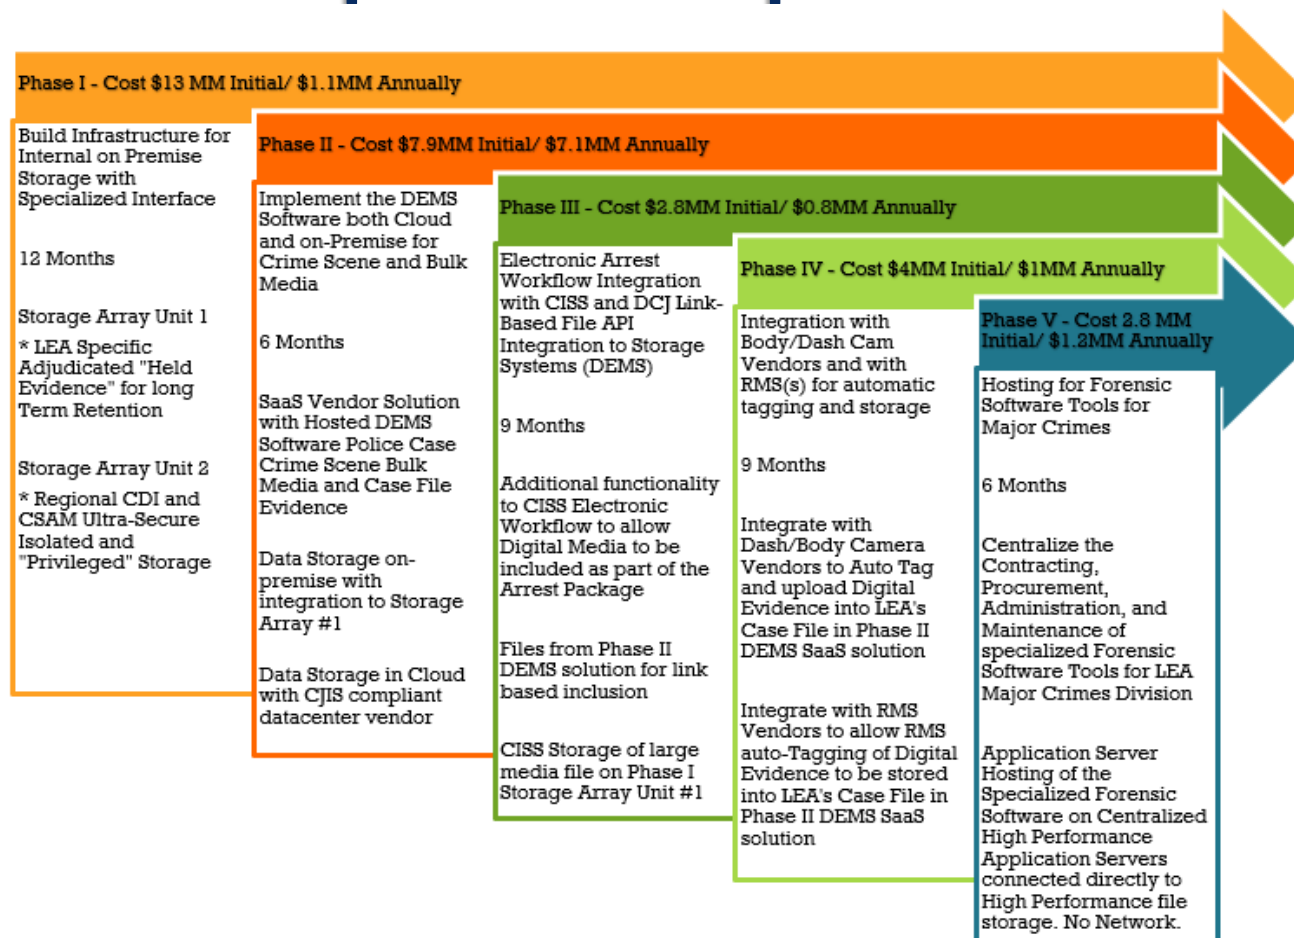

4 Year Timeline

- All 6 Phases
- \$60MM
- 5 Year Budget

Figure 20.17.1: Presumptive Solution #5 Phased Project Build and Deploy Plan

Phase VI – In parallel with Phase III – Create a Judicial Integration for Evidentiary Hearings and Courtroom Presentation (9 Months partly concurrent) – Timeline is 1 Year with overlapping with Start Date, both items Phase III and Phase VI completed in 1 Year. Need one (1) full time Business Analyst and one (1) full time System Integrator Engineer.




Digital Evidence Study – Implementation Phases and Timeline

4 Year Timeline

- All 6 Phases

Timeline Graphic

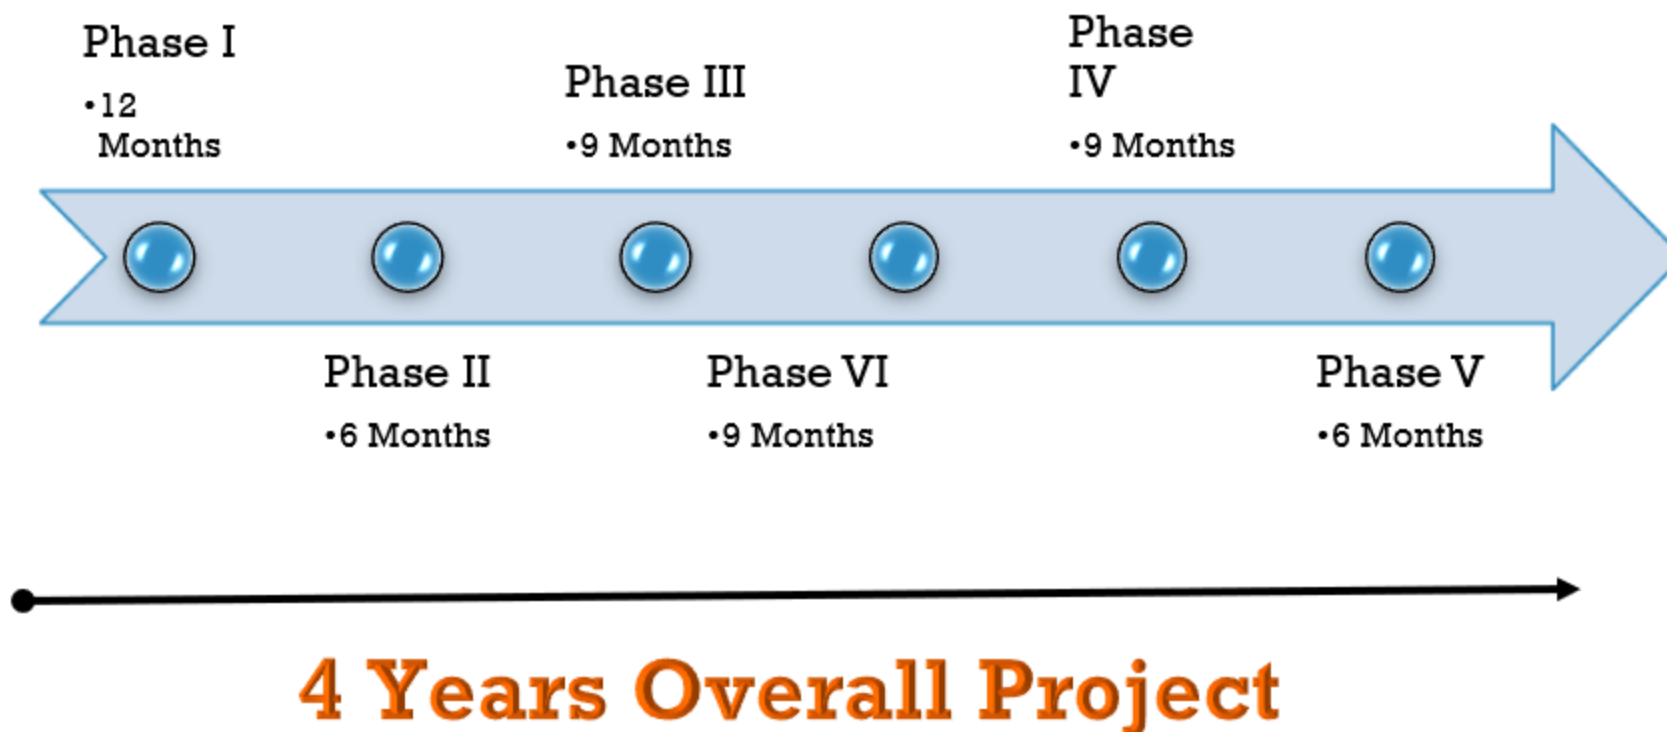



Current CJIS-CT Special Projects & Analytics

Agency Name	CISS Search	CISS Workflow	CJIS-CT Analytics	Partner Agency Support	Current Status
New Agency Onboarding – Departments of DCP, DSS, DRS, DEEP	✓	✓			Active – DEEP
Judicial SSO Identity Federation for CISS Search Access and Identity Reverse Authentication	✓			✓	Active
Judicial Online Communication Exchange (JOCE/JASPA) Tri-Agency Collaboration	✓			✓	Active
State Marshals Self Service Portal (C.G.S §14-10 & C.G.S §6-38a)			✓	✓	Ver. 1 LIVE - Complete Ver. 1.5 – Active
Racial Profiling Prohibition Upgrade			✓	✓	Active
Police Use of Force Transparency (PA 19-90)			✓	✓	Phase 1 – Complete Phase 2 – Complete Phase 3 – RMS - In Process Phase 3B – Complete
OCME – Office of the Chief Medical Examiner – Electronic Document Workflow exchange with LEAs		✓			NEW
Electronic CISS User Access Request (eCUAR) Onboarding Workflow	✓				Active
Digital Evidence – Scoping Study (PA 111, 2021, Section 12-19)		✓	✓	✓	Project Closeout
Sentencing Commission Request to Evaluate Providing a De-Identified Criminal History Database for ongoing Policy Studies and Evaluations			✓	✓	On-Hold
OPM/Urban Institute Request to Providing a De-Identified Criminal History Database for Recidivism Policy Studies			✓	✓	Project Initiation

Other Notables:

- BOPP Data Exchange
- DESPP Data Exchanges



Green highlight indicates new changes.



RMS Vendors – Integration Updates

Targeted Completion for Current Vendors: Q4 2027

Status: Tracking

Budget: On Budget (\$1,880,000 total budget)

Tasks Underway/Accomplishments

- **NexGen RMS:** 24 municipalities using Level 2 CISS Electronic Arrest Package Workflow
- **CT State Police:** Level 2 UAT completed, HQ pilot training ongoing
- **Accucom/IMC RMS:** Final stages of Level 2 certification, PD pilot testing to follow
- **Inform:** Contract initiation phase with Hartford PD
- **ProPhoenix RMS:** Q1 Programming Efforts are underway
- **Standard Operating Procedure (SOP):** CJIS Agencies and RMS vendors is in process


Key Dates/Next

- **Accucom & IMC:** Level 2 pilot projected completion in Q4 2025
- **DESPP LiveScan:**
 - ✓ Initial Idemia interface: Completed in Q4 2024
 - Second round Idemia interface: Programming changes ongoing

Risks/Issues/Mitigations

- **Risk:** New RMS vendor selection by PDs | **Mitigation:** New legislation requires electronic integration, CJIS-CT developing new RMS policy ([Public Act No. 23-36](#))
- **Risk:** Effective and Direct Communications with CJIS-CT from LEA Stakeholders | **Mitigation:** CJIS-CT has become a member of the CT Police Chiefs Association (CPCA) and will attend all regional meetings which will provide an additional continuous path for bi-directional communication.

CT RMS Market Analysis: September 2024 Analysis

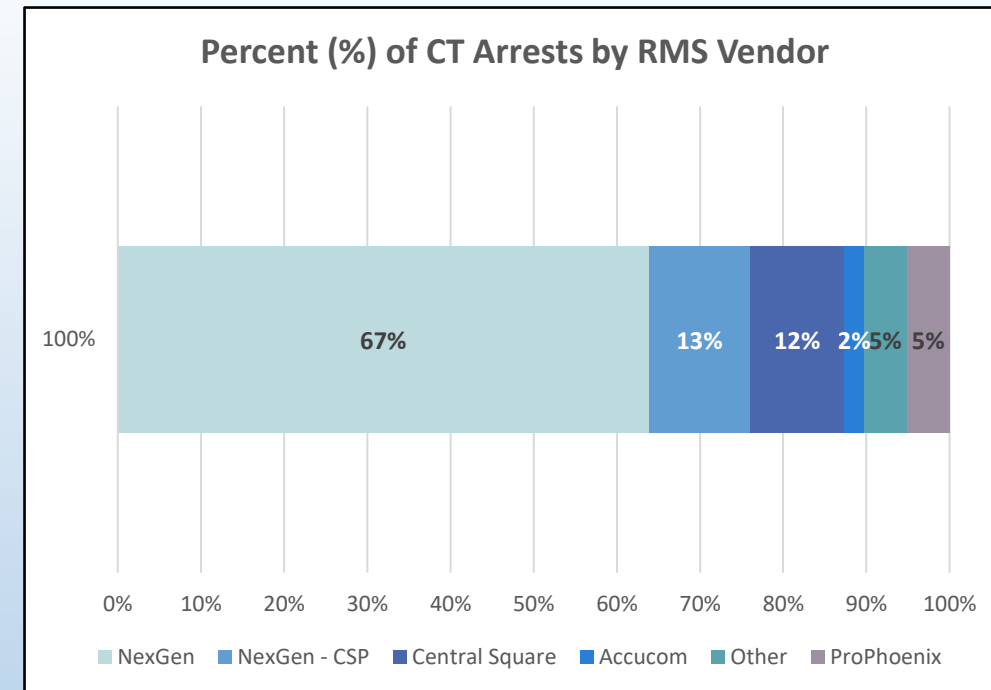



CISS Key Project Risks, Issues & Mitigation

(This Issue has been closed)

#4 Issue – FY25 and FY26 funding


There is a Budget Deficit of approximately \$1.915M for FY25. CJIS-CT had a \$1,604,569 budget lapse (rollover) from FY24 that was planned to be used in FY25 and has not been made available. CJIS-CT's General Fund Allotment for FY25 will be \$4,757,254 after \$250K rescission and no rollover. This has resulted in CJIS-CT using current fiscal year allocations to pay invoices for work incurred in the previous fiscal year, hence reducing the monies available for current year work.

Impact:

- **Key Consultant Cuts** – CJIS-CT has reduced 12 consultants out of 37 in Q3 FY25. That's about 1/3 of our consultant staff. The work required for CISS workflow deployment will increase burden on remaining staff.
- **Key High Visibility Projects Can Be Significantly Delayed** – CJIS-CT is managing about 58 separate projects (both stakeholder-driven and internal infrastructure related).

Proposed Mitigations: (also see next page)

- **Request for funding** – Terminated 12 consultants which will significantly reduce the expected \$1.915M budgetary gap.

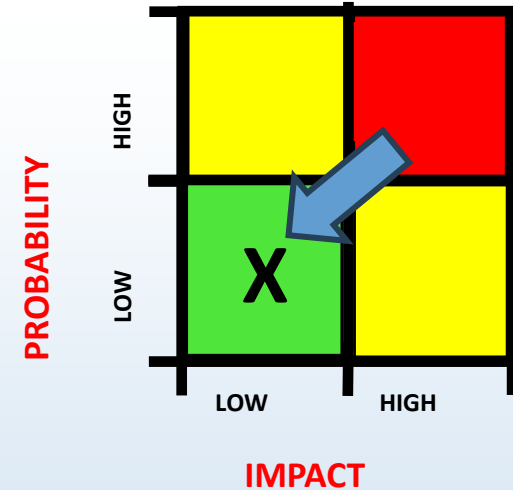

*Based on receiving funds
we are reducing the
severity of the Issue score*

*Important: FY25 Deficiency
funding received (\$1.25M GF)*



CISS Key Project Risks, Issues & Mitigation

Proposed Mitigation Continued:

- IT Capital Investment Funding Request** – On 3/24/25 CJIS-CT met with the IT Capitalization Committee to request additional funding for the CISS Workflow deployment for FY25 and FY26. Deficiency request in process to close the gap for FY25. The delays are primarily from both vendor delays with RMS software updates, and longer than anticipated change management process for onboarding all police departments, courts, and prosecutor offices. Often CJIS-CT must wait until police departments have availability to collaborate with training, connectivity, etc. CJIS-CT anticipates completion of deployment in Q2 FY27 for 90%+ of all arrest information. NEW - Workflow Deployment Bond Funding for FY25 and FY26 Q1 has been approved and received as requested.
- **Clean Slate Erasures IT Capitalization Funding Request** - On 3/24/25 CJIS-CT met with the IT Capitalization Committee to request funding of \$1,283,752 to complete the known scope of work for the Clean slate project. Approximately, \$300K will be use to reimburse the general fund work done in 2025 for Clean Slate. NEW - FY25 Clean Slate funding has been approved and received.
- **CJIS-CT to use more automation, use Artificial Intelligence (AI) to “do a lot more with less” and re-evaluate contracts for Maintenance & Support** - We are automating more of our testing of new code to reduce costs, exploring possibilities of adding AI for CISS Analytics and renegotiating maintenance agreements or instead leverage time & materials contracts. CJIS-CT will use a risk-based methodology for this process. NEW - Working with BITS AI Workgroup/Use Case review as required
- **CJIS-CT to explore chargeback for special projects-** CJIS-CT has been successful of receiving funding from both UCONN (for racial profiling prohibition project) and DMV (State Marshall Project Portal). New projects that are not core scope will require funding. NEW - Exploring additional funding sources for analytics/reporting projects with OPM and IMRP
- **CJIS-CT to continue to pursue grants-** CJIS-CT has received grant funding for JAG Byrne, and NCHIP grants. CJIS-CT will continue to pursue grants going forward to help supplement CJIS’s budget. NEW -Received NOGA on NCHIP grant for DWOR data source integration



CISS Key Project Risks, Issues & Mitigation


#1 Risk – As new RMS vendors come into the state and have LEAs as customers, we will require them to connect to CISS Digital Workflows. The challenge lies with cross-branch/cross agency resource capacity to support the onboarding these new vendors. This work will require resources and hence agency funding may be required for each new vendor integrated into CISS.

Impact:

- If proper planning is not done for onboarding new RMS vendors, CJIS-CT and stakeholders will be negatively impacted financially and delays may occur to existing projects at the time of connecting new RMS vendors.

Mitigation and Contingency:

- ProPhoenix is in the process of completing the security audit for them to participate in the integration effort for CISS Workflows. CJIS-CT is also pursuing adding one more vendor that has the Hartford PD as part of the CISS Workflows.
- CJIS-CT is exploring options to allow smaller PDs that do not have an RMS vendor connected to CISS to be able to send attached documents that can be processed for CISS Workflow.

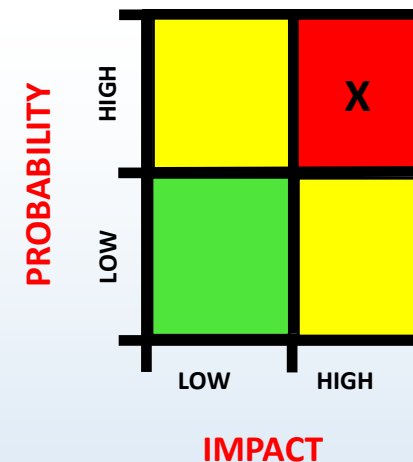



CJIS-CT Information Sharing System

Workflow Components

CISS Workflow Components	Status	Release		Date
Early Arrest Notices	In Production	Release 11	✓	
Arrest Paperwork	In Production	Release 11	✓	
Schedule Notification	In Production	Release 11	✓	
Disposition (Erasure)	In Production	Release 11	✓	
Case Update	In Production	Release 11	✓	
CIB Infraction Disposition Exchange	In Production	Release 11.4	✓	
DCJ Document Service Exchange	In Production	Release 11.4	✓	
Cannabis Legislation - Case Update	In Production	Release 11.4	✓	
Clean Slate Erasure Notifications	In Production	Release 11.4	✓	
MVP and Message Routing Changes for Clean Slate	In Production	Release 11.4.3	✓	
Bond Changes	In Production	Bond Release	✓	
Disposition Changes to Support Clean Slate	In Planning	Release 11.5		Q4 2025
CISS Upgrades (including CSSD Change Control)	In UAT Testing	Release 11.5		Q2 2025
Parole Decision	On Hold	Future Release		TBD
Release Decision	On Hold	Future Release		TBD
Pardon Decision	On Hold	Future Release		TBD
Continuance Mittimus	On Hold	Future Release		TBD



CISS Search Training – 128 Agencies and PDs (1/3)

Organization	Total Trained	Organization	Total Trained	Organization	Total Trained
Amtrak Police (NEW)	4	Department of Motor Vehicles	48	East Hartford Police	61
Ansonia Police	58	Division of Criminal Justice	47	East Haven Police	14
Avon Police	55	Public Defender Services (adding 350)	28	East Lyme Police	43
Berlin Police	55	Judicial Information Technology Division	14	East Windsor Police	19
Bethel Police	25	CCSU Police Department	8	Eastern Connecticut State University Police	2
Bloomfield Police	26	Office of the Victim Advocate	6	Easton Police	6
Branford Police	21	Superior Court Services	19	Enfield Police	155
Bridgeport Police	340	Clinton Police	41	Fairfield Police	41
Bristol Police	65	Colchester Police	14	Farmington Police	66
Brookfield Police	19	Connecticut State Community College	6	Glastonbury Police	36
Canton Police	11	Coventry Police	30	Granby Police	8
Cheshire Police	16	Cromwell Police	47	Greenwich Police	55
Board of Pardons and Paroles	47	Danbury Police	72	Groton City Police Department	30
Court Support Services Division	489	Darien Police	16	Groton Long PT Police	2
Department of Consumer Protection Gaming Division	2	Derby Police	7	Groton Town Police	80
Department of Emergency Services and Public Protection	538	DOC	191	Guilford Police	67
Department of Energy and Environmental Protection (New)	58	East Granby Police	1	Hamden Police	21
Department of Mental Health and Addiction Services Police Department	8	East Hampton Police	27	Hartford Police	192



CISS Search Training - 128 Agencies and PDs (2/3)

Organization	Total Trained	Organization	Total Trained	Organization	Total Trained
Ledyard Police	9	Newtown Police	56	South Windsor Police	77
Madison Police	13	North Branford Police	8	Southbury Police (NEW)	5
Manchester Police	58	North Haven Police	73	Southern Ct State University Police	7
Mashantucket Pequot Tribal Police	7	Norwalk Police	68	Southington Police	30
Meriden Police	50	Norwich Police	31	Stamford Police	57
Metropolitan District Commission Police	1	Old Lyme Police	3	State Capitol Police	23
Middlebury Police	7	Old Saybrook Police	22	Stonington Police	14
Middletown Police	42	Orange Police	71	Stratford Police	140
Milford Police Department	90	Plainfield Police	15	Suffield Police	33
Mohegan Tribal Police Department	17	Plainville Police	21	Thomaston Police	10
Monroe Police Department	10	Plymouth Police	36	Torrington Police	52
Montville Police Department	16	Portland Police	1	Trumbull Police	88
Naugatuck Police Department	104	Putnam Police	12	UConn Police	82
New Britain Police Department	127	Redding Police	41	University of New Haven Police	4
New Canaan Police Department	15	Ridgefield Police	21	Vernon Police	41
New Fairfield Police Department	2	Rocky Hill Police	65	Wallingford Police	43
New Haven Police	272	Seymour Police	3	Waterbury Police	138
New London Police	34	Shelton Police	13	Waterford Police	22
New Milford Police	26	Simsbury Police	48	Watertown Police	40
Newington Police	52	South Central Water Authority Police	2	West Hartford Police	80




CISS Search Training - 128 Agencies and PDs (3/3)

Organization	Total Trained
West Haven Police	32
Westbrook Police	1
Western Connecticut State University Police	3
Weston Police Department	7
Westport Police Department	82
Wethersfield Police Department	36
Willimantic Police Department	18
Wilton Police Department	54
Winchester Police Department	16
Windsor Locks Police Department	35
Windsor Police Department	65
Wolcott Police Department	39
Woodbridge Police Department	46
Yale Police Department	5
Metropolitan Transportation Authority (MTA) Just starting new agency onboarding	Expected - 70
Litchfield County Dispatch Just starting new agency onboarding	Expected - 24
Northwest Connecticut Public Safety Communication Center (NWCTPS) Just starting new agency onboarding	Expected - 30




CISS Search Training & Usage – Monthly Snapshot


ALL TIME USERS TRAINED

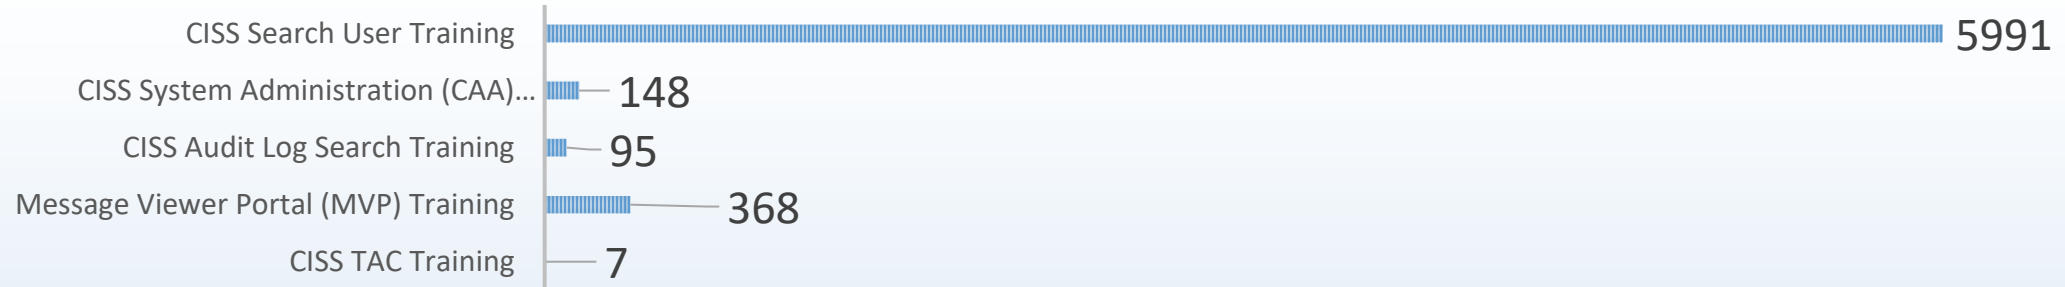

NUMBER OF SEARCHES



CISS usage BY Agency TYPE





CJIS-CT Transition from Deployment to Steady State Phase

Target: 12/31/25 of Key Initiatives

Status: On Schedule

Budget: IT Capitalization Funds requested \$1.7M for FY26

- **Staffing:** CJIS-CT has stabilized with the reduction of 12 consultants to now about 25. Schedules have been pushed forward in the future to adjust for smaller staff number. Legal Council/Attorney required on team to handle >100 MOUs needed and legal issues arising state-wide implementation
- **New - Artificial Intelligence (AI) and Automation:** Projects started for using technology to “do more with less” and in compliance to the State AI responsible use policy.
- **Documentation:** Most required documentation and SOPs completed. Focus on source system MOUs and CISS Digital Workflow SOPs.
- **CISS System Uptime:** Testing telemetry software for easier monitoring and issue resolution to meet 99.9% uptime goal. Project in progress

Financial Plan for Steady State:

Budget Control: Reducing rollover funds between fiscal years.


Funding: Working with OPM for technical adjustments, seeking funding from other agencies for requested projects, and pursuing grants for CJIIs.

Key Dates/Next

- CISS Search 2.0 planned release for 2026
- CISS Analytics product formally added as a product given demand from stakeholders

- Additional funding for one additional RMS has been approved and funds received.

Transition to Steady State Key Steps



Build, Test Deploy CISS State-wide



Transition to:
- Planned Releases
- Key Consultants to State Positions
- Steady Budget



Steady State:
- Operational Support with 99.9% Uptime
- New CISS Releases & CJIS-CT Projects Mgt



Statewide JD Workflow Deployment: NexGen RMS

JD	GA	Nexgen	CJIS		PD1	PD2	PD3	PD4	PD5	PD6	PD7	PD8	PD9	PD10	Mitigation Action Items
Middlesex	GA9-Middletown			6	Clinton	Cromwell	Portland	East Hampton	Middletown	Old Saybrook	Troop F (P)				
PD Ticket Request		Complete	Complete	5	9/30/2019	7/28/2022	2/17/2023	2/22/2023	12/15/2021		Complete				*Middletown PD has requested addition time to refine internal and RMS process
L1 EAN Activation		Complete	Complete	5	9/30/2019	7/28/2022	2/17/2023	2/22/2023	12/15/2021		5/24/2023				East Hampton - Has procured new server will move off regional configuration
L2 Connectivity Validation		Complete	Complete	5	Pilot PD	2/14/2023	3/9/2023	3/7/2023	Pilot PD						Old Saybrook does not wish to participate
DCJ Training		Complete	Complete	5	8/27/2022	1/20/2023	4/13/2023	5/20/2024	2/10/2023		Under Review				
SCO Training		Complete	Complete	5	8/27/2022	1/20/2023	4/13/2023	5/20/2024	2/10/2023						
PD Training		Complete	Complete	5	8/27/2022	1/20/2023	4/13/2023	5/20/2024	2/10/2023						
New Version of Nexgen		Pending	Pending	5	8/5/2024	8/21/2024	8/6/2024		8/2/2024						
Parallel Processing		Complete	Complete	2	8/5/2024	8/21/2024	8/6/2024	5/20/2024	8/2/2024						
Friday File Activation		Pending	Pending												
SCO/DCJ Certification			Pending	3	8/27/2022	9/15/2023	11/1/2024		5/7/2023		Under Review				
Waterbury	GA4-Waterbury	Nexgen	CJIS	6	Naugatuck	Middlebury	Watertown	Wolcott	Waterbury	Southbury	Troop A				
PD Ticket Request		Complete	Complete	6	5/9/2023	6/6/2023	6/13/2023	6/20/2023	6/13/2023	1/15/2025	Complete				Southbury PD needs router configuration completed (Prince)
L1 EAN Activation		Complete	Complete	5	8/3/2023	7/25/2023	7/27/2023	7/25/2023	8/11/2023	1/15/2025	5/24/2023				
L2 Connectivity Validation		Complete	Complete	5	8/3/2023	7/25/2023	7/27/2023	7/25/2023	3/20/2024						
DCJ Training		Complete	Complete	5	8/9/2023	7/25/2023	8/21/2023	8/16/2023	3/12/2025		Under Review				
SCO Training		Complete	Complete	5	8/9/2023	7/25/2023	8/21/2023	8/16/2023	3/12/2025						
PD Training		Complete	Complete	5	8/9/2023	7/25/2023	8/21/2023	8/16/2023	3/12/2025						
New Version of Nexgen		Complete	Complete	6	8/12/2024	8/7/2024	8/29/2024	8/27/2024	1/28/2025	1/18/2025					
Parallel Processing		Pending	Pending	1	8/12/2024	8/8/2024	9/11/2024	8/28/2024	3/11/2025						
Friday File Activation		Pending	Pending												
SCO/DCJ Certification			Pending	4	9/3/2024	3/5/2025	3/5/2025	11/1/2024 MS			Under Review				
New Haven	GA-23 New Haven	Nexgen	CJIS	6	Branford	Guilford	East Haven	North Branford	Woodbridge	Madison	Troop I				
PD Ticket Request		Complete	Complete	6	8/11/2023	8/11/2023	7/28/2023	8/11/2023	8/3/2023	8/11/2023	Complete				*Request for Credentials submitted 7/18/23
L1 EAN Activation		Complete	Complete	5	9/14/2023	8/25/2023	8/25/2023	8/25/2023	8/25/2023		5/24/2023				*PD Kickoff completed on 7/21/23
L2 Connectivity Validation		Complete	Complete	5	10/20/2023	10/27/2023	10/6/2023	9/29/2023	10/13/2023						Madison PD needs complete onboarding (Prince)
DCJ Training		Complete	Complete	5	8/23/2024	8/23/2024	8/23/2024	8/23/2024	8/23/2024						
SCO Training		Complete	Complete	5	8/23/2024	8/23/2024	8/23/2024	8/23/2024	8/23/2024						
PD Training		Complete	Complete	5	8/26/2024	8/27/2024	9/4/2024	9/17/2024	10/22/2024		Under Review				
New Version of Nexgen		Complete	Complete	5	8/27/2024	8/28/2024	9/9/2024	9/18/2024	10/7/2024	3/20/2025					
Parallel Processing		Complete	Complete	4	8/28/2024	8/29/2024	9/10/2024	9/19/2024	10/23/2024						
Friday File Activation		Pending	Pending												
SCO/DCJ Certification		Pending	Pending	1			11/1/2024 MS				Under Review				

Green = On track
Yellow = Watch
Red = Barriers

Yellow and Red need a date for closure. If not started just put planned date in cell. Completion date column is date for entire GA. Mitigation is general statement about how to cure Yellows and Reds. We review as management team 2x a week.



Statewide JD Workflow Deployment: NexGen RMS

JD	GA	Nexgen	CJIS		PD1	PD2	PD3	PD4	PD5	PD6	PD7	PD8	PD9	PD10	Mitigation Action Items
New Haven	GA-7 Meriden	Nexgen	CJIS	5	North Haven	Wallingford	Cheshire	Meriden	Hamden						Request for Credentials submitted 7/18/23
PD Ticket Request		Complete	Complete	5	8/11/2023	7/28/2023	7/28/2023	8/11/2023	10/11/2023						PD Kickoff completed on 7/21/23
L1 EAN Activation		Complete	Complete	5	8/11/2023	8/25/2023	8/11/2023	8/25/2023	10/13/2023						
L2 Connectivity Validation		Complete	Complete	5	9/22/2023	9/29/2023	9/22/2023	10/6/2023	10/13/2023						
DCJ Training		Complete	Complete	5	8/23/2024	8/23/2024	8/23/2024	8/23/2024	8/23/2024						
SCO Training		Complete	Complete	5	8/23/2024	8/23/2024	8/23/2024	8/23/2024	8/23/2024						
PD Training		Complete	Complete	5	9/3/2024	9/3/2024	9/11/2024	9/16/2024	10/8/2024						
New Version of Nexgen		Complete	Complete	5	9/4/2024	9/4/2024	9/12/2024	9/17/2024	9/24/2024						
Parallel Processing		Complete	Complete	5	9/4/2024	9/4/2024	9/13/2024	9/18/2024	10/9/2024						
Friday File Activation		Pending	Pending												
SCO/DCJ Certification		Pending	Pending		4/20/2025	4/20/2025	4/20/2025	4/20/2025	4/20/2025						
New Britain	GA-15 New Britain	Nexgen	CJIS	8	Southington	Berlin	Bristol	Newington	Wethersfield	Rocky Hill	New Britain	Plymouth			Credentials generated by CJIS and given to Nexgen Operations on 8/3/23
PD Ticket Request		Complete	Complete	7	12/5/2023	7/28/2022	10/6/2023	10/6/2023	10/6/2023	11/6/2023	10/6/2023				Kickoff Meeting to be complete by 9/29/23
L1 EAN Activation		Complete	Complete	7	12/15/2023	7/28/2022	10/20/2023	10/20/2023	10/20/2023	11/20/2023	10/20/2023				Plymouth PD signed with Nexgen 9/10/24
L2 Connectivity Validation		Complete	Complete	7	12/15/2023	11/3/2023	11/17/2023	12/1/2023	2/8/2024	11/22/2023	11/24/2023				GA-15 on hold until CSSD (CISS v11.4.7) Release
DCJ Training		Complete	Complete	7	10/15/2024	10/15/2024	10/15/2024	10/15/2024	10/15/2024	10/15/2024	10/15/2024				
SCO Training		Complete	Complete	7	9/15/2024	9/15/2024	9/15/2024	9/15/2024	9/15/2024	9/15/2024	9/15/2024				
PD Training		Complete	Complete	7	10/2/2024	10/16/2024	10/21/2024	11/13/2024	11/19/2024	11/18/2024	10/29/2024				
New Version of Nexgen		Complete	Complete	7	10/7/2024	10/9/2024	10/22/2024	10/30/2024	10/17/2024	10/19/2024	10/8/2024				
Parallel Processing		Pending	Pending	3	10/16/2024	10/21/2024	10/22/2024	9/2/2025	10/7/2025	11/4/2025	12/16/2025				
Friday File Activation		Pending	Pending												
SCO/DCJ Certification		Pending	Pending		4/20/2025	4/20/2025	4/20/2025								
Ansonia/Milford	GA-5 Derby	Nexgen	CJIS	3	Seymour	Ansonia	Shelton								Credentials generated by CJIS and given to Nexgen Operations on 8/3/23
PD Ticket Request		Complete	Complete	3	10/6/2023	10/6/2023	10/6/2023								Kickoff Meeting to be complete by 9/29/23
L1 EAN Activation		Complete	Complete	3	2/20/2024	10/20/2023	10/20/2023								2/13/25 - Shelton PD, Escalated to Chief Perno as we are not getting any response
L2 Connectivity Validation		Complete	Complete	3	2/10/2024	8/29/2024	11/3/2023								from his administrative staff
DCJ Training		Complete	Complete	3	12/8/2024	12/8/2024	12/8/2024								
SCO Training		Complete	Complete	3	12/2/2024	12/2/2024	12/2/2024								
PD Training		Complete	Complete	3	11/18/2024	1/14/2025	12/9/2024								
New Version of Nexgen		Complete	Complete	3	11/13/2024	11/13/2024	11/13/2024								
Parallel Processing		Pending	Pending	2	12/10/2024	2/5/2025									
Friday File Activation		Pending	Pending												
SCO/DCJ Certification		Pending	Pending	2	5/8/2025	5/8/2025									
Windam	GA-11 Windam	Nexgen	CJIS	3	Willimantic	Plainfield	Putnam	Troop D							Request for credential created and sent to CJIS Operations on 7/27/23
PD Ticket Request		Complete	Complete	3	3/14/2024	3/12/2024	3/4/2025	Complete							Kickoff Meeting to be complete by 3/12/24
L1 EAN Activation		Complete	Complete	2	3/19/2024	3/19/2024	3/7/2025	5/24/2023							Putnam needs complete onboarding
L2 Connectivity Validation		Complete	Complete	2	4/14/2024	4/14/2024									
DCJ Training		Complete	Complete	2	1/14/2025	1/14/2025									
SCO Training		Complete	Complete	2	1/13/2024	1/13/2024									
PD Training		Complete	Complete	2	1/23/2025	1/13/2024									
New Version of Nexgen		Complete	Complete	3	1/8/2025	1/6/2025	3/4/2025								
Parallel Processing		Complete	Complete	2	1/28/2025	1/14/2025	9/2/2025								
Friday File Activation															
SCO/DCJ Certification			Pending					Under Review							



Statewide JD Workflow Deployment: NexGen RMS

JD	GA	Nexgen	CJIS		PD1	PD2	PD3	PD4	PD5	PD6	PD7	PD8	PD9	PD10	Mitigation Action Items
New London	GA-10 New London	Nexgen	CJIS	6	Waterford	East Lyme	Groton Town	Stonington	New London	Groton City					Request for credential created and sent to CJIS Operations on 7/27/23
PD Ticket Request		Complete	Complete	6	3/28/2024	2/2/2024	3/20/2024	2/2/2024	3/20/2024						Kickoff Meeting to be complete by 2/2/24
L1 EAN Activation		In Progress	In Progress	5	5/15/2024	2/2/2024	3/20/2024	2/2/2024	2/4/2025						2/11/2025 - Stonington, East Lyme, Groton Town, need schedule
L2 Connectivity Validation		In Progress	In Progress	5	4/14/2024	3/8/2024	4/14/2024	3/1/2024	3/12/2025						Training and go live dates
DCJ Training		Complete	Complete	1	2/26/2025										
SCO Training		Complete	Complete	1	2/24/2025										
PD Training		In Progress	In Progress	1	2/24/2025										
New Version of Nexgen		In Progress	In Progress	5	1/16/2025	2/17/2025	1/9/2025	1/9/2025	2/4/2025						
Parallel Processing		In Progress	In Progress	1	2/25/2025	9/2/2025	10/7/2025	11/13/2025	12/18/2025						
Friday File Activation															
SCO/DCJ Certification			Pending		7/30/2025										
Fairfield	GA-2 Bridgeport	Nexgen	CJIS	5	Trumbull	Fairfield	Stratford	Monroe	Bridgeport	Troop G					Request for credential created and sent to CJIS Operations on 7/27/23
PD Ticket Request		Complete	Complete	5	11/8/2021	12/10/2023	11/29/2023	1/1/2023	11/2/2023	Complete					Operations on 7/27/23
L1 EAN Activation		Complete	Complete	5	11/8/2021	12/19/2024	2/9/2024	1/19/2024	11/2/2023	5/24/2023					
L2 Connectivity Validation		Complete	Complete	5	12/5/2024	2/9/2024	5/10/2024	2/16/2024	3/29/2024						
DCJ Training		Complete	Complete	1	3/13/2025	3/13/2025	3/13/2025	3/13/2025	3/13/2025						
SCO Training		Complete	Complete	1	3/6/2025	3/6/2025	3/6/2025	3/6/2025	3/6/2025						
PD Training		In Progress	In Progress	1	3/13/2025	3/13/2025									
New Version of Nexgen		In Progress	In Progress	4	1/29/2025	1/23/2025	1/30/2025	3/20/2025							
Parallel Processing		In Progress	In Progress	1	3/13/2025	5/1/2025	9/15/2025	10/14/2025	TBD						
Friday File Activation															
SCO/DCJ Certification			Pending		7/30/2025	7/30/2025				Under Review					
Danbury	GA-3 Danbury	Nexgen	CJIS	4	Newtown	Bethel	Ridgefield	Danbury							Request for credential created and sent to CJIS Operations on 7/27/23
PD Ticket Request		Complete	Complete	4	1/10/2024	12/12/2023	12/11/2023	1/10/2024							Kickoff Meeting to be complete by 12/7/23
L1 EAN Activation		Complete	Complete	4	1/19/2024	12/13/2023	1/19/2024	1/19/2024							
L2 Connectivity Validation		Complete	Complete	4	2/6/2024	1/27/2024	3/26/2024	3/28/2024							
DCJ Training		Complete	Complete	1	3/13/2025	3/13/2025	3/13/2025	3/13/2025							
SCO Training		Complete	Complete	1	3/13/2025	3/13/2025	3/13/2025	3/13/2025							
PD Training		Pending	Pending	1	3/13/2025										
New Version of Nexgen		Pending	Pending	3	2/14/2025	2/17/2025		2/25/2025							
Parallel Processing		Pending	Pending	1	3/20/2025	9/2/2025	10/7/2025	11/18/2025							
Friday File Activation															
SCO/DCJ Certification			Pending												
Tolland	GA-19 Tolland	Nexgen	CJIS	1	Vernon	Troop K	Troop C (P)								Request for credential created and sent to CJIS Operations on 7/27/23
PD Ticket Request		Complete	Complete	1	3/12/2024	Complete	Complete								Kickoff Meeting to be complete by 3/12/24
L1 EAN Activation		Complete	Complete	1	3/23/2024	5/24/2023	5/24/2023								
L2 Connectivity Validation		Complete	Complete	1	4/14/2024										
DCJ Training		Complete	Complete	1	4/8/2025										
SCO Training		Complete	Complete	1	12/8/2024										
PD Training		Complete	Complete	1	4/8/2025										
New Version of Nexgen		Complete	Complete	1	12/10/2024										
Parallel Processing		Complete	Complete	1	4/8/2025										
Friday File Activation		Pending	Pending												
SCO/DCJ Certification		Pending	Pending			Under Review	Under Review								



JD	GA	Nexgen	CJIS		PD1	PD2	PD3	PD4	PD5	PD6	PD7	PD8	PD9	PD10	Mitigation Action Items
Litchfield	GA-18 Torrington	Nexgen	CJIS	3	New Milford	Winsted	Torrington	Troop L (P)	Troop B						Request for credential created and sent to CJIS Operations on 7/27/23
PD Ticket Request		Complete	Complete	1	3/14/2024			Complete	Complete						Kickoff Meeting to be complete by 2/2/24
L1 EAN Activation		Complete	Complete	1	3/19/2024			5/24/2023	5/24/2023						Winsted and Torrington PD signed with Nexgen on 9/10/22
L2 Connectivity Validation		Complete	Complete	1	4/14/2024										2/11- NMPD would like to have CJIS review internal arrest process before committing
DCJ Training															"Go Live" Date
SCO Training															
PD Training		Complete	Complete	1	1/21/2025										
New Version of Nexgen		Complete	Complete	1	1/6/2025										
Parallel Processing															
Friday File Activation															
SCO/DCJ Certification			Pending					Under Review	Under Review						
New London	GA-21 Norwich	Nexgen	CJIS	1	Montville	Troop E									Request for credential created and sent to CJIS Operations on 7/27/23
PD Ticket Request		Complete	Complete	1	2/2/2024	Complete									Kickoff Meeting to be complete by 2/2/24
L1 EAN Activation		Complete	Complete	1	2/20/2024	5/24/2023									2/11 - Need "Go Live" date from Montville PD
L2 Connectivity Validation		Complete	Complete	1	3/8/2024										
DCJ Training		Complete	Complete	1	2/26/2025										
SCO Training		Complete	Complete	1	2/24/2025										
PD Training		Complete	Complete	1	2/24/2025										
New Version of Nexgen		Complete	Complete	1	1/7/2025										
Parallel Processing															
Friday File Activation															
SCO/DCJ Certification			Pending			Under Review									
Ansonia/Milford	GA-22 Milford	Nexgen	CJIS	1	West Haven										Request for credential created and sent to CJIS Operations on 7/27/23
PD Ticket Request		Complete	Complete	1	1/3/2024										Kickoff Meeting to be completed on 1/4/24
L1 EAN Activation		Complete	Complete	1	1/12/2024										Escalated to DCJ, no contact from WHPD
L2 Connectivity Validation		Complete	Complete	1	1/30/2024										
DCJ Training		Pending	Pending												
SCO Training		Pending	Pending												
PD Training		Pending	Pending												
New Version of Nexgen		Pending	Pending												
Parallel Processing		Pending	Pending												
Friday File Activation		Pending	Pending												
SCO/DCJ Certification		Pending	Pending												
Stamford	GA-1 Stamford	Nexgen	CJIS	6	Greenwich	Wilton	Westport	Darien	New Canaan	Norwalk					Request for credential created and sent to CJIS Operations on 7/27/23
PD Ticket Request		Complete	Complete	6	12/29/2023	12/29/2023	12/29/2023	1/19/2024	12/29/2023	12/11/2023					Kickoff Meeting to be complete by 12/11/23
L1 EAN Activation		Complete	Complete	6	4/16/2024	1/19/2024	1/19/2024	2/23/2024	1/19/2024	4/1/2024					
L2 Connectivity Validation		Complete	Complete	6	2/28/2024	3/2/2024	3/23/2024	2/23/2024	2/6/2024	1/26/2024					
DCJ Training		Pending	Pending												
SCO Training		Pending	Pending												
PD Training		Pending	Pending												
New Version of Nexgen		Pending	Pending	5	2/25/2025	2/25/2025	2/26/2025	2/18/2025		2/14/2025					
Parallel Processing		Pending	Pending		10/21/2025	11/21/2025	12/23/2025								
Friday File Activation		Pending	Pending												
SCO/DCJ Certification		Pending	Pending												



Statewide JD Workflow Deployment: NexGen RMS

JD	GA	Nexgen	CJIS		PD1	PD2	PD3	PD4	PD5	PD6	PD7	PD8	PD9	PD10	Mitigation Action Items
Hartford	GA-14 Hartford	Nexgen	CJIS	10	Enfield	Avon	Bloomfield	West Hartford	Windsor Locks	Farmington	Windsor	East Windsor	Simsbury	Canton	Request for credential created and sent to CJIS Operations on 7/27/23
PD Ticket Request		Complete	Complete	10	3/3/2020	11/29/2023	11/29/2023	1/9/2024	11/17/2023	10/13/2020	1/7/2024	12/5/2023	1/17/2024	2/6/2024	Preliminary Meeting complete on by 11/8/23 & 12/7/23
L1 EAN Activation		In Progress	In Progress	9	3/3/2020	12/8/2023	12/6/2023	2/8/2024	12/8/2023	10/27/2020	1/18/2024	12/8/2023	1/18/2024		Windsor Locks -Need FW Open to allow L2
L2 Connectivity Validation		In Progress	In Progress	9	3/22/2024	2/6/2024	2/2/2024	2/6/2024	12/10/2024	3/22/2024	2/21/2024	3/22/2024	3/22/2024		Canton- PD needs new servers
DCJ Training		In Progress	In Progress												
SCO Training		In Progress	In Progress												
PD Training		In Progress	In Progress												
New Version of Nexgen		In Progress	In Progress	9	2/17/2025	12/9/2025	2/4/2025	12/9/2024	12/9/2024	2/26/2025	2/26/2025	2/26/2025	2/26/2025	2/18/2025	
Parallel Processing		In Progress	In Progress		10/21/2025	11/21/2025	12/16/2025								
Friday File Activation		In Progress	In Progress												
SCO/DCJ Certification		In Progress	In Progress												
Hartford	GA-12 Manchester	Nexgen	CJIS	6	Manchester	East Hartford	South Windsor	Granby	Suffield	Glastonbury	Troop H				Request for credential created and sent to CJIS Operations on 7/27/23
PD Ticket Request		Complete	Complete	6	9/19/2023	11/14/2023	12/17/2024	12/4/2023	12/18/2023	12/5/2023	Complete				Preliminary Meeting complete by 11/8/23
L1 EAN Activation		Complete	Complete	6	10/6/2023	12/8/2023	12/18/2024	12/8/2023	12/18/2023	12/12/2023	5/24/2023				Follow-up meeting scheduled for 12/7/23
L2 Connectivity Validation		In Progress	In Progress	5	12/15/2023	12/5/2023	12/29/2024	7/15/2024	2/22/2024	3/22/2024					Glastonbury - Has procured new server will move off regional configuration
DCJ Training		In Progress	In Progress												
SCO Training		In Progress	In Progress												
PD Training		In Progress	In Progress												
New Version of Nexgen		In Progress	In Progress	4	12/10/2024	2/17/2025	2/17/2025	1/20/2025							
Parallel Processing		In Progress	In Progress		10/28/2025	11/25/2025									
Friday File Activation		In Progress	In Progress												
SCO/DCJ Certification		In Progress	In Progress								Under Review				



Comprehensive Acronyms List

Acronym	Description
ADFS	Active Directory Federated Services
AFIS	Automated Fingerprint Identification System
API	Application Program Interface
AST	Application Support System
BEST	Bureau of Enterprise Systems and Technology
BICE	Bureau of Immigration and Customs Enforcement
BOPP	Board of Pardons and Paroles
CAA	Community Agency Administrator
CAD	Computer Aided Dispatch
CCH	Computerized Criminal History (DESPP)
CIB	Centralized Infraction Bureau (Judicial)
CIDRIS	Connecticut Impaired Driver Records Information System
C-ISO	C-ISO = CJIS-CT Information Officer
CISS	Connecticut Information Sharing System
CIVLS	Connecticut Integrated Vehicle & Licensing System
CJIS-CT	Connecticut Criminal Justice Information System
CJPPD	Criminal Justice Policy Development and Planning Division
CMIS	Case Management Information System (Judicial - CSSD)
COLLECT	Connecticut On-Line Law Enforcement Communications Teleprocessing Network (DESPP)
COTS	Computer Off the Shelf (e.g., software)
CPCA	Connecticut Police Chiefs Association
CRCOG	Capital Region of Council of Governments
CRMVS	Criminal Motor Vehicle System (Judicial)
CSO	Connecticut Information Security Officer
CSSD	Court Support Services Division (Judicial)
CUAR	CISS User Authorization Request
DAS	Department of Administrative Services
DCJ	Division of Criminal Justice



Comprehensive Acronyms List

Acronym	Description
DEMHS	Department of Emergency Management and Homeland Security
DESPP	Department of Emergency Services and Public Protection
DMV	Department of Motor Vehicles
DMV LOBS	Department of Motor Vehicles / Line of Business
DNS	Domain Name System
DOC	Department of Correction
DOIT	Department of Information Technology
DPDS	Division of Public Defender Services
ECM	ECM
Enhanced CBT	Instructor Led Computer-Based Training (POST)
ETL	Extraction, Transformation, and Load
FIM	Forefront Identity Manager (Microsoft)
FOIA	Freedom of Information Act
GFIPM	Global Federated Identity and Privilege Management (security standard used by FBI)
GUI	Graphical User Interface
HAC	High Availability Clusters
IAFIS	Integrated Automated Identification System
IEPD	Information Exchange Package Document
IExUI	Information Exchange User Interface
I-SIM	IBM Secure Identity Manager
IST	Infrastructure Support Team
JMI	Jail Management System
JUD	Judicial Branch
LAN	Local Area Network
LASO	Local Agency Security Officer
LEA	Law Enforcement Agency
LIMS	State Crime Laboratory Database
LMS	Learning Management System



Comprehensive Acronyms List

Acronym	Description
MFA	Multi-Factor Authentication
MNI	Master Name Index (DESPP)
NAT	Network Address Translation
OBIS	Offender Based Information System (DOC)
OBTS	Offender Based Tracking System
OCPD	Office of Chief Public Defender
ORI	Originating Agency Identification
OSET	Office of Statewide Emergency Telecommunications
OVA	Office of the Victim Advocate
OVS	Office of Victim Services
PCDN	Private Content Delivery Network
PIR	Project Intake Request (CJIS-CT)
POC	Proof of Concept
POR	Protection Order Registry (DESPP)
PRAWN	Paperless Re-Arrest Warrant Network (Judicial)
PSDN	Public Safety Data Network
RDB	Relational Database
RMS	Records Management System
SAN	Storage Area Network
SCO	Superior Court Operations Div. (Judicial)
SCOM	Systems Center Operations Manager
SDLC	Software Development Life Cycle
SDM	Software Development Model
SLEO	Sworn Law Enforcement Officer
SLFU	Special Licensing of Firearms Unit (DESPP)
SME	Subject Matter Expert
SOA	Service Oriented Architecture
SOR	Sex Offender Registry (DESPP)



Comprehensive Acronyms List

Acronym	Description
SPBI	State Police Bureau of Identification (DESPP)
SQL	Structured Query Language
TAC	Terminal Access Coordinator
UAR	Uniform Arrest Report
